

**Camden County Department of Public Works  
Division of Engineering  
Roadway and Drainage Improvements Evesham Road  
Runnemede Borough, Magnolia Borough and  
Gloucester Township, Camden County, New Jersey  
Contract B22-21 Hartford to Charles  
Progress Report No. 21  
October 31, 2022 to November 4, 2022**



*Figure 1: 8 Inch Gutter*

**Work Completed Period of November 4, 2022**

- Removed asphalt, concrete curbs, and sidewalks.
- Installed curb forms and completed concrete curb, gutter, and sidewalk installation.
- ADA curb ramp placement.



Figure 2: Forms for gutter placement



Figure 3: Concrete curb placement



Figure 4: Concrete curb and apron completed

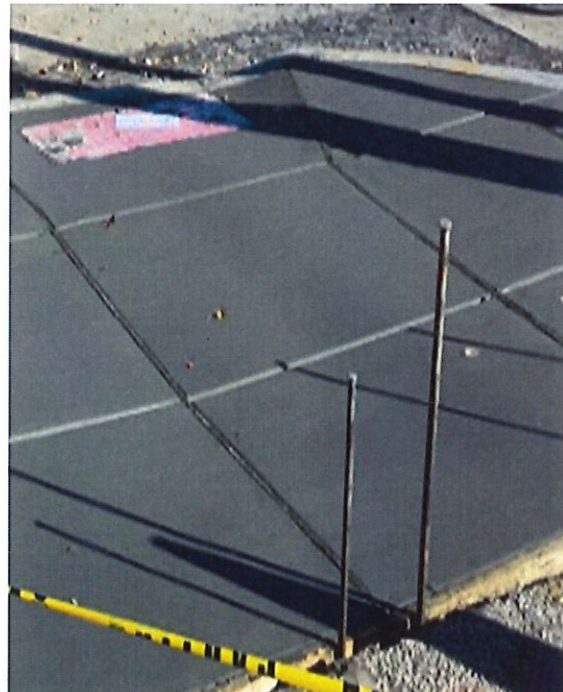


Figure 5: ADA curb ramp and sidewalk



**Quantities Period of November 4, 2022**

- **Item #27:** Hot Mix Asphalt 19M64 Base Course (Trench Restoration) (10 TON)
- **Item #65:** Concrete Sidewalk, 4" Thick (64 SY)
- **Item #67:** Concrete Driveway, Reinforced, 6" Thick (11 SY)
- **Item #69:** Detectable Warning Surface (4 SY)
- **Item #71:** 9" X 16" Concrete vertical curb (271.70 LF)
- **Item #72:** Concrete Curb and Gutter (170 LF)
- **Item #73:** Concrete Gutter, 8" Thick (66.36 SY)
- **Item #88:** Reset Manhole, Sanitary Sewer, Using Existing Casting (1 UNIT)

**Summary of Work Completed Period of November 4, 2022**

The contractor began with removing asphalt, concrete curbs, and sidewalks. The crew then installed forms and placed concrete curbs, sidewalks, and gutters. Also completed placement of ADA curb ramps.

**Anticipated Work for Period of November 7, 2022**


- Continue with concrete work.

**Notice to Proceed:** May 16, 2022

**Substantial Completion:** November 12, 2022 (Time extension expected)

**Final Completion:** December 12, 2022

**Prepared By:**



Joseph R. Ragusa, P.E.  
Remington & Vernick Engineers
