


Clementon-Berlin Road (CR 534) Bridge over
North Branch of Timber Creek Structure No. 048E006

Borough of Clementon
County of Camden, NJ
Weekly Progress Report #15
January 14 to January 18, 2019



Contractor using hopper and shoot due to height of Wing wall. This was on the west side of structure.

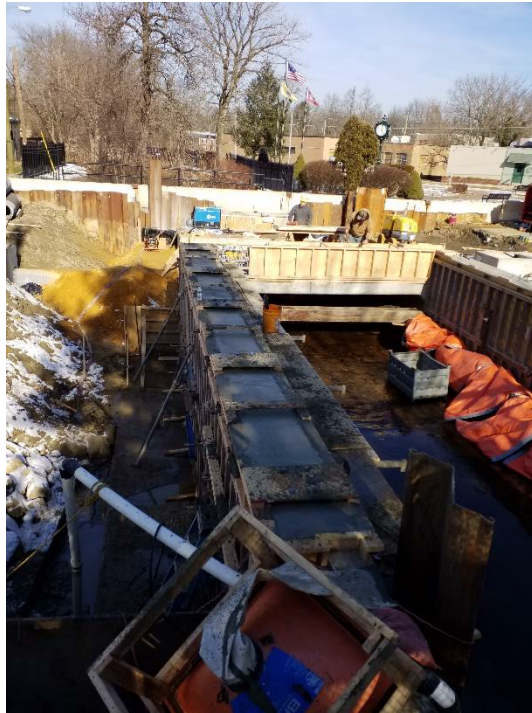

West wing wall after concrete is poured



Contractor is using blankets and heater to comply with winter concrete requirements



I-9 is being placed in lifts and compacted



Parapet was poured on Wednesday with the anchor bolts for the railing. Railing was delivered to project also on Wednesday

Partial NTP : August 15, 2018
NTP : September 20, 2018

Contractor Duration: 512 days
Completion date February 14, 2020

23.4% of time used to date

50.9% paid to date

The Notice to Proceed was given on September 20, 2018. Contractor has the duration of 512 day making the completion date on February 14, 2020.

Contractor has finished all pours that are needed for this stage of construction. They have placed and compacted the I-9 as per plan. Some roadway items have been installed, such as inlets and pipe in this stage. On Friday the contractor milled the asphalt off to where the limits of the full box out is called for on the plans. The contractor is questioning the need to remove the concrete slabs as per plan. It was asked of this to shoot grades to finish surface to see if there could be another option/

The contractor will continue the roadway work needed for this stage. Their temporary header has been approved that is required at the stage line. Project continues to be ahead of schedule.

Prepared by: Tony Guerrieri, AECOM Project Manager
