



**Improvements to Avondale Avenue (CR646) from Hopkins Road to Woodland Ave.
and Improvements to Breslin Avenue from Graisbury Avenue to Avondale Avenue**

*Township of Haddon
Camden County
Bid No. B2-19*

MC Project No. 19000074G

Progress Report # 6

Monday, June 24, 2019 to Saturday, June 29, 2019



Figure 1: Replacement of concrete base course at each corner.

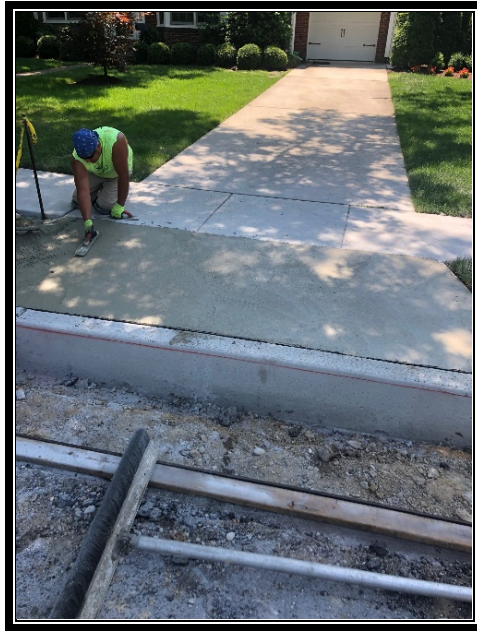


Figure 2: New concrete driveway apron.



Figure 3: New sidewalk and handicap ramp at Avondale & Tomlinson Avenues.



Work Completed this week:

Charles Marandino Concrete continues installing monolithic curb, gutter and sidewalk on Avondale Avenue from Tomlinson Avenue to Crystal Lake Avenue. The contractor has also continued to pour driveways and handicap ramps. The areas behind the new curb were restored with topsoil. All of the required tree and stump removal has been completed. He will continue to work in two block increments. These blocks will be closed to traffic during the daytime. A short detour around the block will be posted. Access to homeowners will be maintained.

Items completed this week:

#2:	Police Traffic Directors	97 HOURS
#6:	Removal of Concrete Roadway	82 SY
#11:	Concrete Roadway, 9" Thick, Class V	82 SY
#22:	Concrete Sidewalk, 4" Thick	136 SY
#23:	Concrete Driveway, 6" Thick	95 SY
#25:	Detectable Warning Surface	7 SY
#27:	Monolithic Concrete Curb and Gutter	1670 LF

• PROGRESS NEXT TWO (2) WEEKS

- Charles Marandino Concrete will continue working on Avondale Avenue working west to east. He will continue to install curb, gutter, driveways and handicap ramps in two block increments. These two blocks will be closed during the work day.
- The contractor plans on working between Crystal Lake and Woodland Avenues.
- All areas behind the curb will be backfilled and topsoiled.
- The contractor will continue to work 7:00 AM to 4:30 PM.
- The contractor may also work on selected Saturdays.

• NEXT MEETING

- Next Progress Meeting is scheduled for Tuesday, July 9, 2019 at 10:00 AM.

Notice to Proceed Date: May 13, 2019

Contract Completion Date: August 11, 2019

Anticipated Completion Date: August 11, 2019

Prepared by: Vincent E. Baglivo
Maser Consulting
