



**Improvements to Avondale Avenue (CR646) from Hopkins Road to Woodland Ave.
and Improvements to Breslin Avenue from Graisbury Avenue to Avondale Avenue**

*Township of Haddon
Camden County
Bid No. B2-19*

MC Project No. 19000074G

Progress Report # 20

Monday, September 30, 2019 to Friday, October 4, 2019



Figure 1: Contractor installed crosswalks and stop bars on Avondale & Breslin Avenues.



Figure 2: Crosswalks, stop bars and yellow curb on Avondale & Jess Avenues.

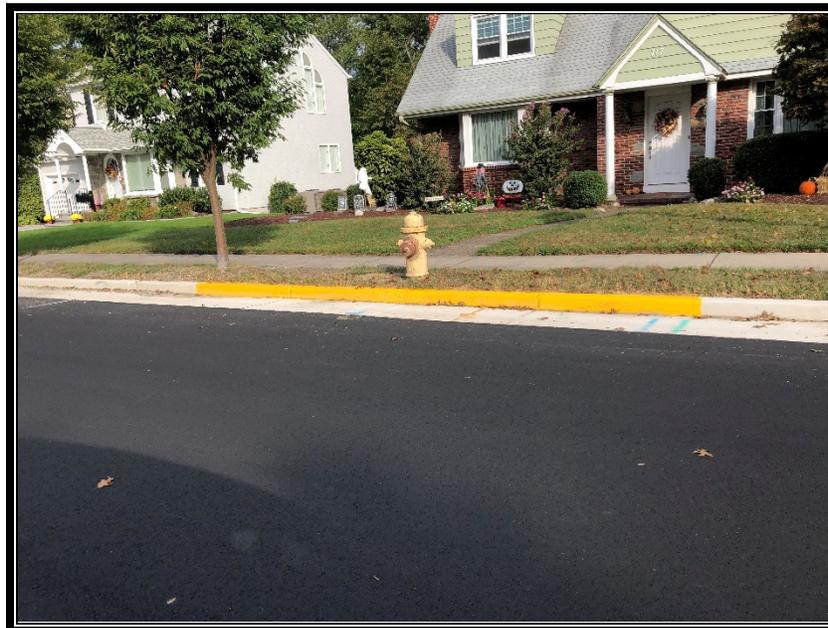


Figure 3: Yellow curb marking fire hydrants along Avondale Avenue.



Work Completed this week:

The contractor completed the traffic stripes and markings, which included crosswalks and stop bars. The contractor also painted curbs yellow at the designated locations.

Items completed this week:

#2:	Police Traffic Directors	24 HOURS
#28:	Traffic Stripes, Thermoplastic 6" Wide	1378 LF
#29:	Traffic Stripes, Thermoplastic 12" Wide	1364 LF
#30:	Traffic Markings, Thermoplastic	285 SF
#41:	Paint Curb Yellow	1378 LF

• PROGRESS NEXT TWO (2) WEEKS

- The contractor plans to install new traffic signs along Avondale Avenue.
- He will also begin work on the punch list items.
- The contractor will continue to work 7:00 AM to 4:30 PM.

• NEXT MEETING

- Next Progress Meeting is scheduled for Tuesday, October 15, 2019 at 10:00 AM.

<u>Notice to Proceed Date:</u>	May 13, 2019
<u>Contract Completion Date:</u>	August 11, 2019
<u>Anticipated Completion Date:</u>	October 15, 2019

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
