

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 1
October 20, 2019 to October 26, 2019**



Figure 1: Concrete curb ramp

Work Completed Week of October 26, 2019

- Installation of concrete sidewalk, curb, reinforced driveways, and curb ramps

Quantities Week of October 26, 2019

- **Item #1:** Construction Layout (0.1 LS)
- **Item #9:** Portable Variable Message Sign (2 UNIT)
- **Item #17:** Dense-Graded Aggregate Base Course, 8" Thick (11.33 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (7.57 TON)
- **Item #25:** Reset Existing Casting (1 UNIT)
- **Item #30:** Concrete Sidewalk, 4" Thick (54.99 SY)
- **Item #31:** Concrete Driveway, Reinforced, 6" Thick (49.11 SY)
- **Item #32:** Detectable Warning Surface (2.67 SY)
- **Item #34:** 9"x18" Concrete Vertical Curb (45 LF)

- **Item #66:** Topsoiling, 4” Thick (48.69 SY)
- **Item #68:** Fertilizing and Seeding, Type F (48.69 SY)
- **Item #70:** Police Uniform Law Enforcement Officers (47 HR)
- **Item #1C:** Concrete Sidewalk, 4” Thick (175.56 SY)

Summary of Work Completed Week of October 26, 2019

Lexa Concrete (Lexa) mobilized to the site in preparation to begin the project. Lexa started demolition of existing concrete and replacement with new concrete sidewalk, curb, reinforced driveways, and curb ramps. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control.

Anticipated Work for Week of November 2, 2019

Lexa will continue with the removal and replacement of concrete curb, sidewalk, driveways, and curb ramps as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project. An onsite progress meeting will be held on October 28, 2019 to review all project related activities.



Figure 2: Concrete sidewalk formed



Figure 3: Concrete sidewalk placed



Figure 4: Concrete being cured

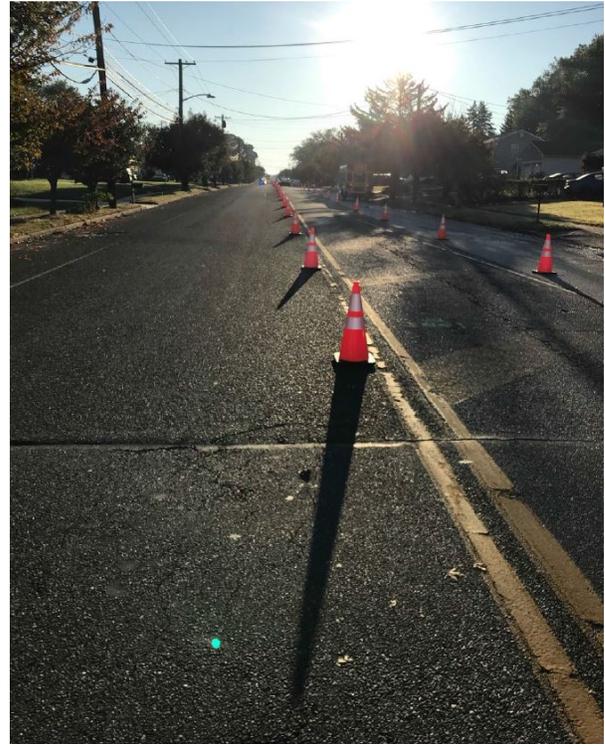


Figure 5: Traffic control implemented

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
