

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 15
March 15, 2020 to March 21, 2020**



Figure 1: New Concrete driveway apron, curb and topsoil

Work Completed Week of March 21, 2020

- Installation of concrete sidewalk, curb and reinforced driveways along Chapel Avenue
- Road restoration
- Reset one existing casting

Quantities Week of March 21, 2020

- **Item #17:** Dense-Graded Aggregate Base Course, 8" Thick (252.22 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (99.52 TON)
- **Item #25:** Reset Existing Casting (1 UN)
- **Item #31:** Concrete Driveway, Reinforced, 6" Thick (155.72 SY)
- **Item #34:** 9"x18" Concrete Vertical Curb (1,034.00 LF)

- **Item #66:** Topsoiling, 4” Thick (193.00 SY)
- **Item #68:** Fertilizing and Seeding, Type F (193.00 SY)
- **Item #70:** Police Uniform Law Enforcement Officers (66.00 HR)
- **Item #1C:** Concrete Sidewalk, 4” Thick (114.48 SY)

Summary of Work Completed Week of March 21, 2020

Lexa Concrete (Lexa) continued with demolition of existing concrete and replacement with new concrete sidewalk, curb, reinforced driveways, curb ramps, and detectable warning surfaces. The seven trees that conflicted with construction were removed by Cherry Hill Township on Saturday. Lexa also worked on Saturday pouring concrete driveway aprons. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Uniformed Law Enforcement Officers are additionally utilized for traffic control. A progress meeting via teleconference was held on March 18, 2020 to review all project related activities. The project will continue as planned despite the current pandemic.

Anticipated Work for Week of March 28, 2020

Lexa will continue with the removal and replacement of concrete curb, sidewalk, driveways, and curb ramps as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project.

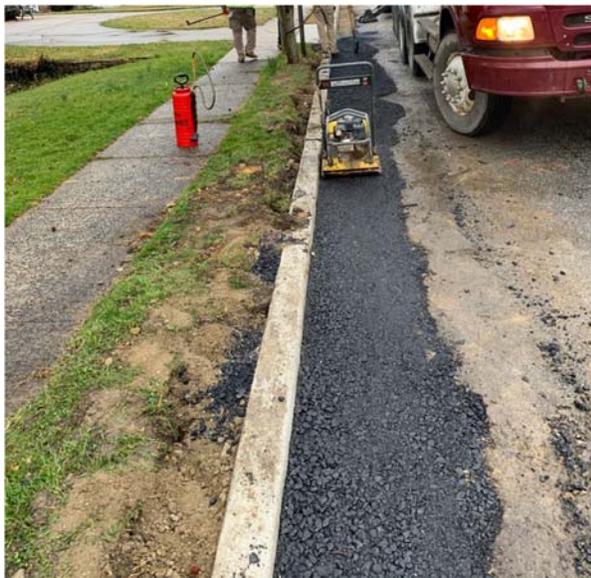


Figure 2: Road restoration



Figure 3: New concrete sidewalk and forms for vertical curb



Figure 4: Pouring vertical curb



Figure 5: Forming new concrete apron

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:


Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
