


**Bid #B7-19, Reclamation and Resurfacing of Jarvis Road (CR 687)  
NJDOT County Aid: CA-PRO-2018-CC-00084  
Township of Gloucester, Camden County, NJ**

**Progress Report #5**

**Week Ending April 10, 2020**


**Progress Photographs:**

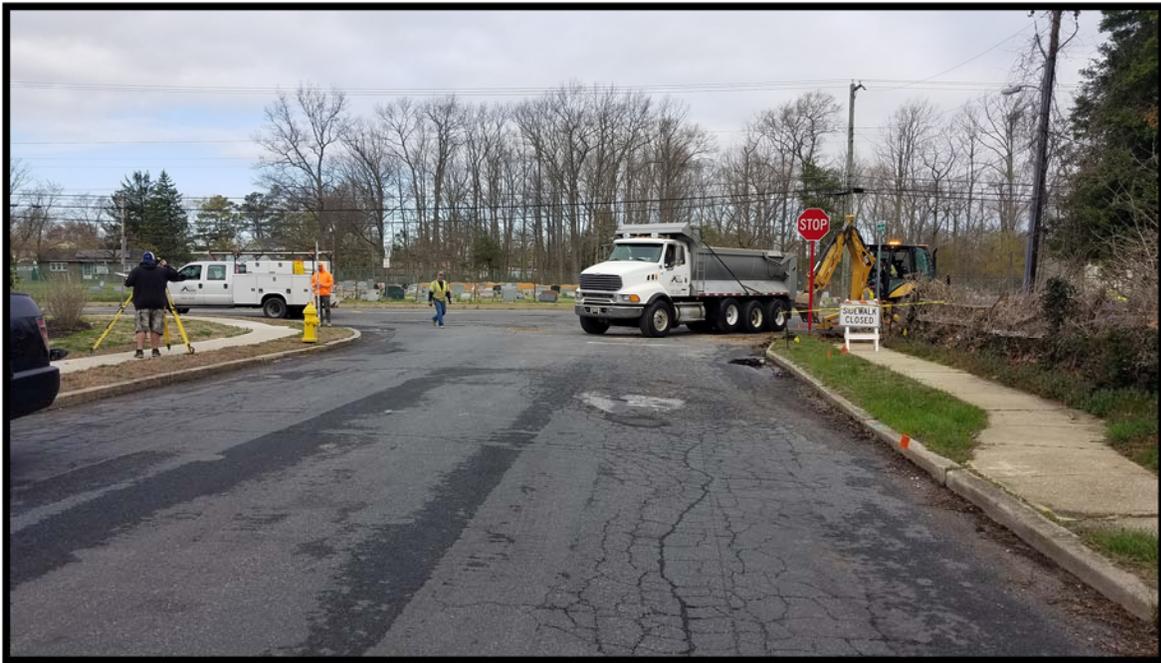

Contractor remobilized on April 6, 2020 after winter shutdown period and began concrete flatwork installation on Jarvis Road at the intersection of Cottage Gate Road.



Concrete curb forms installed at the intersection of Jarvis Road and Cottage Gate Road.

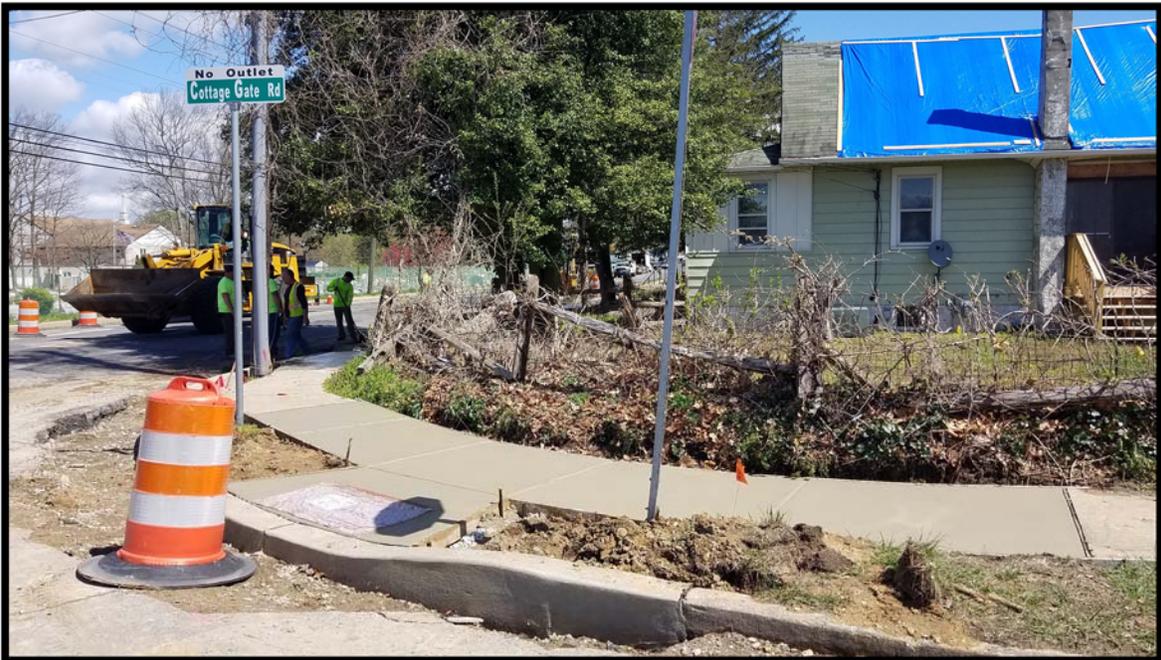

Concrete curb, sidewalk and ADA Accessible Ramp installed at the intersection of Jarvis Road and Cottage Gate Road.




Preparing for Concrete Curb and Gutter adjacent to Double "B" Inlets near cemetery at STA 87+00, Left.



Concrete Curb and Gutter placed at "E" Inlet near cemetery at STA 87+00, Right.




Trench box in place for installation of 18" Reinforced Concrete Pipe (RCP) between existing manhole near STA 95+15 heading towards proposed manhole at STA 97+05.

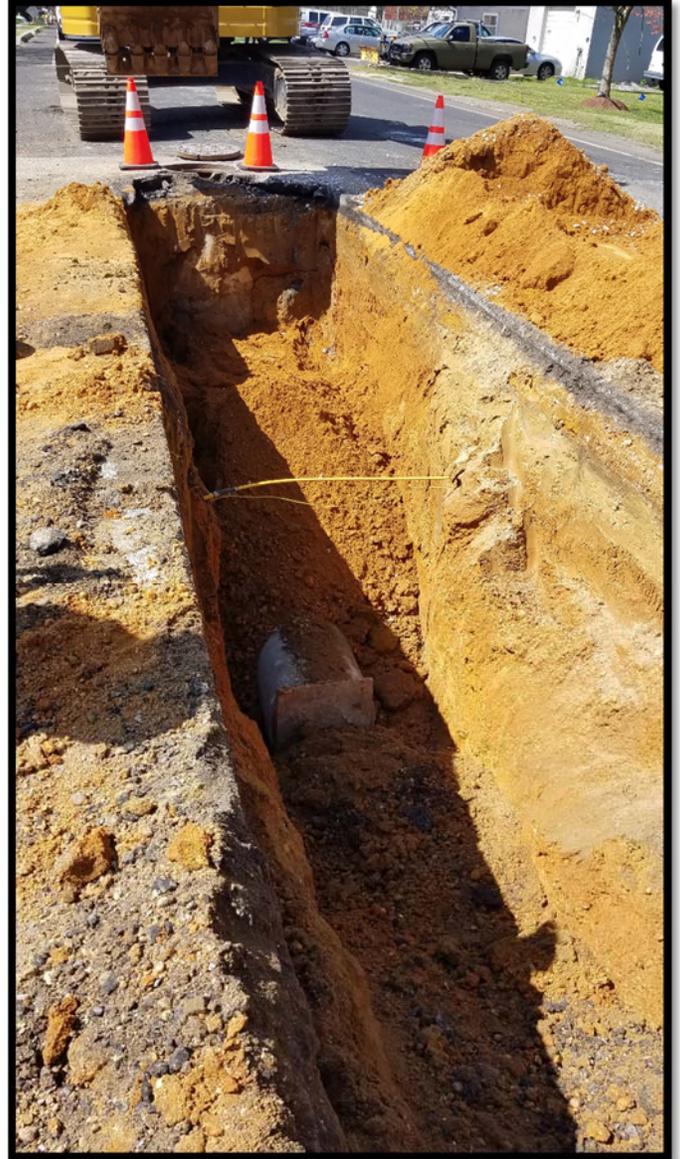

18" RCP installed in trench near STA 95+20 before compaction and setting of next section of pipe.



Dense Graded Aggregate being installed above new 18" RCP at STA 95+10.

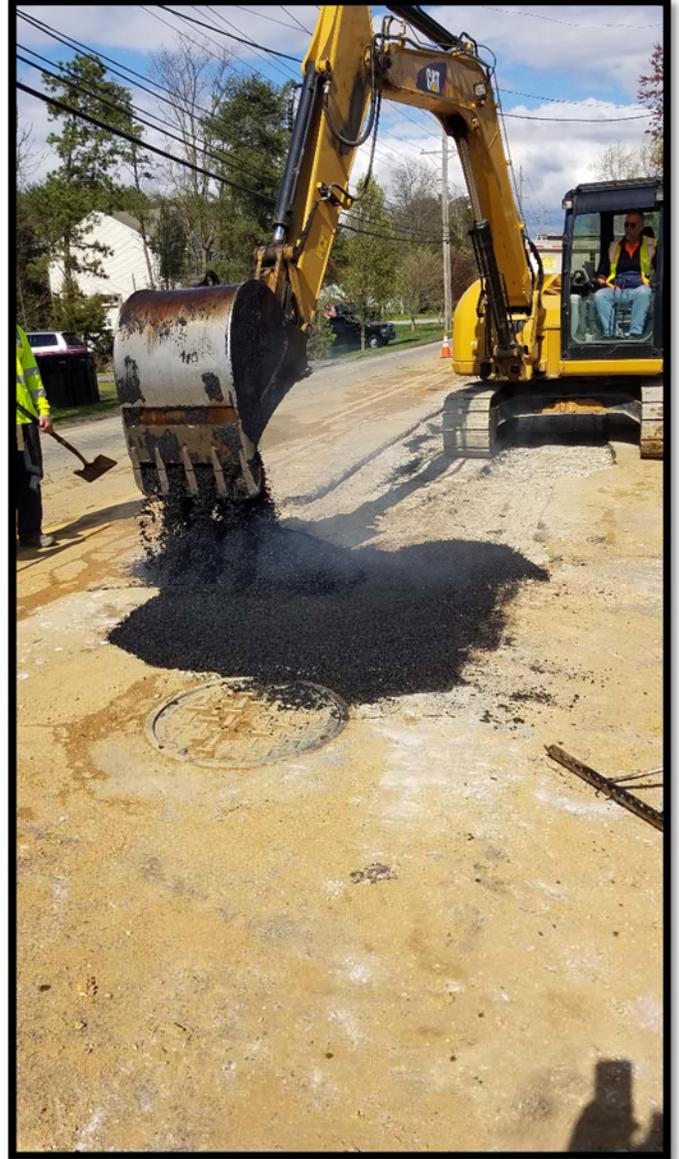

Hot Mix Asphalt Trench restoration above new 18" RCP at STA 95+10.



Hot Mix Asphalt Trench restoration above new 18" RCP at STA 95+10.



18" Reinforced Concrete Pipe Certification Stamp from Oldcastle.

### Work Completed this Report Cycle:

- The contractor re-mobilized from the winter shutdown on Monday April 6th 2020.
- The concrete crew began removing existing concrete and installing new curb, gutter and flat work as per the plan, beginning at station 82+40 (which corresponds with Cottage Gate Rd) and continued to 89+50 (New Brooklyn - Erial Rd). They omitted 20 LF of curb at STA 85+60 right and added 8 SY of concrete driveway apron at STA 85+60 left (cemetery).
- The pipe crew began work on Tuesday April 7th. They spent Tuesday and Wednesday digging test holes and locating existing utilities between stations 94+00 and 103+00. A utility conflict at station 97 + 15 has resulted in RFI #4. RFI #4 was approved by the Assistant County Engineer on April 9, 2020. The Contractor will be re-locating the manhole and inlets 10 feet up station, utilize an offset Double "B" Inlet on the right side and "A" or "D" double inlets on the left shoulder.
- The pipe crew spent Thursday and Friday installing approximately 140 lf of 18 inch RCP pipe from the existing manhole at station 95 + 05 towards the proposed inlets at station 97 + 15.

### Changes to the Initial Contract items:

- No change orders to the Contract to Date, but Work Directives #1 and #2 have been authorized to resolve utility conflicts with negligible impacts to the overall construction cost.

### Project Schedule:

- The initial date for Substantial Completion was Saturday, April 25, 2020 and the date of Final Completion was Monday, May 25, 2020. However, since the winter shutdown was implemented, the dates have been adjusted accordingly. The amended Notice To Proceed issued by the County Engineer on April 1, 2020 delineates the project completion dates as Friday, August 28, 2020 for Substantial Completion and Sunday, September 27, 2020 for Final Completion.
- 19% of time used to date
- 5.2% paid to date.

Prepared by: Mark R. Basehore, Jr., PE, CME  
Bach Associates, PC
