

**Bid #B7-19, Reclamation and Resurfacing of Jarvis Road (CR 687)
NJDOT County Aid: CA-PRO-2018-CC-00084
Township of Gloucester, Camden County, NJ**

Progress Report #3

Week Ending November 29, 2019

Progress Photographs:



Double "B" inlet and 18" Reinforced Concrete Pipe (RCP) being installed near STA 83+25.



Road restoration between Double "B" inlet and existing inlet near STA 83+25.




Existing "B" inlet at STA 113+00R being converted to Double "B" inlet.




Gas Main at STA 113+00 in direct conflict with proposed 15" RCP.



Cradle installed to protect gas main at STA 113+00

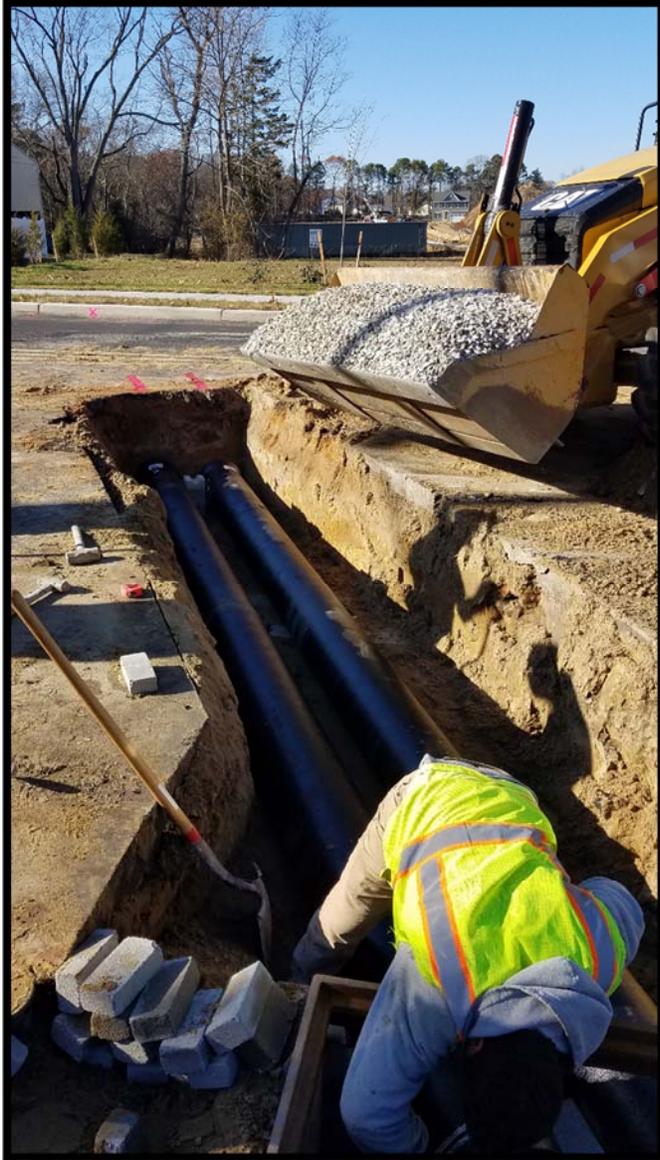

Double 12" Ductile Iron Pipe being installed in lieu of 15" RCP at STA 113+00 due to gas main conflict.

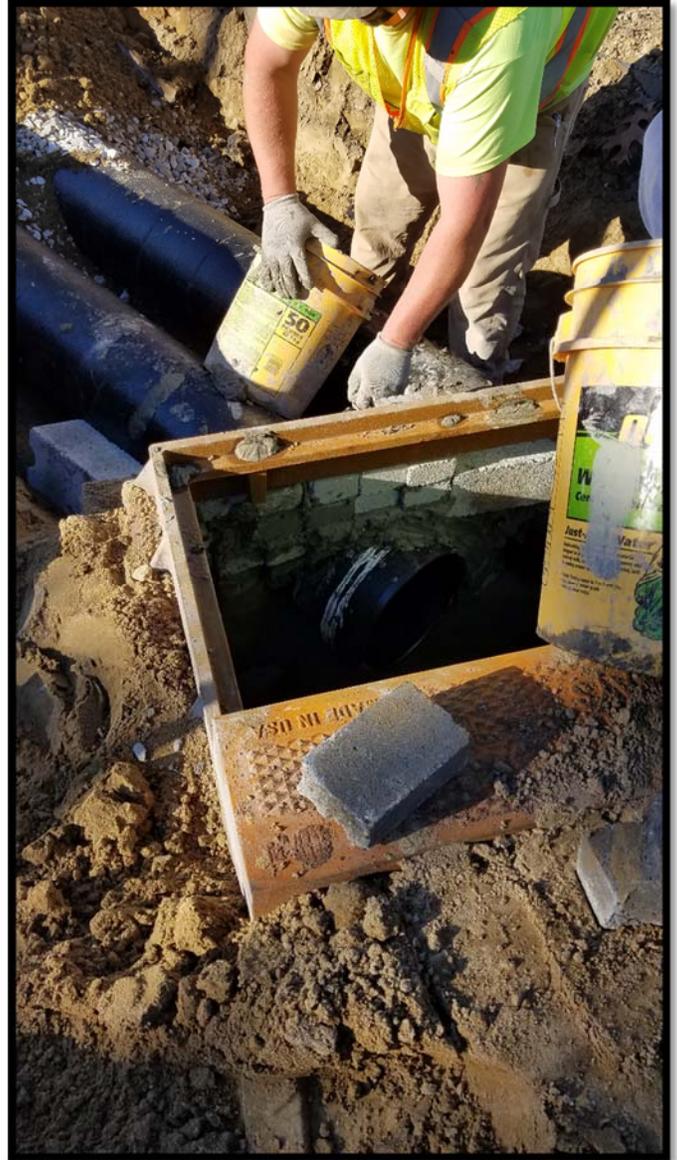

Double 12" Ductile Iron Pipe being grouted into inlet.



New double "B" inlet being installed at STA 113+00L.



Road restoration being completed at STA 113+00.

Work Completed this Report Cycle:

- Upgrades to storm sewer system at STA 83+25 was completed including installation of Double "B" inlet and installation of connecting 18" RCP from new inlet to existing manhole.
- Upgrades to storm sewer system at STA 113+00 was completed including the conversion of a "B" inlet into a Double "B" inlet on the right side of the Base Line and installation of a Double "B" inlet on the left side of the Base Line. Double 15" Ductile Iron Pipe was installed between inlets in lieu of 15" RCP due to direct conflict with proposed 15" RCP.
- No construction occurred over the Thanksgiving Day holiday.

Changes to the Initial Contract items:

- No changes to the Contract to Date.
- RFI #1 for conflict between proposed 18" RCP storm pipe and existing traffic signal foundation at STA 80+25R to be resolved with "If & Where Directed" quantities for a Storm Manhole and additional length of 18" RCP.
- RFI #2 for conflict between proposed 15" RCP storm pipe and existing gas main at STA 113+00 was resolved with "If & Where Directed" quantities for 12" Ductile Iron Pipe.

Project Schedule:

- The date for Substantial Completion is Saturday, April 25, 2020 and the date of Final Completion is Monday, May 25, 2020. However, if a winter shutdown is in effect, the dates will be adjusted accordingly. Additionally, final pavement in the spring/summer will be coordinated with the school schedule.
- 14% of time used to date
- 0.0% paid to date.

Prepared by: Mark R. Basehore, Jr., PE, CME
Bach Associates, PC
