

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 25
June 7, 2020 to June 13, 2020**



Figure 1: Concrete island construction

Work Completed Week of June 13, 2020

- Lexa Concrete sawcut and demolished roadway for concrete islands construction
- Concrete edge restraint and subbase placed for concrete islands

Quantities Week of June 13, 2020

- **Item #6:** Drum (70 UN)
- **Item #16:** Removal of Pavement (333.28 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (37.23 TON)
- **Item #70:** Police Uniform Law Enforcement Officers (81.5 HR)
- **Item #71:** 6"x12" Concrete Edge Restraint (808 LF)

Summary of Work Completed Week of June 13, 2020

Lexa Concrete (Lexa) began work on concrete islands along Chapel Avenue. Lexa sawcut and demolished sections of the existing roadway in preparation for concrete island construction. Concrete edge restraint and concrete subbase was placed for future installation of pavers. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Uniformed Law Enforcement Officers are additionally utilized for traffic control. The project will continue as planned despite the current pandemic. An onsite progress meeting was held on June 8, 2020 to review all project related activities.

Anticipated Work for Week of June 20, 2020

Lexa will continue with the removal of existing roadway and installation of concrete islands as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project.



Figure 2: Sawcuts for concrete island



Figure 3: Concrete island subbase

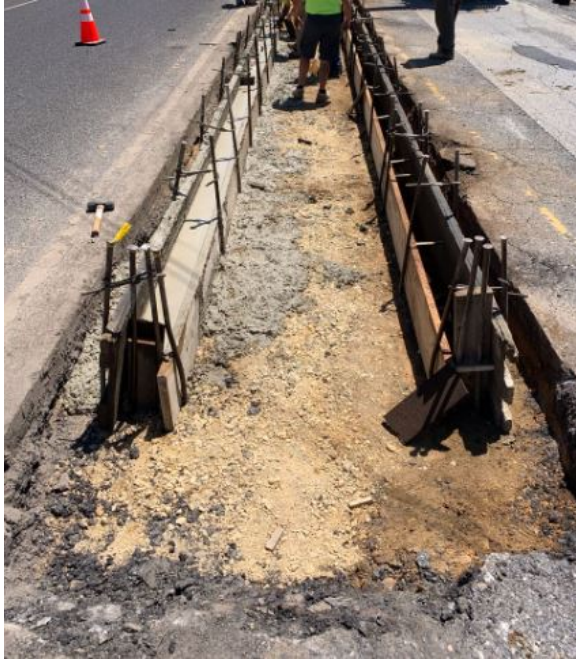


Figure 4: Concrete curb restraint placed



Figure 5: Concrete island base placed

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read "JR".

Joseph R. Ragusa, P.E.

Remington & Vernick Engineers
