

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 26
June 14, 2020 to June 20, 2020**



Figure 1: Concrete island construction

Work Completed Week of June 20, 2020

- Lexa Concrete sawcut and demolished roadway for concrete islands construction
- Concrete edge restraint and subbase placed for concrete islands
- Installed cobblestone pavers in concrete islands

Quantities Week of June 20, 2020

- **Item #8:** Construction Signs (96 F)
- **Item #16:** Removal of Pavement (448.77 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (65 TON)
- **Item #70:** Police Uniform Law Enforcement Officers (113 HR)
- **Item #71:** 6"x12" Concrete Edge Restraint (1121 LF)
- **Item #72:** Cobblestone Paving (149.78 SY)

Summary of Work Completed Week of June 20, 2020

Lexa Concrete (Lexa) continued work on concrete islands along Chapel Avenue. Lexa sawcut and demolished sections of the existing roadway in preparation for concrete island construction. Concrete edge restraint and concrete subbase was placed for the installation of concrete pavers within the islands. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Flaggers are being utilized and continuously coordinated with the Cherry Hill Township Police Department. Uniformed Law Enforcement Officers are additionally utilized for traffic control. The project will continue as planned despite the current pandemic.

Anticipated Work for Week of June 27, 2020

Lexa will continue with the removal of existing roadway and installation of concrete islands as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project. An onsite progress meeting will be held on June 22, 2020 to review all project related activities.



Figure 2: Concrete island reinforced subbase



Figure 3: Concrete island base placed



Figure 4: Roadway restoration

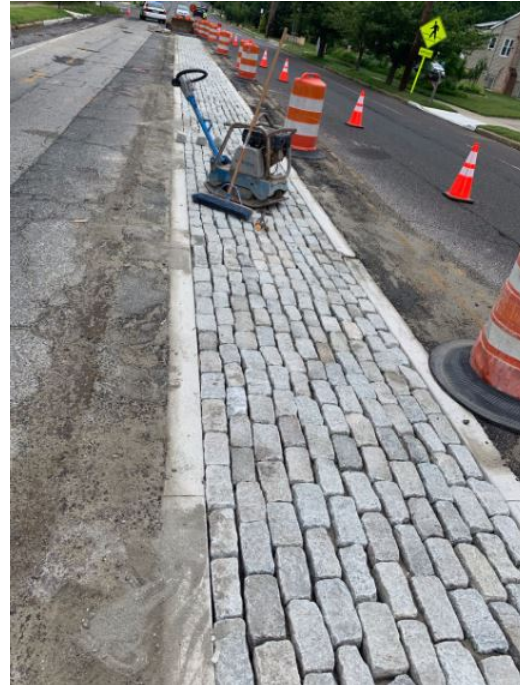


Figure 5: Concrete island pavers installed

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read "JR".

Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
