

**Bid #B7-19, Reclamation and Resurfacing of Jarvis Road (CR 687)
NJDOT County Aid: CA-PRO-2018-CC-00084
Township of Gloucester, Camden County, NJ**

Progress Report #19

Week Ending July 17, 2020

Progress Photographs:



Photograph 1 – Base paving of the returns at Sherri Lane, Lynn Drive, Kay Lane and Rhode Island Avenue were completed this week.



Photograph 2 – Preparing gutterline for full depth reclamation of the roadway.



Photograph 3 – Full depth reclamation admixture of cement placed prior to being mixed with the reclaimer/stabilizer.




Photograph 4 – Water truck and reclaimer/stabilizer in use along northbound lanes of Jarvis Road.



Photograph 5 – Sheep's foot roller compacting reclaimed mixture of existing, pulverized roadway base, water and cement.



Photograph 6 – Reclaimed roadway begin compacted by roller and plate tamper

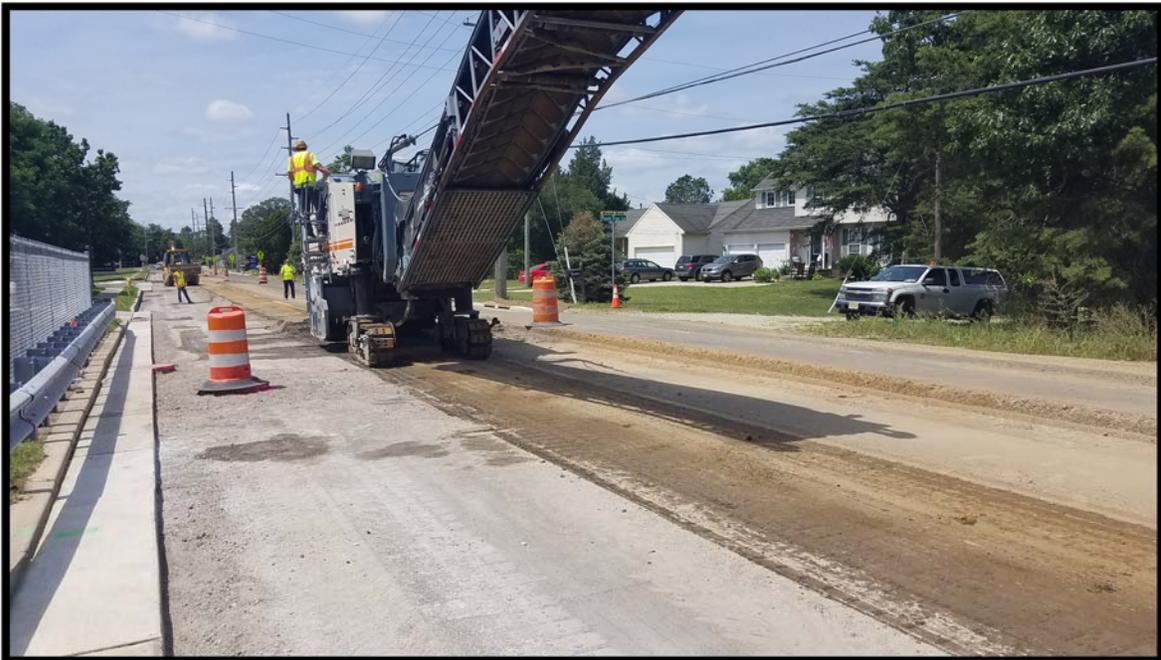

Photograph 7 – Milling of compacted, reclaimed surface to finished subgrade elevation.



Photograph 8 – Handicapped accessible ramp and concrete header curb being installed at Sturbridge Drive.



Photograph 9 – Restorations being completed near Mary Ellen Lane.



Photograph 10 – Concrete curb being installed along 1540 Jarvis Road.

Work Completed this Report Cycle:

This summarizes progress from July 13th through July 17th, 2020.

- Monday, the concrete crew poured concrete for the sidewalk and aprons at 1480 Jarvis Road, completed the apron at station 129+50R and poured sidewalk between stations 126+20R and 127+35R. Tuesday they did not pour concrete, but excavated and set forms for the curb at 1570 Jarvis Road and sidewalk at 1436 and 1464 Jarvis Road. Wednesday the concrete crew poured the radius curb at the north corner of Sturbridge Drive and the access ramp at the south corner. Thursday they poured concrete for the apron at 1570 Jarvis Road and sidewalk at 1436 and 1464 Jarvis Road. Friday the concrete crew poured concrete for the monolithic curb/gutter at inlet D-63 (Sturbridge Drive) and vertical curb along 1500, 1540, 1560 and part of 1570 Jarvis Road.
- Monday the paving crew base paved the returns at Sherri Lane, Lynn Drive, Kay Lane and Rhode Island Avenue.
- Monday and Tuesday the road crew continued the full depth reclamation along both sides of Jarvis Road between stations 115+00 and 126+00. Wednesday the road crew continued the full depth reclamation along both sides of Jarvis Road between stations 126+00 and 133+00. Thursday they began milling out the excess material and fine grading the roadway subbase between stations 115+00 and 122+50. Friday the road crew continued milling and fine grading the roadway from 122+50 to 130+00.

- Also on Friday, a third crew was onsite adjusting manhole castings and valve boxes beginning at station 115+00 and working their way north.

Changes to the Initial Contract items:

- No change orders to the Contract to Date, but Work Directives #1 and #2 have been authorized to resolve utility conflicts with negligible impacts to the overall construction cost.

Project Schedule:

- The initial date for Substantial Completion was Saturday, April 25, 2020 and the date of Final Completion was Monday, May 25, 2020. However, since the winter shutdown was implemented, the dates have been adjusted accordingly. The amended Notice To Proceed issued by the County Engineer on April 1, 2020 delineates the project completion dates as Friday, August 28, 2020 for Substantial Completion and Sunday, September 27, 2020 for Final Completion.
- Status of Work Completed to Date based on approximate percentages:
 - Concrete Flatwork: 96%
 - Storm Sewer: 100%
 - Paving: 30%
 - Overall Project: 78%

 - Time Used to Date: 66%
 - Paid to Date: 12.9% (Not including Payment Application #3 currently under review)

Prepared by: Mark R. Basehore, Jr., PE, CME
Bach Associates, PC
