

Camden County Department of Public Works

Division of Engineering

Kresson Road (CR 671)

Roadway and Drainage Improvements

From Brace Road (NJSH 154) to Howard Johnson Road

Cherry Hill Township, Camden County, New Jersey

Weekly Progress Report # 10

August 3, 2020 to August 7, 2020



Figure 1

Concrete curb constructed along WB Kresson Road with expansion joints 10 feet apart and topsoil applied. Temporary egress created for residents along WB Kresson Road.



Figure 2

Contractor used 13' curb taper for storm drainage inlet at Sta. 132+58 (left offset) due to proximity to the intersection corner



Figure 3

McNaughton's driveway at Sta. 119+20 (left offset) being constructed



Figure 4

Monolithic curb and gutter constructed for the driveway at Sta. 129+90 (left offset)



Figure 5

Form placed for potential field modification of adding a concrete curb header for curb ramp 'P' at Sta. 132+82 (left offset)



Figure 6

Additional 15 LF of existing sidewalk removed at Sta.133+30 (left offset) due to existing curb and sidewalk being monolithic



Figure 7

Pavers reset with concrete base underneath of the driveway at Sta. 119+20 (left offset)



Figure 8

Sawcut contractor on site in preparation for excavation for the gutter construction along WB Kresson Road

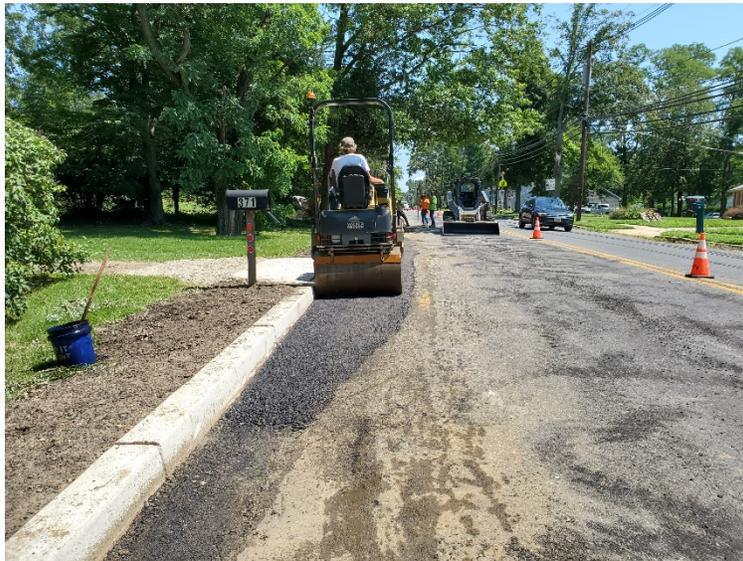


Figure 9

8" HMA used with temporary 8" curb reveal along WB Kresson Road

Work Completed Week of August 7, 2020:

- Contractor mobilized
- Daily detour of traffic on Kresson Road
- Construction of 9" x 18" concrete vertical curb, monolithic curb and gutter, 8" HMA, and topsoil from Sta. 129+50 to Sta. 132+82
- Installation of Curb Piece, Eco Type 'N' on storm drainage inlet located at Sta. 132+58 (left offset)
- Pavers reset and concrete base used at the driveway at Sta. 119+20 (left offset)

Quantities Week of August 7, 2020:

- Item C13- Reset Mailbox- 1 UN
- Item C14- Reset Concrete Pavers- 35 SY
- Item C15- Concrete Driveway, 6" Thick- 35 SY
- Item C18- 9" x 18" Concrete Vertical Curb- 281 LF
- Item C33- Curb Piece, Eco Type 'N'- 1 UN
- Item C36- Monolithic Curb and Gutter- 157 LF

Summary of Work Completed Week of August 7, 2020:

The contractor mobilized on site and setup traffic control for a daily detour to allow construction to commence. Traffic police directors are on site assisting with traffic control daily. Installation of concrete vertical curb continued from Sta. 130+50 to Sta. 132+82. Installation of monolithic curb and gutter continued from Sta. 129+50 to Sta. 130+50. Concrete pavers reset at Sta. 119+20 (left offset) using concrete base underneath. Topsoil was spread behind the new curb along WB Kresson Road. Mailbox reset at Sta. 130+47.

Anticipated work for Week of August 14, 2020:

There will be a detour with one-way traffic setup daily. Traffic police directors are on site assisting with traffic control daily. Contractor will continue to install concrete curb, concrete driveways, and monolithic curb and gutter along WB Kresson Road. Contractor will continue apply 8" HMA adjacent to the new concrete curb and spread topsoil along WB Kresson Road. Contractor will start to construct curb ramp 'P' from plans at Sta. 132+82 (left offset). Contractor will start to construct concrete sidewalk at Sta. 133+50.

Notice to Proceed Date: Tuesday, May 26, 2020

Contract Completion Milestones

Substantial Completion Date: Monday, August 24, 2020

Final Completion Date: Wednesday, September 23, 2020

Concrete Flatwork/Curb: 34%

Storm Sewer: 100%

Paving: 0%

Percent Complete by Duration: 44%

Percent Complete by Payments: 32%

Prepared By:

Maser Consulting



Richard A. Brown

Discipline Leader
