

Camden County Department of Public Works

Division of Engineering

Kresson Road (CR 671)

Roadway and Drainage Improvements

From Brace Road (NJSH 154) to Howard Johnson Road

Cherry Hill Township, Camden County, New Jersey

Weekly Progress Report # 13

August 24, 2020 to August 28, 2020

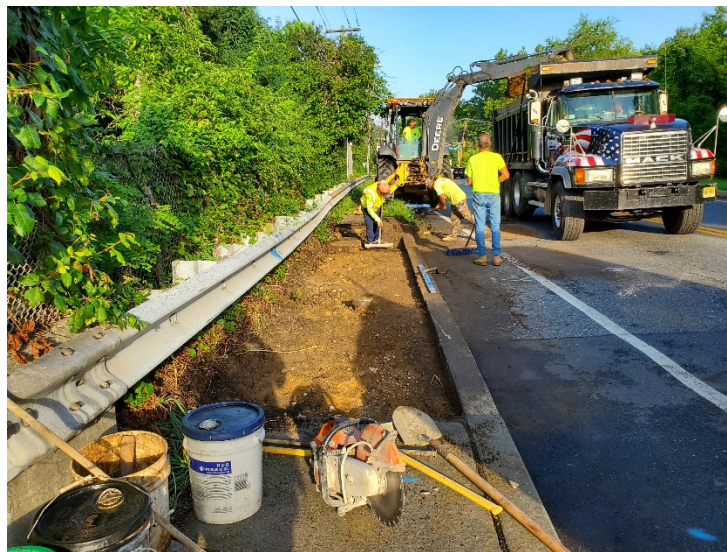


Figure 1

Removal of existing concrete curb and concrete sidewalk along EB Kresson Road



Figure 2

Concrete sidewalk 4" thick and a walking space 4' wide constructed from Sta. 140+30 to Sta. 147+55 (right offset)



Figure 3

Concrete sidewalk 4" thick and a walking space 4' wide constructed from Sta. 135+50 to Sta. 136+50 (right offset)



Figure 4

Monolithic curb gutter constructed from Sta. 134+08 to Sta.138+75 (right offset)



Figure 5

Concrete curb constructed from Sta. 138+75 to Sta. 142+74



Figure 6

Field modification at Sta. 139+40 as proposed curb was in line with existing Verizon manholes. Concrete curb shifted 1' away using 6' taper on both sides.



Figure 7

Sawcut subcontractor was on site to cut along EB Kresson Road.



Figure 8
Forms erected and left overnight for use in future workday

Work Completed Week of August 28, 2020:

- Contractor mobilized
- Daily detour of traffic on Kresson Road
- Construction of 9" x 18" concrete vertical curb, concrete sidewalk, monolithic curb and gutter along EB Kresson Road

Quantities Week of August 28, 2020:

- Item C18- 9" x 18" Concrete Vertical Curb- 450 LF
- Item C36- Monolithic Curb and Gutter- 467 LF
- Item M2- Concrete Sidewalk, 4" Thick Township- 305 SY

Summary of Work Completed Week of August 28, 2020:

The contractor mobilized on site and setup traffic control for a daily detour to allow construction to commence. Traffic police directors are on site assisting with traffic control daily. Construction of concrete vertical curb, concrete sidewalk, and monolithic curb and gutter were done from Sta. 134+10 to Sta. 147+55 (right offset). Topsoil was spread behind the new curb along EB Kresson Road.

Anticipated work for Week of September 4, 2020:

There will be a detour with alternating traffic setup daily. Traffic police directors are on site assisting with traffic control daily. In anticipation of the school reopening, milling, paving, striping, and any outstanding concrete flatwork are to be completed from Sta. 134+00 to 144+00. Contractor will also finish constructing the curb ramps at Sta. 140+06 and 140+26 (both right offsets). Contractor will continue construction on the driveway at Sta. 121+20 (left offset).

Notice to Proceed Date: Tuesday, May 26, 2020

Contract Completion Milestones

Substantial Completion Date: Monday, August 24, 2020

Final Completion Date: Wednesday, September 23, 2020

Concrete Flatwork/Curb: 52%

Storm Sewer: 100%

Paving: 0%

Percent Complete by Duration: 80%

Percent Complete by Payments: 60%

Prepared By:

Maser Consulting



Richard A. Brown
Discipline Leader
