

**Camden County Department of Public Works  
Division of Engineering  
Improvements to Chapel Avenue (CR 626) from  
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)  
Township of Cherry Hill, Camden County, New Jersey  
Weekly Progress Report No. 38  
September 6, 2020 to September 12, 2020**



*Figure 1: Concrete center island construction*

**Work Completed Week of September 12, 2020**

- Lexa continued with demolition of roadway for the construction of center cobblestone islands along Chapel Avenue
- Concrete edge restraint curb and paver base for center islands placed
- Tough Turf continued with installation of cobblestone pavers for center islands

**Quantities Week of September 12, 2020**

- **Item #16:** Removal of Pavement (214 SY)
- **Item #17:** Dense-Graded Aggregate Base Course, 8" Thick (37.67 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (18.58 TON)
- **Item #34:** 9"x18" Concrete Vertical Curb (80.5 LF)
- **Item #66:** Topsoiling, 4" Thick (18.86 SY)
- **Item #68:** Fertilizing and Seeding, Type F (230.74 SY)
- **Item #70:** Police Uniform Law Enforcement Officers (75 HR)
- **Item #71:** 6"x12" Concrete Edge Restraint (356 LF)

### Summary of Work Completed Week of September 12, 2020

Lexa Concrete continued work on the center cobblestone islands along Chapel Avenue between Haddonfield Road and Cooper Landing Road. The existing roadway was demolished, and concrete edge restraint curb and concrete paver base was placed for the proposed center islands. Lexa installed concrete curb along Chapel Avenue and restored the roadway. Tough Turf onsite to continue with installation of cobblestone pavers for center islands. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Flaggers are being utilized and continuously coordinated with the Cherry Hill Township Police Department. Uniformed Law Enforcement Officers are additionally utilized for traffic control. The project will continue as planned despite the current pandemic. The project is approximately 83% complete. An onsite progress meeting was held on September 9, 2020 to review all project related activities.

### Anticipated Work for Week of September 19, 2020


Lexa will continue with center cobblestone island work, roadway reconstruction, and preparation for paving operations on Chapel Ave. Daily traffic control will continue to be implemented for the duration of the project.



Figure 2: Concrete center island workzone



Figure 3: Excavation for center island

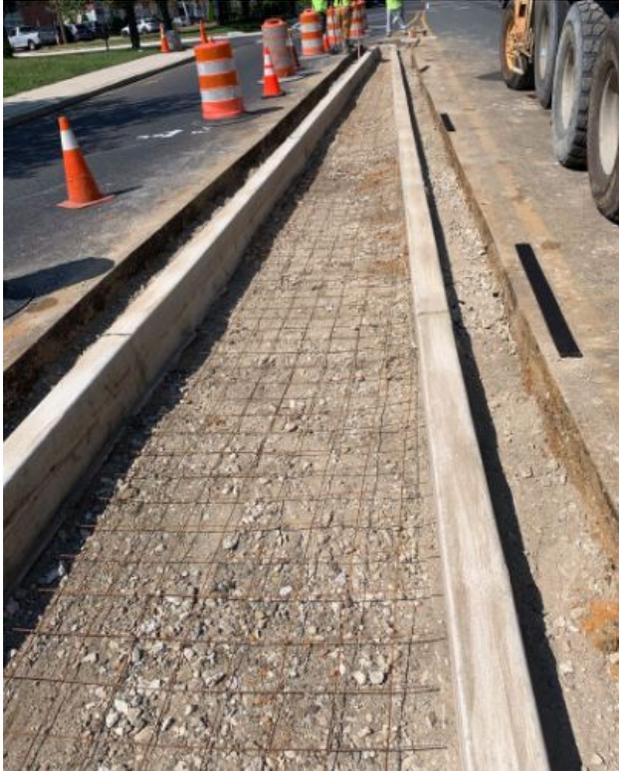

*Figure 4: Center island concrete base preparation*



*Figure 5: Cobblestone pavers installation*

**Notice to Proceed**

October 14, 2019

**Contract Completion**

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

Joseph R. Ragusa, P.E.  
Remington & Vernick Engineers
