

Camden County Department of Public Works

Division of Engineering


Roadway and Drainage Improvements

Along Peter Cheeseman Road (CR 759)

Hickstown Road (CR 688) to Erial Road (CR 706)

Gloucester Township, Camden County, New Jersey

*Weekly Progress Report # 8
August 3, 2020 to August 7, 2020*

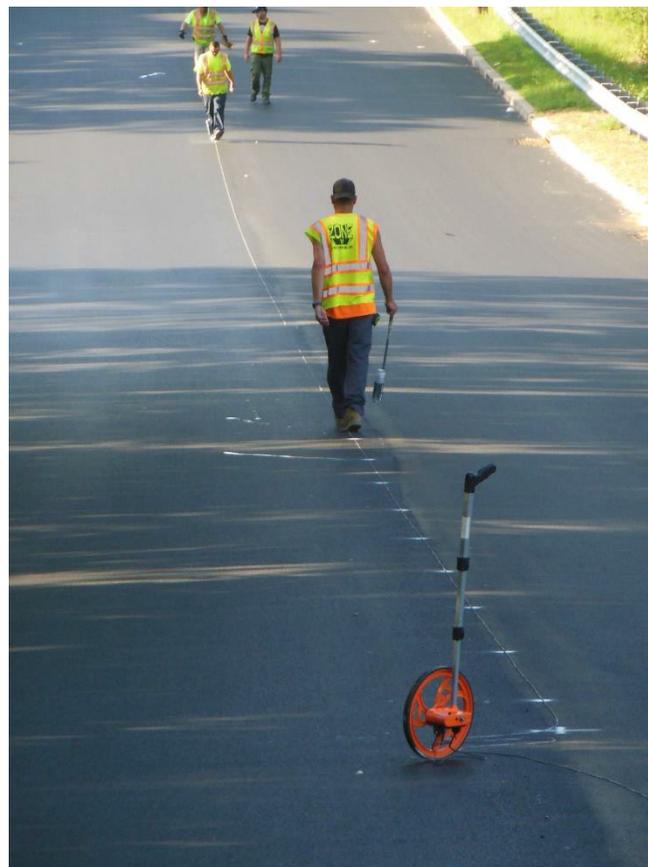

*Figure 1
Layout of final striping*

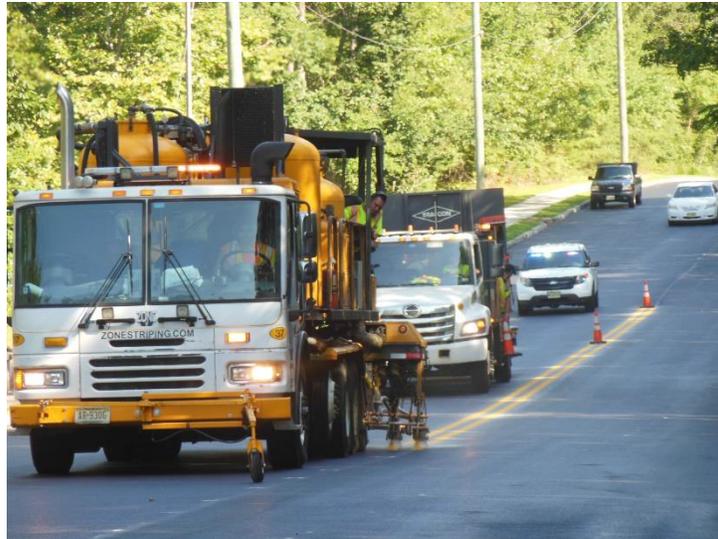


Figure 2
Sub-contractor Zone installing double yellow with GTPD assistants

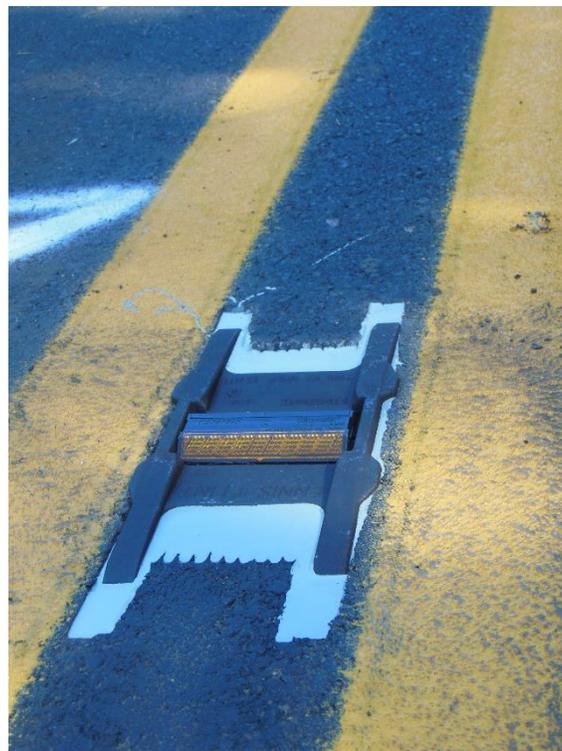


Figure 3
New RPM installed throughout project



*Figure 4
Installing thermo of an Only at Hickstown Road*



*Figure 5
Installing the yellow gorge 24" lines*



Figure 6

Sign posts being installed for a required sign on project

Work Completed Week of August 3, 2020:

- Contractor completed pavement markings and RPM's installation
- Warning signs were installed

Quantities Week of August 3, 2020:

- Item #3: Uniformed Police (36 MH)
- Item #5: Fuel Adjustment (-1.1462 DOL)
- Item #6: Asphalt Adjustment (-1.485974667 DOL)
- Item #44: Traffic Stripes. 4" (25,113 LF)
- Item #45: Traffic Stripes 6" (1,030 LF)
- Item #46: Traffic Stripes 8" (897 LF)
- Item #47: Traffic Marking Symbols (782 SF)
- Item #48: RPM Mono White (41 U)
- Item# 49: Traffic Marking Lines 24" (1,129 LF)
- Item # 50: RPM Mon Amber (64 U)
- Item #51: RPM Bi-directional Amber (78 U)

- Item #52: RPM Bi-directional Blue (8 U)
- Item #53: Regulatory And Warning Signs (61 SF)

Summary of Work Completed Week of July 27, 2020:

Contractor completed the pavement markings and installation of RPM's and signs throughout project

Anticipated work for Week of August 10, 2020:

Finalize the electrical items at the intersection of College Drive and Hickstown Road with Peter Cheeseman.

Notice to Proceed Date: Monday, June 15, 2020

Contract Completion Milestones

Substantial Completion Date: Sunday , September 13, 2020

Final Completion Date: Tuesday, October 13, 2020


Accelerated Completion Date: **Saturday, August 15, 2020**

Percent Complete by Duration: **85% (are calculated to Accelerated Date)**

Percent Complete by Payments: **69%**

Prepared By:

AECOM



Anthony Guerrieri
Project Manager
