Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Making It Better, Together.

Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

Berlin-Cross Keys Road Improvements Contract 3 Bid No. B9-22

Borough of Pine Hill and Townships of Gloucester and Winslow Camden County, New Jersey

CED Project No. 19002364G4

Progress Report #31 Monday, April 17, 2023 to Friday April 21, 2023



Figure: P&A Construction continues to reconstruct the decorative wall.

Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Making It Better, Together.

Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

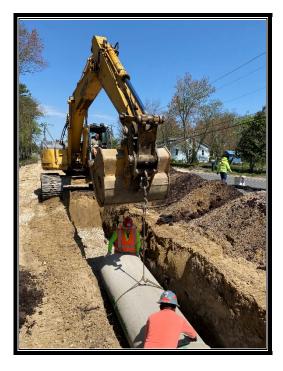


Figure 2: P&A Construction installing reinforced concrete pipe.



Figure 3: P&A Construction crew tying new pipe into existing inlet.

Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

• Work Completed this week:

- P&A Construction continued to install the reinforced concrete pipe installation.
- \circ $\;$ P&A Construction continued precast concrete structures.
- P&A Construction completed constructing the decorative wall.

• Items completed this period:

- Item No.4 Traffic Safety Services 80 Hours
- Item No.8 Excavation, Test Pits 12.44 CY
- o Item No.21 HMA 25M64 Base Course 77.10 Tons
- o Item No.30 24" Reinforced Concrete Pipe, Class V 364 L.F.
- Item No.31 30" Reinforced Concrete Pipe, Class V 150 L.F.
- Item No.33 19"x30" HERCP 144 L.F.
- Item No.41 Inlet Type "B" 2 Unit
- Item No.84 Reconstruction of Decorative Wall Completed 100%
- Item No.91 Relocate Sanitary Sewer Vent 1 Unit
- Item No.SA-2 Manhole 5' Diameter 2 Units

• Progress Next Two Weeks:

- P&A Construction will continue to install the new storm drainage along the main-line.
- P&A Construction continue to install the vertical concrete curb.
- P&A Construction will start grading the sub-grade for the new road widening.

• Next On-Site Meeting:

- The 8th Progress Meeting rescheduled for May 4, 2023 at 1:00 PM on site. (This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
 - Bid Opening Date: June 2, 2022
 - Notice to Proceed: August 23, 2021
 - Start Date: August 23, 2021
 - Substantial Completion Date: July 24, 2023
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: August 23, 2023
 - Initial Award: \$6,946,586.14

Prepared by: Dennis Brown, C.E.T., IV Resident Engineer Colliers Engineering & Design
