

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Berlin-Cross Keys Road Improvements Contract 3
Bid No. B9-22

*Borough of Pine Hill and Townships of Gloucester and Winslow
Camden County, New Jersey*

CED Project No. 19002364G4

Progress Report #32

Monday, April 24, 2023 to Friday April 28, 2023



Figure: P&A Construction completed the decorative wall at Mater Ecclesiae.

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

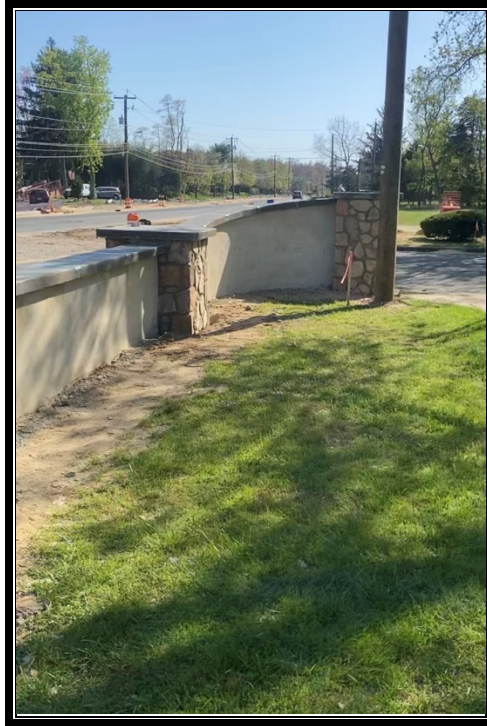


Figure 2: P&A Construction completed the decorative wall at Mater Ecclesiae.



Figure 3: P&A Construction crew installing pipe at Water Quality Chamber.

- **Work Completed this week:**
 - P&A Construction continued to install the reinforced concrete pipe installation.
 - P&A Construction continued precast concrete structures.
 - P&A Construction completed constructing the decorative wall.

- **Items completed this period:**
 - Item No.4 Traffic Safety Services – 80 Hours
 - Item No.8 Excavation, Test Pits – 2.37 CY
 - Item No.14 I-8 Soil Aggregate – 387 CY
 - Item No.21 HMA 25M64 Base Course – 20.40 Tons
 - Item No.29 18” Reinforced Concrete Pipe, Class V – 21 LF
 - Item No.31 30” Reinforced Concrete Pipe, Class V – 174 LF
 - Item No.33 19”x30” HERCP – 214 LF
 - Item No.41 Inlet Type “B” – 2 Unit
 - Item No.42 Inlet Type "Double B" – 1 Unit
 - Item No.68 9"x18" Conc. Vert. Curb – 1257 LF
 - Item No.84 Reconstruction of Decorative Wall – Completed 100%
 - Item No.90 Relocate Sanitary Sewer Connection – 1 Unit

- **Progress Next Two Weeks:**
 - P&A Construction will continue to install the new storm drainage along the main-line.
 - P&A Construction continue to install the vertical concrete curb.
 - P&A Construction will start grading the sub-grade for the new road widening.

- **Next On-Site Meeting:**
 - The 8th Progress Meeting rescheduled for May 4, 2023 at 1:00 PM on site.
(This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
 - Bid Opening Date: June 2, 2022
 - Notice to Proceed: August 23, 2021
 - Start Date: August 23, 2021
 - Substantial Completion Date: July 24, 2023
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: August 23, 2023
 - Initial Award: \$6,946,586.14

Prepared by: Dennis Brown, C.E.T., IV
Resident Engineer
Colliers Engineering & Design
