Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

Berlin-Cross Keys Road Improvements Contract 3 Bid No. B9-22

Borough of Pine Hill and Townships of Gloucester and Winslow Camden County, New Jersey

CED Project No. 19002364G4

Progress Report # 42 Monday, July 3, 2023 to Friday July 7, 2023

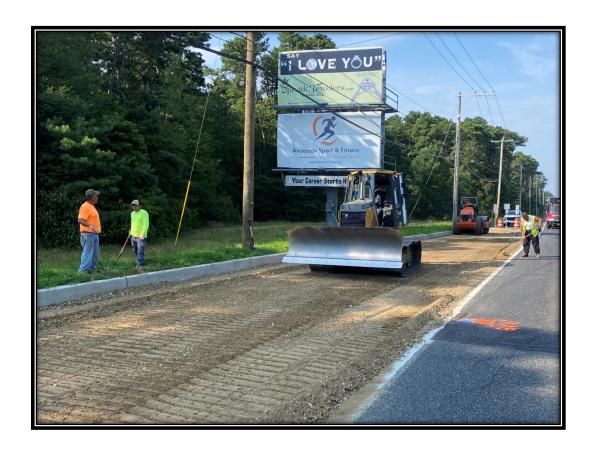


Figure: P&A Construction excavated roadway and installed DGA Base Course.

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com



Figure 2: P&A Construction excavated roadway and installed DGA Base Course.



Figure 3: P&A Construction set drainage structures to finished grade.

Department of Public Works

Almar Dyer Commissioner Liaison

county Making It Better, Together.

Robert Harris Director

2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com

Department of Public Works

Charles J. DePalma Complex

CamdenCounty.com

Work Completed this week:

- o P&A Construction started roadway reconstruction work, excavation and D.G.A..
- P&A reopened roadway to traffic last Friday.

Items completed this period:

- Item No. 4 Traffic Safety Services 48 Hours
- Item No. 8 Excavation, Test Pit 2 Cubic Yards
- Item No.9 Excavation, Unclassified 1,452 Cubic Yards
- Item No.15 Dense Graded Aggregate, 8" Thick 3,066 Square Yards

Progress Next Two Weeks:

- P&A Construction will continue to perform Roadway, Excavation Unclassified
- P&A Construction will continue to install Dense Graded Aggregate

Next Progress Meeting:

- The 13th Progress Meeting has been rescheduled for July,13 2023 at 1:00pm on site. (This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
 - Bid Opening Date: June 2, 2022
 - Notice to Proceed: August 23, 2021
 - Start Date: August 23, 2021
 - Substantial Completion Date: July 24, 2023
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: August 23, 2023
 - Initial Award: \$6,946,586.14

Prepared by: Dennis S. Brown, C.E.T.

Resident Engineer

Colliers Engineering & Design

James Winckowski, PE, County Engineer William England, PE, Assistant County Engineer
