## Department of Public Works

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

# Berlin-Cross Keys Road Improvements Contract 3 Bid No. B9-22

Borough of Pine Hill and Townships of Gloucester and Winslow Camden County, New Jersey

# CED Project No. 19002364G4

Progress Report #45
Monday, July 24, 2023 to Friday July 28, 2023



Figure: P&A Construction continues to excavate and install dense graded aggregate.

Almar Dyer Commissioner Liaison

Robert Harris Director



Department of Public Works Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

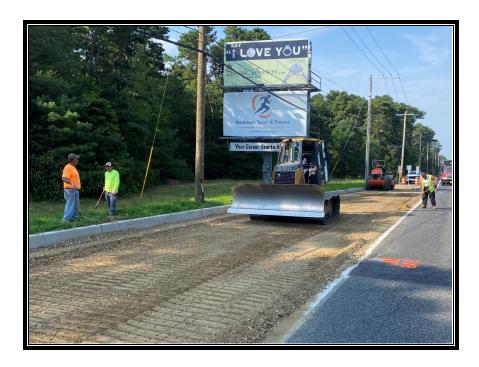


Figure 2: P&A Construction continues to excavate and install dense graded aggregate.



Figure 3: Reviewing additional topsoiling and seeding in the off-site easement.

#### Department of Public Works

Almar Dyer Commissioner Liaison Camden county

Making It Better, Together.

Robert Harris Director 2311 Egg Harbor Road Lindenwold, NJ 08021 phone 856.566.2980 fax 856.566.2988 highway@camdencounty.com CamdenCounty.com

Department of Public Works

Charles J. DePalma Complex

# • Work Completed this week:

- o P&A Construction continued to install topsoil, grass seed and fertilizer.
- o P&A Construction continued to excavate and install dense graded aggregate.

#### • Items completed this period:

- o Item No. 4 Traffic Safety Services 80 Hours
- o Item No. 9 Roadway Excavation, Unclassified 466 Cubic Yards
- o Item No. 15 DGA, Base Course, 8" Thick 1029 Square Yards

## Progress Next Two Weeks:

- o P&A Construction will continue to perform Roadway, Excavation Unclassified
- o P&A Construction will continue to install Dense Graded Aggregate.
- o P&A Construction will continue to install Topsoil, Seed and Fertilizer.
- o P&A Construction to install the last Dual Vortex Separator unit.

## • Next Progress Meeting:

- The next Progress Meeting has been rescheduled for August 3, 2023 at 1:00pm on site.
   (This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
  - Bid Opening Date: June 2, 2022
  - Notice to Proceed: August 23, 2021
  - Start Date: August 23, 2021
  - Substantial Completion Date: July 24, 2023
  - Stop Work: N/AAmended NTP: N/A
  - Final Completion Date: August 23, 2023
  - Initial Award: \$6,946,586.14

Prepared by: Dennis S. Brown, C.E.T.

Resident Engineer

Colliers Engineering & Design

James Winckowski, PE, County Engineer William England, PE, Assistant County Engineer
