

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

Berlin-Cross Keys Road Improvements Contract 3 ***Bid No. B9-22***

*Borough of Pine Hill and Townships of Gloucester and Winslow
Camden County, New Jersey*

CED Project No. 19002364G4

Progress Report #47

Monday, August 7, 2023 to Friday August 11, 2023

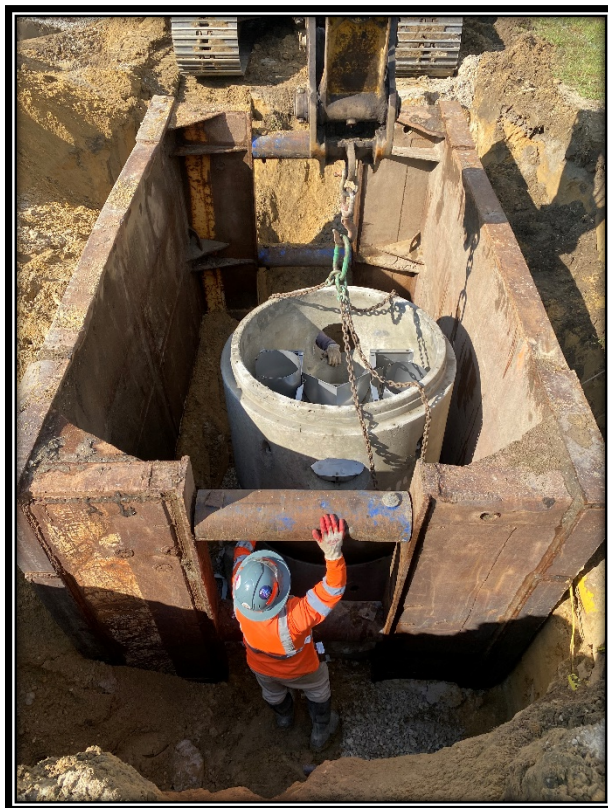


Figure: P&A Construction installing the final Dual Vortex Separator Unit.



Figure 2: P&A Construction completes the installation of the reinforced concrete pipe.



Figure 3: P&A Construction continues to pave the base course.

- **Work Completed this week:**
 - P&A Construction continued to build the widening part of the roadway.
 - P&A Construction completed the installation of the dual vortex unit and pipe.
 - P&A Construction continues to fine grade the D.G.A. and install the base course.

- **Items completed this period:**
 - Item No.4 Traffic Safety Services – 82 Hours
 - Item No.9 Excavation, Unclassified – 284.17 Cubic Yards
 - Item No.15 D.G.A. Base Course, 8” Thick – 337.26 Square Yards
 - Item No.18 Tack Coat – 6 Gallons
 - Item No.21 HMA 25.M64 Base Course, 4” Thick – 750.94 Tons
 - Item No.27 12” PVC Schedule 80/C900 Pipe – 74 L.F.
 - Item No.29 18” R.C.P., Class V – 69.50 L.F.
 - Item No.52 Dual Vortex Separator (WQ-6) – 1 Unit
 - Item No.96 Topsoiling Spreading, 4” Thick – 266.66 SY
 - Item No.97 Fertilizing and Seeding, Type “A-3” – 266.66 SY
 - Item No.SA-19 Removal of Unmarked 24” R.C.P. Pipe – 24 L.F.

- **Progress Next Two Weeks:**
 - P&A Construction will continue to fine grade the D.G.A. along the new widening area.
 - P&A Construction will continue to install HMA 25.M64 Base Course in the widening area.
 - P&A Construction will continue right-of-way transitions into several properties.

- **Next Progress Meeting:**
 - The next Progress Meeting has been rescheduled for August 17, 2023 at 1:00pm on site.
(This meeting may be rescheduled if necessary or become a Microsoft Teams Meeting)
 - Bid Opening Date: June 2, 2022
 - Notice to Proceed: August 23, 2021
 - Start Date: August 23, 2021
 - Substantial Completion Date: July 24, 2023
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: August 23, 2023
 - Initial Award: \$6,946,586.14

Prepared by: Dennis S. Brown, C.E.T.
Resident Engineer
Colliers Engineering & Design
