

Construction Management and Inspection Services



LITTLE GLOUCESTER ROAD (CR 759) ROADWAY IMPROVEMENTS

ERI Job #:30750 78

Township of Gloucester

County of Camden, New Jersey

BI-WEEKLY PROGRESS REPORT #8

July 15, 2024 to July 26, 2024



Figure: 1 – Installation of thermoplastic markings approaching the intersection with Chews Landing Road

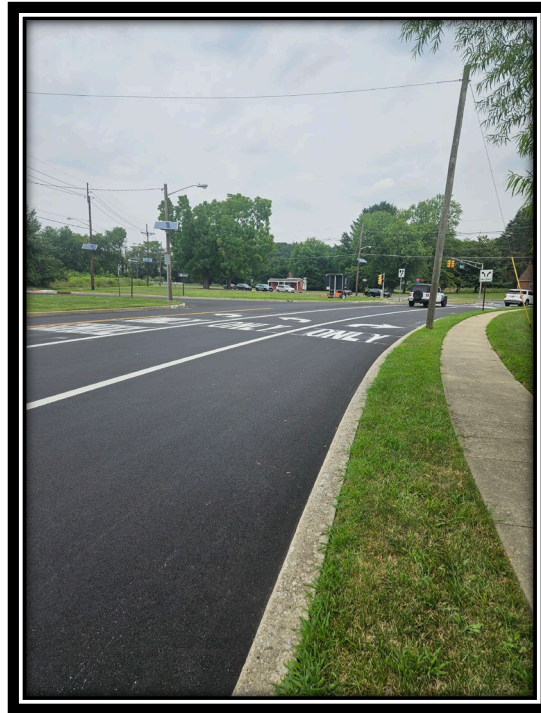


Figure: 2 – Installation of thermoplastic markings approaching the intersection with Chews Landing Road



Figure: 3 – AID taking HMA cores of newly paved roadway to test for thickness and airvoids

Work Completed the Weeks of July 15, 2024 & July 22, 2024:

South State's paving crew completed the installation of HMA driveways for the project. The paving crew installed 268 square yards of HMA driveway. Zone Striping mobilized to the site and installed the majority of the traffic striping and RPMs for the project. Zone installed 13,887 linear feet of 4" white thermoplastic striping, 19,437 linear feet of 4" yellow thermoplastic striping, 119 linear feet of 8" white thermoplastic striping, 445 linear feet of 24" yellow thermoplastic striping, 13 thermoplastic arrows, 16 thermoplastic "ONLY" markings, 176 mono-directional white lens RPMs, 56 mono-directional amber lens RPMs, 111 bi-directional amber lens RPMs and 14 bi-directional blue lens RPMs.

- #6: Traffic Safety Services – 67 MH**
- #33: HMA Driveway, 5" Thick – 268 SY**
- #37: 4" Wide Thermoplastic Striping, White – 13,887 LF**
- #38: 4" Wide Thermoplastic Striping, Yellow – 19,437 LF**
- #40: 8" Wide Thermoplastic Striping, White – 119 LF**
- #42: 24" Wide Thermoplastic Striping, Yellow – 445 LF**
- #43: Traffic Markings Symbols, Arrow – 13 Units**
- #45: Traffic Markings Symbols, Only – 16 Units**
- #46: RPM, Mono-Directional, White Lens – 176 Units**
- #47: RPM, Mono-Directional, Amber Lens – 56 Units**
- #48: RPM, Bi-Directional, Amber Lens – 111 Units**
- #S4: RPM, Bi-Directional, Amber Lens – 14 Units**

Anticipated Work for the Weeks of July 29, 2024 & August 5, 2024:

South State's signage contractor will install the warning and regulatory signs. South State's punch list crew will begin working on punch list items as well.

Bid Opening Date: July 12, 2023

Notice to Proceed Date: November 13, 2023

Revised Notice to Proceed Date: March 14, 2024

Start Date: November 13, 2023

Anticipated Completion Date: August 2, 2024

Original Contract Completion Date: May 10, 2024

Revised Contract Completion Date: October 5, 2024

Contract Completion Percentage: 85.24%

Initial Project Cost: \$1,559,525.00

Prepared By:



C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.
