



# Camden County Department of Public Works Division of Engineering

Roadway Reconstruction and Traffic Signal Improvements to Route 70 Feeder – 27<sup>th</sup> Street (CR 601) to Federal Street (CR 537)

City of Camden, Camden County, New Jersey Contract Bid - B6-23

Progress Report No. 02

September 18, 2023 to September 29, 2022



Figure 1: Concrete Sidewalk

## Work Completed Period of September 29, 2023

- Installed sidewalk, curb and driveway forms and finished new concrete curb, sidewalk, and driveway.
- Installed ADA compliant curb ramps.
- Reset sanitary sewer cleanout, water meter, and gas valve boxes.





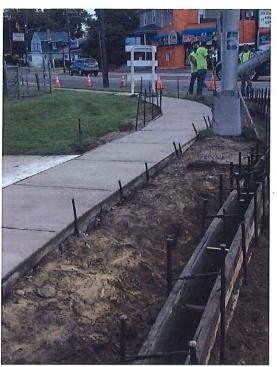


Figure 2: Concrete Sidewalk & Forming Curb



Figure 3: ADA Compliant Curb Ramp



Figure 4: Reset Gas Valve Box



Figure 5: Concrete Driveway





## Quantities Period of September 29, 2023

- Item #7: Inlet Filter Type 2, 2'x 4' (1.00 UN)
- Item #42: Concrete Sidewalk, 5" Thick (499.89 SY)
- Item #44: Concrete Driveway, 6" Thick (50.60 SY)
- Item #45: Detectable Warning Surface (2.67 SY)
- Item #46: 8" x 6" x 18" Concrete Vertical Curb (1,058.00 LF)
- Item #54: Reset Water Meter Box (40.00 UN)
- Item #57: Reset Sanitary Sewer Cleanout (41.00 UN)
- Item #60: Reset Gas Valve Box (6.00 UN)
- Item #87: Police Traffic Director (85.25 HR)

#### Summary of Work Completed Period of September 29, 2023

 Contractor began with removing existing concrete curb, sidewalk, and driveways along 27<sup>th</sup> Street between Marlton Pike and Washington Street. Forms were then installed at the removed sections and new concrete curb, sidewalk and driveways were then poured and finished. Sanitary sewer cleanouts, gas valves, and water meter boxes were also reset within those limits. Police traffic directors were utilized during the days work for traffic control safety measures.

#### Anticipated Work for Period of October 13, 2022

- Continuation of concrete work.
- Begin drainage work and installation of brick pavers.

Notice to Proceed: September 5, 2023

Substantial Completion: February 11, 2024

Final Completion: March 2, 2023

Prepared By:

Joseph R. Ragusa, P.E.

Remington & Vernick Engineers
