

**Camden County Department of Public Works
Division of Engineering
Roadway Reconstruction and Traffic Signal Improvements
to Route 70 Feeder – 27th Street (CR 601) to Federal Street (CR 537)
City of Camden, Camden County, New Jersey
Contract Bid - B6-23
Progress Report No. 10
January 8, 2024 to January 19, 2024**



Figure 1: Compacting HMA Base Course

Work Completed Period of January 19, 2024

- Paving HMA 19M64 base course, 6" thick throughout project limits.
- Resetting manhole castings.

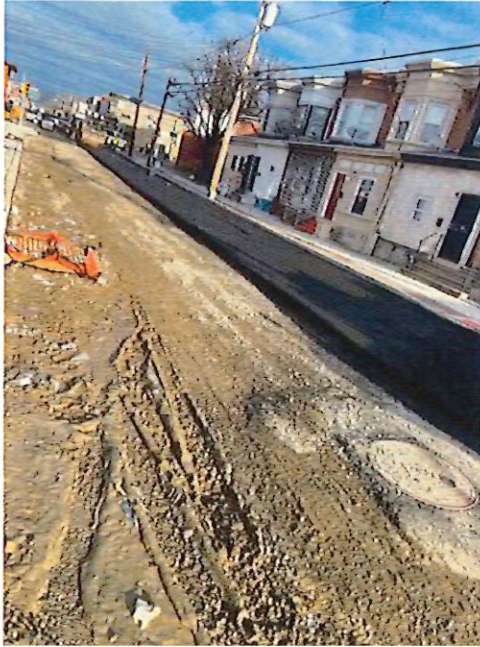


Figure 2: Paving HMA Base Course

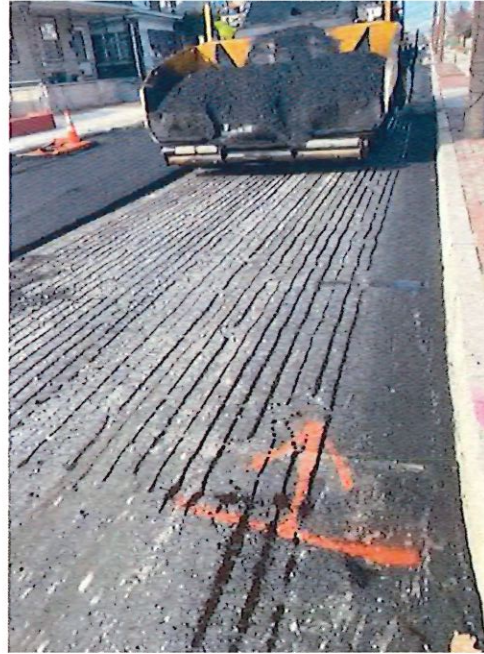


Figure 3: Applied Tack Coat



Figure 4: Compacting HMA Base Course



Figure 5: Resetting Manhole Casting

Quantities Period of January 19, 2024

- **Item #29:** Tack Coat (130.00 GAL)
- **Item #32:** Hot Mix Asphalt 19M64 Base Course, 6" Thick (1,885.85 TON)
- **Item #33:** Reset Existing Casting (7.00 UN)

Summary of Work Completed Period of January 19, 2024

- The 6" DGA base course has since been installed throughout the project limits, and the sub-contractor (South State Inc) has initiated paving with hot mix asphalt 19M64 base course, 6" thick along 27th Street between Federal Street and Marlton Pike. Asphalt was provided from South States Downer Plant per the approved submittals. The paving operation consisted of two 3" lifts, with a tack coat placement between layers. During the placement of asphalt, temperature checks were performed, and cross slope measurements were taken to ensure the paved roadway met the designed 2% cross slope. After the asphalt base course was installed, manholes throughout the project limits were reset to roadway grade to eliminate any uneven sections in the roadway. Police Traffic Directors, advanced warning signs, VMS boards, traffic control mounted crash trucks, breakaway barricades, and cones were utilized in setting up traffic control safety measures during this period of work.

Anticipated Work for Period of February 2, 2024


- The continuation of work on this project will be on hold for a few weeks of the winter months. Final asphalt surface course and traffic signal equipment is planned to be installed in the beginning of the spring season.

Notice to Proceed: September 5, 2023

Substantial Completion: February 11, 2024

Final Completion: March 2, 2024

Prepared By:


Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
