



**Camden County Haddonfield Berlin Road
 Intersection Improvements
 Weekly Progress Report #004
 From: Monday, June 10th to Friday, 14th,
 2024**

Contractor:	South State, Inc.
Design Engineer:	Environmental Resolutions, Inc.
Subcontractor:	Berenato
Notice to Proceed date (NTP)	
Contract Completion Date:	December 27, 2024
Original Contract Value:	\$1,216,507.00
Approved Amendment Value:	\$0.00
Current Contract Value:	\$1,216,507.00
Percentage Complete (Time):	14.47%
Percentage Complete (Cost):	
Time of Completion	120 Calendar days from the NTP for Substantial Completion and 150 days from the NPT for Completion of all work
	Liquidated Damages for failure to complete project on time (Per the Proposal, B: \$2,100.00 per day).

Contract Work for this Period

- Electrical Sub Berenato continued contract work for 3" RMC, 2" RMC and various Foundation work.
- Item 52 – Foundation, Type P-MC placed at STA 6+22, 57 FT Right
- Item 53 – Foundation, Type SPF placed at STA 7+05, 63 FT Right
- Item 53 – Foundation, Type SPF placed at STA 7+11, 52 FT Right
- Item 54 – Foundation, Type STF placed at 7+35, 47 FT Right
- Item 54 – Foundation, Type STF placed at STA 6+25, 61 FT Right
- Item 49 – 2" RMC, 10 FT used on (6/11/24)
- Item 49 – 2" RMC, 52 FT used on (6/13/24)
- Item 50 – 3" RMC, 14 FT used on (6/10/24)
- Item 50 – 3" RMC, 24 FT used on (6/11/24)
- Item 50 – 3" RMC, 28 FT used on (6/13/24)
- Item 50 – 3" RMC, 5 FT used on (6/14/24)



Pay Quantity this Period

Item No.	Item Description	Unit	Previous Qty Covered period June 2 nd to June 9 th , 2024		This Period Qty (June 10 th to 14 th , 2024)		Total Summary	
			Qty	Amount	Qty	Amount	Qty	Amount
50	3" Rigid Metallic Conduit	LF	0	0	71	\$6,160	71	\$6,160
53	Foundation, Type SPF	UNIT	0	0	2	\$5,600	2	\$5,600
54	Foundation, Type STF	UNIT	0	0	2	\$15,460	2	\$15,460
49	2" Rigid Metallic Conduit	LF	0	0	62	\$3,968	62	\$3,968
52	Foundation, Type P-MC	UNIT	0	0	1	\$5,520	1	\$5,520

Naik Personnel Time Utilization

Personnel	Title	Weekly Time Utilization					
		June 10, 2024	June 11, 2024	June 12, 2024	June 13, 2024	June 14, 2024	Total Hrs
Ankur Vaidya	Project Manager	0	0	0	0	0	0hrs
Sachin Patel	Resident Inspector	0	0	0	0	0	0hrs
Georgi Nakani	Electrical Inspector	8	8	4	8	8	36 hrs

Personnel	Title	Total Summary of Hours covered period: June 1st to June 14 th		
		Covered June 1 st to June 9 th	June 10 th to June 14 th	Total summary
Ankur Vaidya	Project Manager	0	0	0
Sachin Patel	Resident Inspector	0	0	0
Georgi Nakani	Electrical Inspector	0	36	36

Photos Reference A



Photo A-1 of 2
Date Taken: June 13, 2024. **Description:**
 Foundation Type P-MC, STA 6+22, 57'
 Right (P.S 11 OF 16 Electrical Plan)



Photo A-2 of 2,
Date Taken: June 13, 2024
Description: Foundation Type STF, STA
 6+25, 61' Right
 (P.S 11 OF 16 Electrical Plan)

Photo Reference B

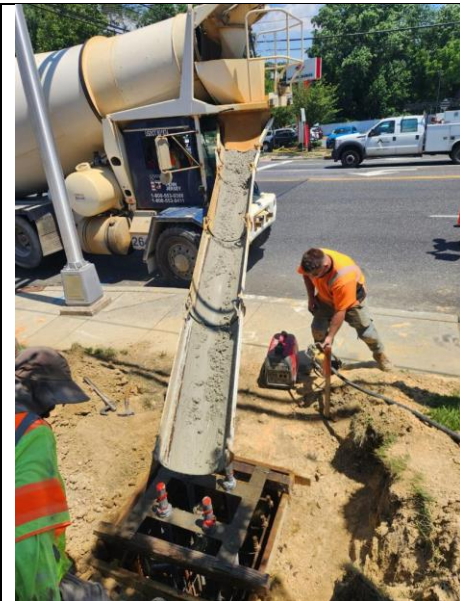


Photo B-1 of 2
Date Taken: June 14, 2024
Description: Foundation Type STF, STA
 7+35, 47' Right, Concrete being poured
 (P.S 11 OF 16 Electrical Plan)

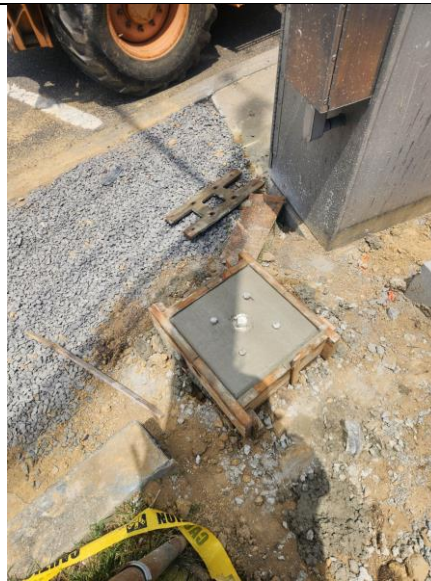


Photo B-2 of 2
Date Taken: June 14, 2024, **Description:**
 Foundation Type SPF, STA 7+05, 63' Right.
 (P.S 11 OF 16 Electrical Plan)

Photo Reference C

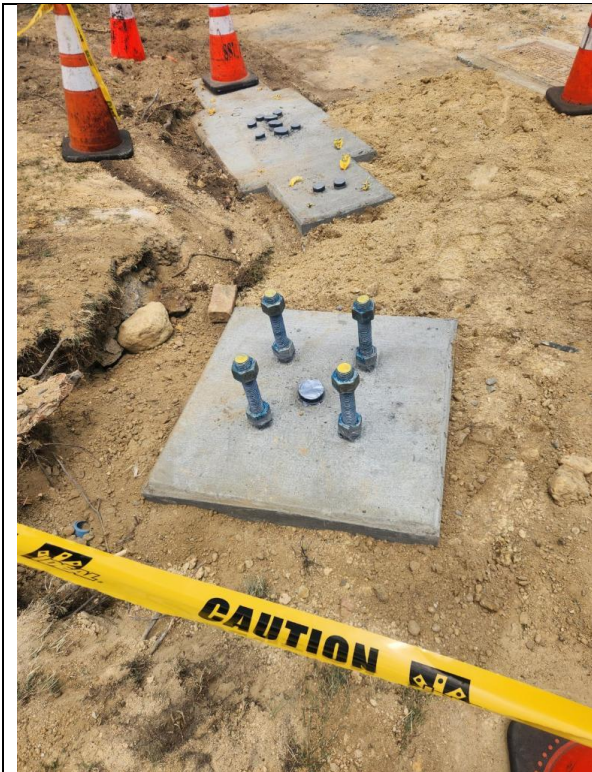


Photo C-1 of 1

Date Taken: June 14, 2024

Description: Foundation P-MC and STF
at STA 6+22 & STA 6+25

Formwork Removed (P.S 11 OF 16
Electrical Plan)

End of Photo Reference
