



**Camden County Haddonfield Berlin Road
 Intersection Improvements
 Weekly Progress Report #006
 From: Monday, June 24th to Friday, 28th, 2024**

Contractor:	South State, Inc.
Design Engineer:	Environmental Resolutions, Inc.
Subcontractor:	Berenato
Notice to Proceed date (NTP)	
Contract Completion Date:	December 27, 2024
Original Contract Value:	\$1,216,507.00
Approved Amendment Value:	\$0.00
Current Contract Value:	\$1,216,507.00
Percentage Complete (Time):	21.52%
Percentage Complete (Cost):	
Time of Completion	120 Calendar days from the NTP for Substantial Completion and 150 days from the NPT for Completion of all work
	Liquidated Damages for failure to complete project on time (Per the Proposal, B: \$2,100.00 per day).

Contract Work for this Period

- Electrical Subcontractors Diehl and Berenato performed various work activities which included the following:
- Item 48: Overhead Street Name Signs by STA 5+89 and STA 6+91
- Item 56: Ground wire, NO. 8 AWG – 800 LF
- Item 59: Generator Auxiliary Cabinet at STA 6+22
- Item 62: Traffic Signal Standard, Steel at STA 6+04, STA 7+07, STA 7+05, STA 7+11
- Item 63: Pedestrian Signal Standard at STA 6+04, STA 7+07, STA 7+05, STA 7+11
- Item 64: Traffic Signal Mast Arm, Steel at STA 5+89, STA 6+91
- Item 65: Traffic Signal Cable 2 Conductor – 1186 LF
- Item 66: Traffic Signal Cable 5 Conductor – 1186 LF
- Item 67: Traffic Signal Cable 10 Conductor – 1997 LF
- Item 68: Traffic Signal Heads at STA 5+89 and STA 6+91 (9) units total
- Item 73: Image Detector Cable 3 Conductor – 615 LF



Weekly Pay Quantity Update this Period for June 24th to 28th, 2024

Item No.	Item Description	Unit	This Period Qty (June 24 th to 28 th , 2024)	
			Qty	Amount
48	Overhead Street Name Signs	SF	30	\$1,560
56	Ground wire, NO. 8 AWG	LF	800	\$800
59	Generator Auxiliary Cabinet	Unit	1	\$5,720
62	Traffic Signal Standard, Steel	Unit	4	\$40,240
63	Pedestrian Signal Standard	Unit	4	\$3,150
64	Traffic Signal Mast Arm, Steel	Unit	2	\$17,400
65	Traffic Signal Cable 2 Conductor	LF	1186	\$1,589.24
66	Traffic Signal Cable 5 Conductor	LF	1186	\$2,372
67	Traffic Signal Cable 10 Conductor	LF	1997	\$7,388.9
68	Traffic Signal Heads	Unit	9	\$14,220
73	Image Detector Cable 3 Conductor	LF	615	\$1845



Pay Quantity Summary June 2nd to June 28th, 2024

Item No.	Item Description	Unit	Previous Qty Covered period June 2th to June 21st, 2024		This Period Qty (June 24 th to 28th, 2024)		Total Summary	
			Qty	Amount	Qty	Amount	Qty	Amount
48	Overhead Street Name Signs	SF			30	\$1560	30	\$1560
56	Ground wire, NO. 8 AWG	LF	0	0	800	\$800	800	\$800
59	Generator Auxiliary Cabinet	Unit	0	0	1	\$5720	1	\$5720
62	Traffic Signal Standard, Steel	Unit	0	0	4	\$40,240	4	\$40,240
63	Pedestrian Signal Standard	Unit	0	0	4	\$3150	4	\$3150
64	Traffic Signal Mast Arm, Steel	Unit	0	0	2	\$17,400	2	\$17,400
65	Traffic Signal Cable 2 Conductor	LF	0	0	1186	\$1589.24	1186	\$1589.24
66	Traffic Signal Cable 5 Conductor	LF	0	0	1186	\$2372	1186	\$2372
67	Traffic Signal Cable 10 Conductor	LF	0	0	1997	\$7,388.9	1997	\$7,388.9
68	Traffic Signal Heads	Unit	0	0	9	\$14,220	9	\$14,220
73	Image Detector Cable 3 Conductor	LF	0	0	615	\$1845	615	\$1845

Personnel	Title	Weekly Time Utilization					
		June 24, 2024	June 25, 2024	June 26, 2024	June 27, 2024	June 28, 2024	Total Hrs
Ankur Vaidya	Project Manager	0	0	0	0	0	0hrs
Sachin Patel	Resident Inspector	0	0	0	0	0	0hrs
Georgi Nakani	Electrical Inspector	8	8	8	8	0	32 hrs

Time Utilization for the period of June 1st to June 28th

Personnel	Title	Summary for the period				
		Covered June 1 st to June 9 th	June 10 th to June 14 th	June 17 th to June 21 st	June 24 th to June 28 th	Total summary
Ankur Vaidya	Project Manager	0	0	0	0	0
Sachin Patel	Resident Inspector	0	0	0	0	0
Georgi Nakani	Electrical Inspector	0	36	20	32	88

Photos Reference A

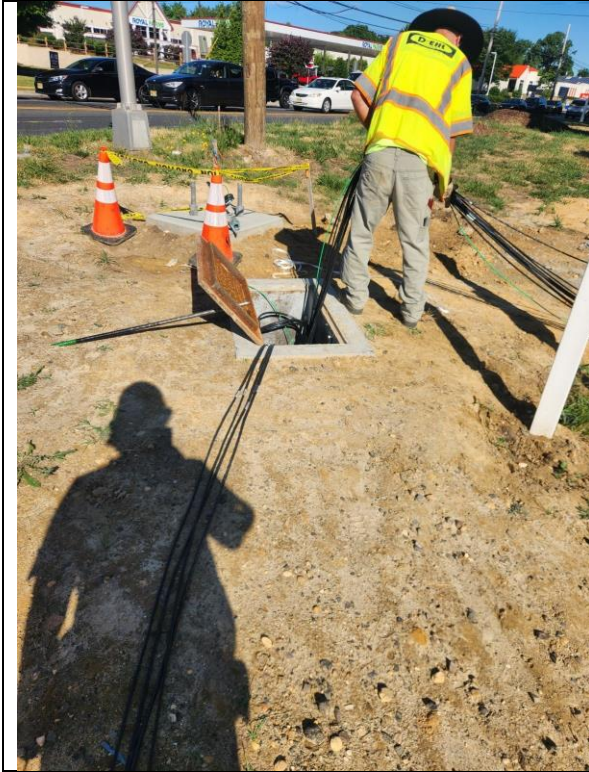


Photo A-1 of 2, Date Taken: June 24, 2024

Description: Pulling Various Cables from electric Junction Box to STF Foundation. (P.S 11 OF 16 Electrical Plan)



Photo A-2 of 2, Date Taken: June 24, 2024

Description: Cables being pulled (P.S 11 OF 16 Electrical Plan)

Photo Reference B



Photo B-1, of 2

Date Taken: June 25, 2024.



Description: Installation of Traffic Signal Standard, STA 5+89 (P.S 11 OF 16 Electrical Plan)

Photo B-2, of 2

Date Taken: June 25, 2024.

Description: Pedestrian Signal Installation at STA 7+07, (P.S 11 OF 16 Electrical Plan)

Photo Reference C

	
<p> Photo C-1 of 1 Date Taken: June 27, 2024 Description: Installation of Traffic Signal Mast Arm, STA 5+89 (P.S 11 OF 16 Electrical Plan) </p>	<p> Photo C-1 of 2, Date Taken: June 27, 2024 Description: Installation of Traffic Signal Mast Arm, STA 6+91 (P.S 11 OF 16 Electrical Plan) </p>
