



**Camden County Haddonfield Berlin Road
 Intersection Improvements
 Weekly Progress Report #007
 From: Monday, July 1st to Friday, 5th, 2024**

Contractor:	South State, Inc.
Design Engineer:	Environmental Resolutions, Inc.
Subcontractor:	Berenato
Notice to Proceed date (NTP)	
Contract Completion Date:	December 27, 2024
Original Contract Value:	\$1,216,507.00
Approved Amendment Value:	\$0.00
Current Contract Value:	\$1,216,507.00
Percentage Complete (Time):	23.41%
Percentage Complete (Cost):	
Time of Completion	120 Calendar days from the NTP for Substantial Completion and 150 days from the NPT for Completion of all work
	Liquidated Damages for failure to complete project on time (Per the Proposal, B: \$2,100.00 per day).

Contract Work for this Period

- Electrical Subcontractors Diehl and Berenato performed various work activities which included the following:
- Continue to connect Signal wires of Various STF and SPF foundations to respective Traffic and Pedestrian Signal Lights. (DIEHL)
- Berenato arrived on (7/3) to place gravel around STF foundations at STA 6+25 and STA 6+91 in order to stabilize the area around the foundations.



Naik Consulting Group, P.C
200 Metroplex Drive, Suite 403
Edison, NJ 08817
T: 732.777.0030
F: 732.777.0040
www.naikgroup.com

Weekly Pay Quantity Update this Period for July 1st to 5th, 2024

- N/A For this Period



Pay Quantity Summary June 2nd to July 5th, 2024

Item No.	Item Description	Unit	Previous Qty Covered period June 2th to June 21st, 2024		This Period Qty (June 24 th to 28th, 2024)		Total Summary	
			Qty	Amount	Qty	Amount	Qty	Amount
48	Overhead Street Name Signs	SF			30	\$1560	30	\$1560
56	Ground wire, NO. 8 AWG	LF	0	0	800	\$800	800	\$800
59	Generator Auxiliary Cabinet	Unit	0	0	1	\$5720	1	\$5720
62	Traffic Signal Standard, Steel	Unit	0	0	4	\$40,240	4	\$40,240
63	Pedestrian Signal Standard	Unit	0	0	4	\$3150	4	\$3150
64	Traffic Signal Mast Arm, Steel	Unit	0	0	2	\$17,400	2	\$17,400
65	Traffic Signal Cable 2 Conductor	LF	0	0	1186	\$1589.24	1186	\$1589.24
66	Traffic Signal Cable 5 Conductor	LF	0	0	1186	\$2372	1186	\$2372
67	Traffic Signal Cable 10 Conductor	LF	0	0	1997	\$7,388.9	1997	\$7,388.9
68	Traffic Signal Heads	Unit	0	0	9	\$14,220	9	\$14,220
73	Image Detector Cable 3 Conductor	LF	0	0	615	\$1845	615	\$1845

Personnel	Title	Weekly Time Utilization					
		July 1, 2024	July 2, 2024	July 3, 2024	July 4, 2024	July 5, 2024	Total Hrs
Ankur Vaidya	Project Manager	0	0	0	0	0	0hrs
Sachin Patel	Resident Inspector	0	4	0	0	0	4hrs
Georgi Nakani	Electrical Inspector	0	4	8	0	0	12 hrs

Time Utilization for the period of June 1st to June 28th

	Title	Covered June 1 st to June 9 th	June 10 th to June 14 th	June 17 th to June 21 st	June 24 th to June 28 th	July 1 st to July 5 th	Total summary
Ankur Vaidya	Project Manager	0	0	0	0	0	0
Sachin Patel	Resident Inspector	0	0	0	0	4	0
Georgi Nakani	Electrical Inspector	0	36	20	32	12	100

Photos Reference A



Photo A-1 of 1
Date Taken: July 2, 2024
Description: Stabilization
(P.S 11 OF 16 Electrical Plan, STA 6+25)



Photo A-2 of 2
Date Taken: July 2, 2024
Description: Prior to stabilization
(P.S 11 OF 16 Electrical Plan, STA 6+25)

Photo Reference B

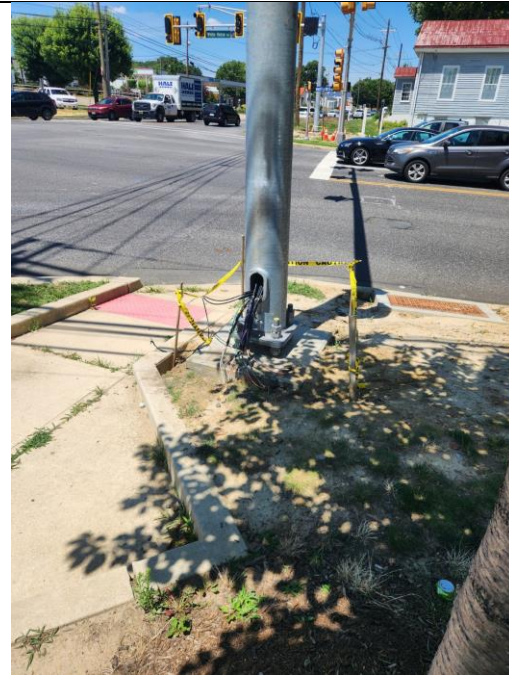
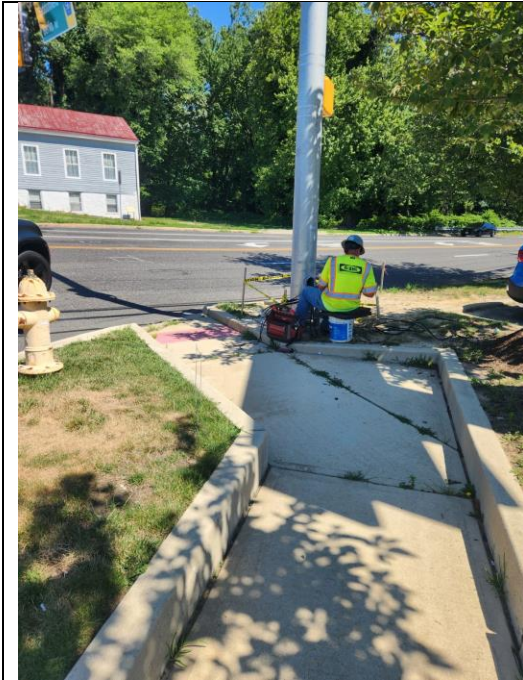


Photo B-1 of 1
Date Taken: July 2, 2024
Description: DIEHL continues signal cable work (P.S 11 OF 16 Electrical Plan)

Photo B-2 of 2
Date Taken: July 2, 2024
Description: DIEHL continues signal cable work) (P.S 11 OF 16 Electrical Plan)

End of Photo Reference
