

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

**Kaighn Avenue Dam – East Tide Gate
(NJDEP Dam #31-066)
*Bid No. B1-24***

*Township of Pennsauken and City of Camden
Camden County, New Jersey*

CED Project No. 230005437G2

***Progress Report #5
Monday, June 24, 2024 to Friday, July 5, 2024***



*Figure:1
Additional repair area on East Tide Gate.*

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

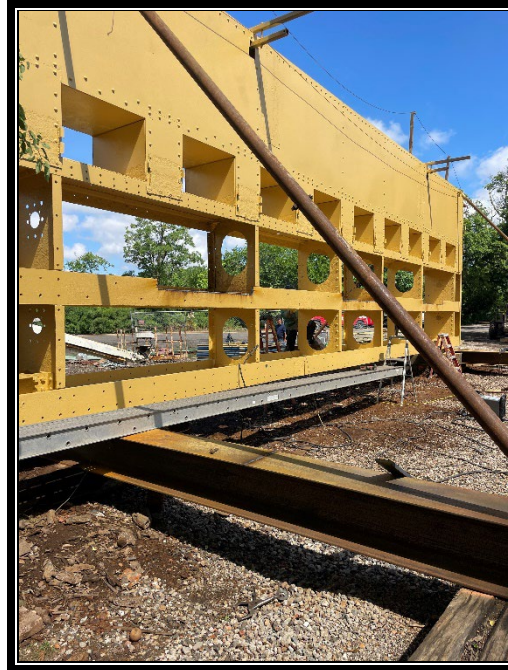


Figure 2: East Tide Gate primed.

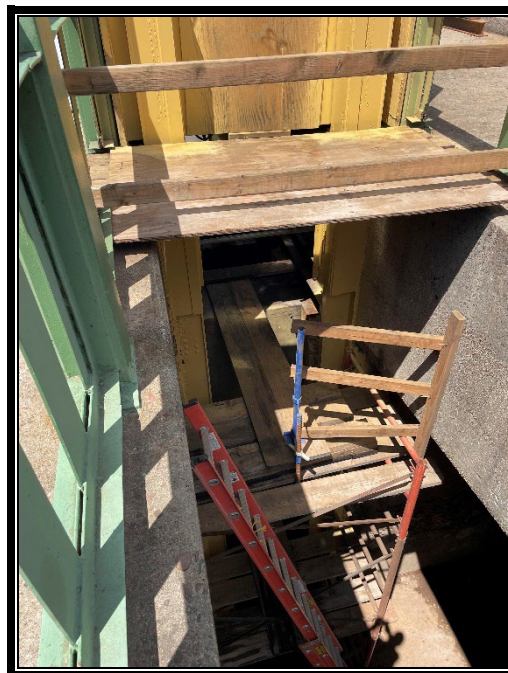


Figure 3: Primer applied to lifting structure.

Department of Public Works

Almar Dyer
Commissioner Liaison

Robert Harris
Director



Department of Public Works
Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
phone 856.566.2980
fax 856.566.2988
highway@camdencounty.com
CamdenCounty.com

- **Work Completed this week:**
 - Contractor continues dewatering.
 - Contractor continues repairs of east tide gate.
 - Contractor primed east tide gate and internal components of the dam.

- **Items completed this period:**
 - Item No. 11 – Cleaning of East Tide Gate
 - Item No. 12 – Existing Skin Plate Removal
 - Item No. 19 – Tide Gate Internal Diaphragm Replacement
 - Item No. 20 – Tide Gate Horizontal Member Reinforcement
 - Item No. 30 – Coating of East Tide Gate

- **Progress Next Two Weeks:**
 - Continue tide gate rehabilitation.

- **Next Progress Meeting:**
 - The next Progress Meeting has been rescheduled for Thursday, July 11, 2024 at 2:30 PM.
 - Bid Award Date: March 21, 2024
 - Notice to Proceed: April 29, 2024
 - Start Date: May 7, 2024
 - Substantial Completion Date: October 25, 2024
 - Stop Work: N/A
 - Amended NTP: N/A
 - Final Completion Date: November 14, 2024
 - Initial Award: \$ 2,026,422.00

Prepared by: Vincent Baglivo, PE
Project Manager
Colliers Engineering & Design

James Winckowski, PE, County Engineer
