



**Mill and Overlay of Westfield Avenue (CR 610) from Tinsman Avenue (MP 1.57) TO NJ Route 130 (MP 2.92)  
Pennsauken Township, Camden County, New Jersey**

**Notice to Proceed issued: August 30, 2019**  
**Project Completion: August 12, 2020**  
**Project Substantial Completion: July 13, 2020.**  
**Project start: September 4, 2019.**

**Weekly Progress Report**  
**04-27-2020 – 05-01-2020**

**Following Construction Activities took place during above period:**

**Concrete Curb and Sidewalk:**

- a. East and West Concrete curb and sidewalks, and driveway were constructed along Westfield Avenue, RT at following locations.
  - 1) West concrete sidewalk along Marlon Avenue.
  - 2) West concrete curb, sidewalk, and handicap ramp along Cove Road.
  - 3) Concrete driveway along Westfield Avenue STA 93+00 – 93+50, 23' RT.
  - 4) Header curbs between proposed sidewalk and existing brick pavers at Lexington Avenue - West Merchantville Avenue – West, Gross Avenue – West, Horner Avenue – West, Scovel Avenue –

**Topsoil and Seeding:**

- a. Topsoil and seeding were performed along concrete sidewalk and HC Ramps at following locations along Westfield Avenue, RT.
  - 1) East and West sidewalk and HC Ramps at Marlon Avenue.

**Brick pavers:**

- a. Existing brick pavers were reset along proposed East and West sidewalk and existing brick pavers and between header curb and existing brick pavers along Westfield Avenue, RT.
  - 1) At Lexington Avenue, Merchantville Avenue, Gross Avenue, Hollinshead Avenue, Horner Avenue, and Penn street.

**Two Week Look Ahead:**

- a. Construction of concrete curb and sidewalk started from March 24, 2020 and will be under progress for next two weeks. – South State Inc.
- b. Construction of Concrete gutters.

Prepared by:  
Gunvant Mistry  
Resident Engineer



Figure 1: Concrete driveway 6" thick along Westfield Avenue STA 93+00-93+50, RT, and West sidewalk at Marlon Avenue, RT



Figure 2: West concrete curb, sidewalk and HC Ramp at Cove Road, RT



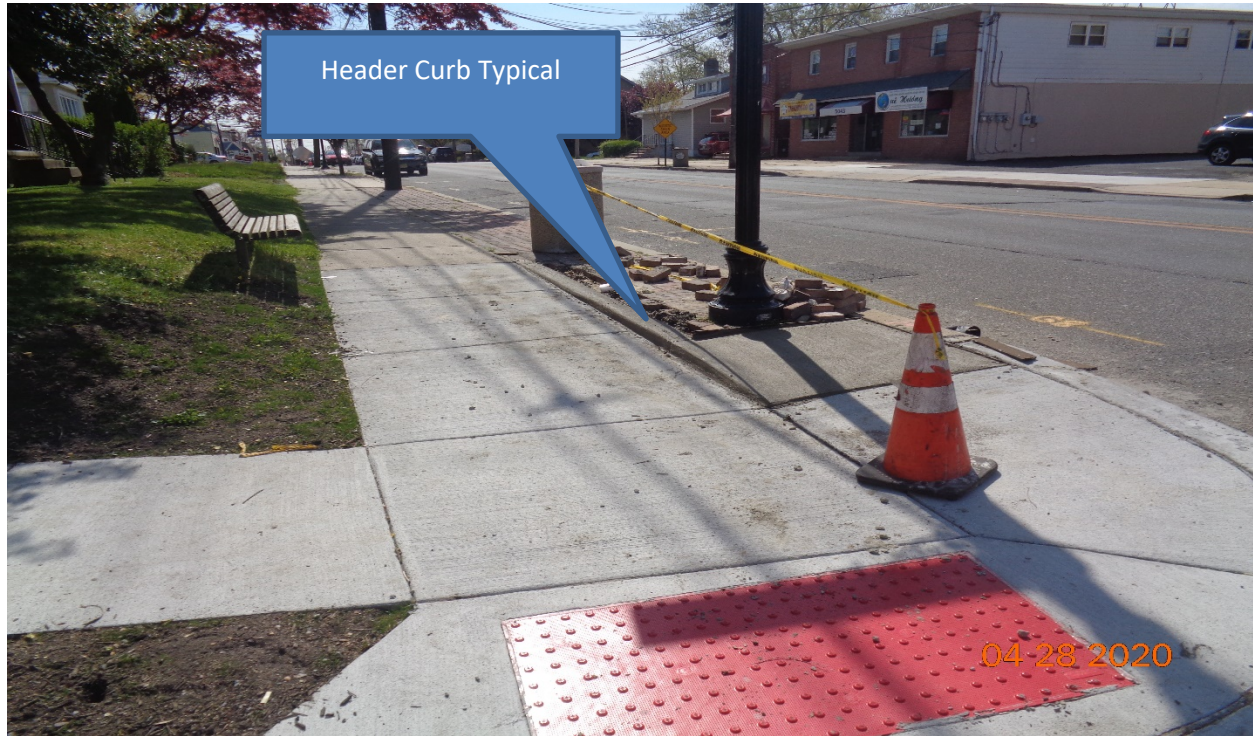


Figure 3: Hader Curb along Lexington Avenue West, RT



Figure 4: Hader Curb along Gross Avenue West, RT





Figure 5: Hader Curb along Scovel Avenue East, RT



Figure 6: Hader Curb along Penn Street, East, RT





Figure 7: Hader Curb along Horner Avenue East, RT



Figure 8: Topsoil and seeding along East sidewalk at Marlon Avenue, RT





Figure 9: Topsoil and seeding along West sidewalk at Marlon Avenue, RT, And DGA along edges of driveway



Figure 10: Resetting existing brick pavers along proposed sidewalk and existing brick pavers





Figure 11: Resetting existing brick pavers along proposed sidewalk and existing brick pavers



Figure 12: Resetting existing brick pavers along proposed sidewalk and existing brick pavers
