

**Camden County Department of Public Works
Division of Engineering
Roadway and Drainage Improvements Evesham Road
Runnemedede Borough, Magnolia Borough and
Gloucester Township, Camden County, New Jersey
Contract B22-21 Hartford to Charles
Progress Report No. 20
October 24, 2022 to October 28, 2022**



Figure 1: Curb forms

Work Completed Period of October 28, 2022

- Removed existing asphalt, concrete curbs, and aprons.
- Installed curb forms and completed concrete curb, gutter curb, and apron installation.
- Filled in area behind new curb with topsoil.
- Temporary repairs to potholes and ditches where asphalt patches settled.



Figure 2: Removal of asphalt, curb, and aprons

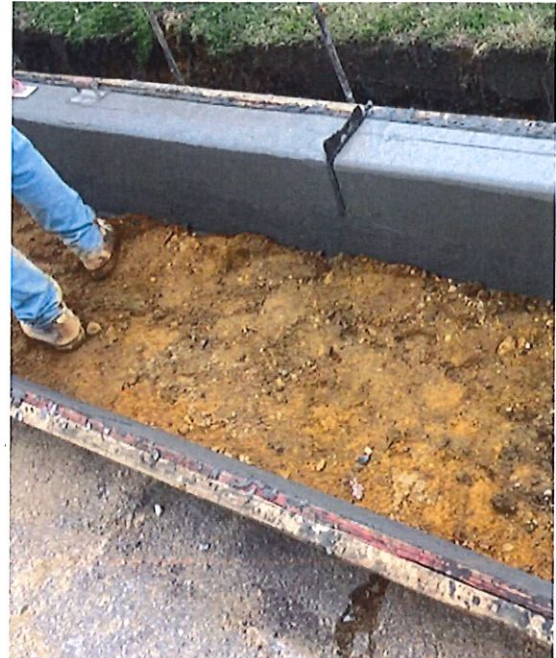


Figure 3: Concrete curb placement



Figure 4: Concrete apron placement

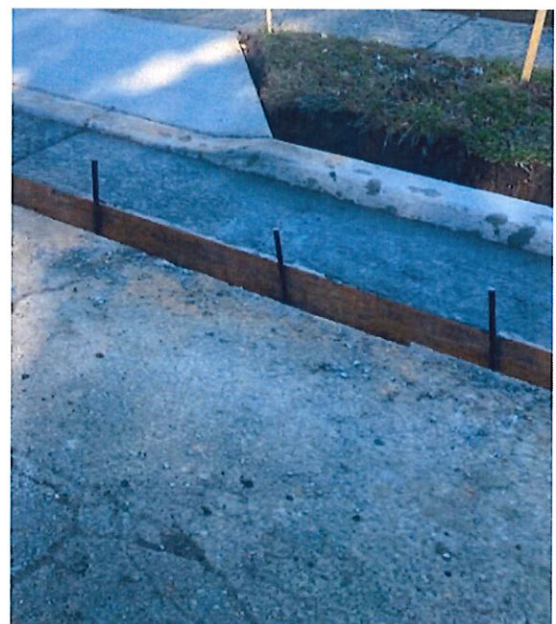


Figure 5: Gutter curb placement

Quantities Period of October 28, 2022

- **Item #27:** Hot Mix Asphalt 19M64 Base Course (Trench Restoration) (50 TON)
- **Item #67:** Concrete Driveway, Reinforced, 6" Thick (97.49 SY)
- **Item #71:** 9" X 16" Concrete vertical curb (80 LF)
- **Item #72:** Concrete Curb and Gutter (556 LF)

Summary of Work Completed Period of October 28, 2022

The contractor began with removing asphalt, concrete curbs, and aprons. The crew then placed curb and apron forms and placed concrete curbs, aprons, and gutter curbs. Completed filling in potholes and trenches in the roadway where the asphalt patches settled. Filled in the area behind new curbs with topsoil.

Anticipated Work for Period of October 31, 2022


- Continue with concrete work.

Notice to Proceed: May 16, 2022

Substantial Completion: November 12, 2022

Final Completion: December 12, 2022

Prepared By:



Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
