

**Camden County Department of Public Works  
Division of Engineering  
Roadway Improvements along Blackwood Clementon Road  
Gloucester Township, Camden County, New Jersey  
Progress Report No. 13  
October 31, 2022 to November 4, 2022**



*Figure 1: Milled surface*

**Work Completed Period of November 4, 2022**

- Reconstructed B inlet for mill and overlay.
- Adjusted existing push buttons and installed new push buttons for pedestrian cross walks.
- Manhole castings reset, HMA installed adjacent to the manholes.
- HMA milling and surface course placement.



Figure 2: Casting reset

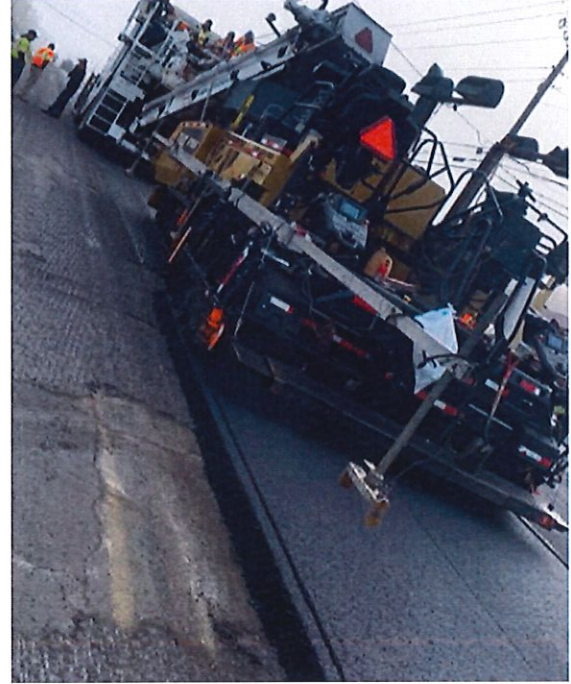


Figure 3: Paving



Figure 4: Reconstruction of B inlet



Figure 5: New push button installed



**Quantities Period of November 4, 2022**

- **Item #8:** Traffic Safety Services (128 MH)
- **Item #13:** HMA Surface Course, 12.5 M 64, 2" Thick (2079.84 TON)
- **Item #15:** HMA Milling, 3" or Less, 2" Thick (16,722.22 SY)
- **Item #20:** Reset Existing Casting (9 Unit)
- **Item #23:** Reconstruct Inlet, Type B Using New Casting (1 Unit)
- **Item #40:** Pedestrian Push Button (9 Unit)

**Summary of Work Completed Period of November 4, 2022**

- Verizon sub-contractor removed existing asphalt adjacent to six Verizon manholes then used brick and mortar to set castings to existing grade. HMA was installed adjacent to the manholes. The crew excavated a small patch in new HMA apron at the Fire Department and installed a new clean out for sewer repair. Contractor continued with adjusting existing push buttons and installing new push buttons on site. The crew began HMA milling and surface course placement.

**Anticipated Work for Period of November 7, 2022**

- Continue with milling and paving.

**Notice to Proceed:** August 1, 2022

**Substantial Completion:** October 30, 2022

**Final Completion:** November 29, 2022

**Prepared By:**



Joseph R. Ragusa, P.E.

Remington & Vernick Engineers
