



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report #4

Monday, August 27, 2018 to Friday, August 31, 2018



Figure 1: New curb and sidewalk at south end of project.

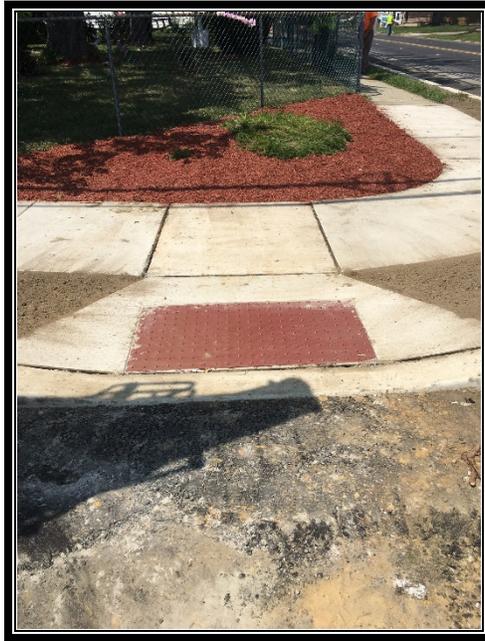


Figure 2: Completed HC ramp at Preston Avenue.



Figure 3: Sidewalk and gutter being completed in from of the "Wick" .



Making It Better, Together.



Work Completed this week:

APS, Inc. continued to pour concrete curb, gutter and HC ramps at various location on the project south of Wood Avenue. Completed sidewalk on west side of roadway to south end of project, also backfilled, topsoiled and seeded the same areas. All sidewalks in front of the Highschool from Preston to the south end of the project are completed. APS began working on the east side of the roadway, starting at Preston Avenue installing curb and sidewalk. Restored base asphalt in front of new curb; and installed asphalt driveways at locations where sidewalk was completed.

Items completed this week:

#02:	Police Traffic Directors	192 MHS
#08:	HMA, 9.5M64, Surface Course 2" TH	7 TONS
#09:	HMA, 19M64, Base Course 3" TH	50 TONS
#21:	Concrete Sidewalk, 4" TH	250 SY
#22:	Concrete Driveway, 6" TH	80 SY
#24:	9" x 18" Concrete Vertical Curb	200 LF
#46:	Topsoiling, 5" TH	200 SY

• **PROGRESS NEXT TWO (2) WEEKS**

- APS will continue to pour concrete curb, sidewalk, HC ramps and driveway aprons on the east side of Warwick Road from Preston Avenue to Fox Ridge Drive. Areas in front of the new curb will be restored with asphalt and behind the curb backfilled and topsoiled and asphalt driveways installed.
- APS will continue working new work hours, 8:00 AM to 4:00 PM.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Friday, September 14, 2018 at 9:00 AM.

Department of Public Works

Susan Shin-Angulo
Freeholder Liaison

John Wolick
Director



Making It Better, Together.

Charles J. DePalma Complex
2311 Egg Harbor Road
Lindenwold, NJ 08021
Phone 856.566.2980
Fax 856.566.2988
highway@camdencounty.com



Notice to Proceed Date:

August 6, 2018

Anticipated Completion Date:

November 4, 2018

Prepared by:

Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS
