



**IMPROVEMENTS TO WARWICK ROAD (CR669)
BETWEEN SOMERDALE ROAD (CR667) AND FOX RIDGE DRIVE (A.K.A. OLD WARWICK
ROAD)**

*Boroughs of Somerdale, Hi-Nella and Stratford
Camden County
Bid No. B8-18*

MC Project No. 17006851G

Progress Report # 14 Final

Monday, November 5, 2018 to Friday, November 30, 2018



Figure 1: Final milling of the project.

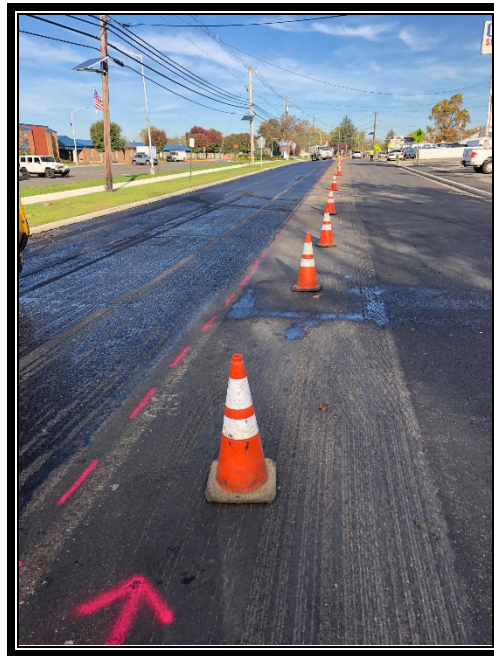


Figure 2: Preparing for final surface paving of Warwick Road.



Figure 3: Completed pavement surface of Warwick Road in front of the Highschool.



Figure 4: Completed pavement of Warwick Road.



Figure 5: Final striping of Warwick Road.



Work Completed this period:

APS, Inc. worked intermittently during this period to complete the project. Work was completed during periods of favorable weather conditions. The asphalt base repairs were completed, and the entire project was milled and paved. The final traffic stripes were applied, and all final traffic signs installed.

Items completed this week:

#02: Police Traffic Directors	254 MHS
#07: HMA Milling, 4"-6"	4046 SY
#08: HMA, 9.5M64, Surface Course 2" TH	1800 TONS
#28: Traffic Stripes, Epoxy Resin, 4" TH	12909 LF
#31: Traffic Markings, Thermoplastic	500 SF
#32: Raised Pavement Markers	177 UN

- **PROGRESS NEXT TWO (2) WEEKS**

- The project has been completed.

Notice to Proceed Date: August 6, 2018

Contract Completion Date November 30, 2018

Anticipated Completion Date: November 27, 2018

Prepared by: Vincent E. Baglivo
Maser Consulting

Anthony O'Toole, Project Engineer
Kevin Becica, PE, County Engineer
John Wolick, Director CCDPW
Don Potter, APS
