



ROAD IMPROVEMENT PROJECT GOOD INTENT – LOWER LANDING ROAD (CR 681)

Federal Project #: STPGP-0681 (304) NJDOT Project #: 5815302

ERI Job #: 30750 65

Township of Gloucester

County of Camden, New Jersey

WEEKLY PROGRESS REPORT #11

August 30, 2021 to September 3, 2021

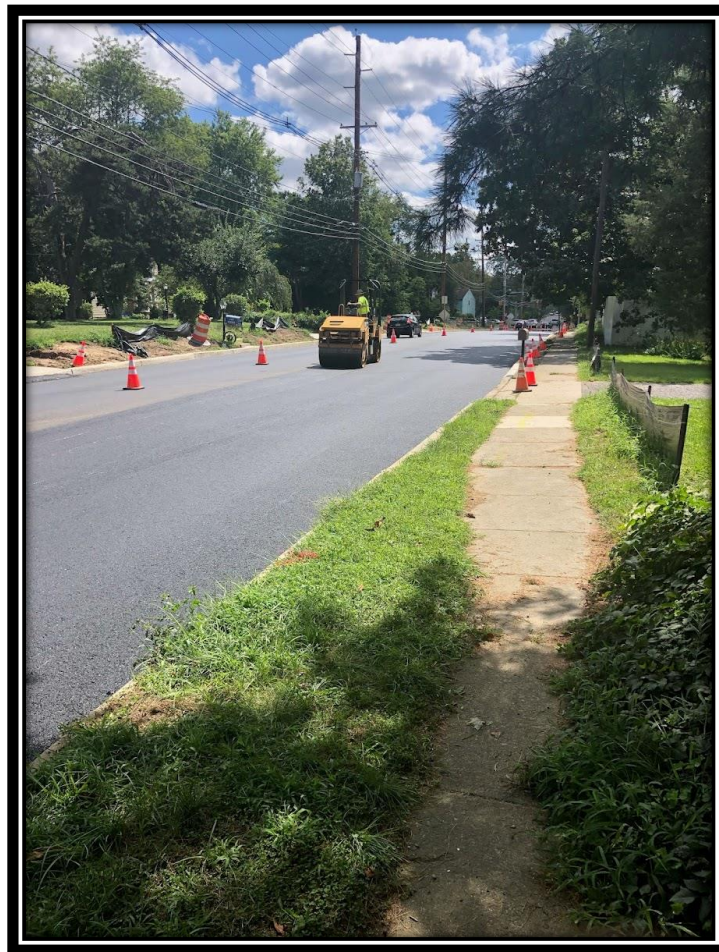


Figure: 1 – APS installed HMA 19M64 base course from Oak Ave to Almonesson intersection.



Figure: 2 – APS concrete crew setting forms for gutters by drilling dowels into concrete vertical curb and pouring concrete.

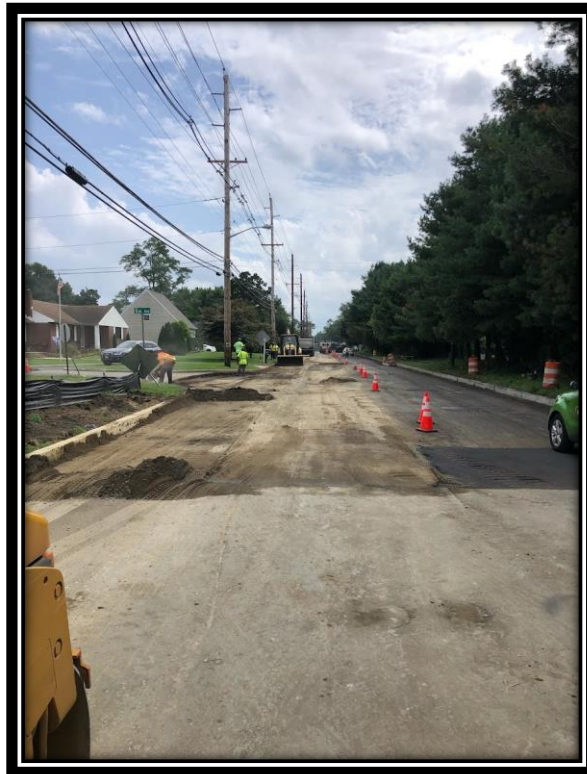


Figure: 3 – Repair area from water main breakage at STA 43+0.

Work Completed the Week of August 30, 2021:

APS concrete crew poured concrete for aprons, curbs, sidewalks and gutters along Lower Landing Road. All aprons were reinforced with welded wire and gutters were doweled from curb to gutter. All curbs, gutters, aprons and sidewalks were backfilled and compacted with DGA and restored with asphalt. Work completed this week was on both sides of the road along the Northbound Lane of Lower Landing Road on the Southside of the Almonesson/Lower Landing Intersection. No roads were closed but a lane shift was implemented during working hours to ensure the safety of the workers.

APS FDR crew performed full depth reclamation with cement from STA 43+0 to 44+50 both sides of the road (36') to repair the water main break and finish FDR to contract limits on the Northside of Almonesson Road. APS also installed HMA 19M64 base course of asphalt STA 43+0 – 51+50. APS also reset existing manhole castings at STA 43+59 Lt, 46+65 Lt and 49+72 Lt. At the end of each day, they tacked the surface of the road with fog seal to prevent dust spreading from traffic driving over it.

- #12: Police – Uniform Law Enforcement Officer – 82 MH
- #14: Hot Mix Asphalt, Full Depth Reclamation, Cement – 644.4 SY
- #15: Hot Mix Asphalt, Full Depth Repair – 55.1 SY
- #17: Hot Mix Asphalt, 19M64, Base Course – 631.27 Tons
- #26: Reset Existing Casting (Manhole/Utility/Inlet) – 3 units
- #32: Concrete Sidewalk, 4” Thick – 3.3 SY
- #34: Concrete Driveway, Reinforced, 6” Thick – 65 SY
- #36: 9” x 16” Concrete Vertical Curb – 700 LF
- #36.1: 9” x 16” Concrete Monolithic Curb and Gutter – 126 LF

Anticipated Work for the Week of September 6, 2021:

APS concrete crew will continue along the Northbound Lane of Lower Landing Road on the Southside of Almonesson Road working towards the bridge at the county line. APS’s subcontractor, Clean Earth Matters, will begin to work on restoration along Lower Landing Road. APS FDR and paving crew will continue behind the concrete crew moving towards the bridge with pulverizing, milling, grading and paving.

Notice to Proceed Date: June 1, 2021

Amended NTP: N/A

Anticipated Completion Date: December 28, 2021

Initial Award: March 18, 2021

Contract Completion Date: January 27, 2022

Contract Completion Percentage: 51.00%

Prepared By:



Bid Opening Date: February 9, 2021

Start Date: June 1, 2021

C. Jeremy Noll, PE, CME, CPWM
Resident Engineer
Environmental Resolutions, Inc.

Stop Work: N/A
