



**HAMPTON ROAD (CR 623)  
ROADWAY IMPROVEMENT PROJECT  
CUTHBERT BOULEVARD (CR 636) TO CHAPEL AVENUE (CR 626)  
ERI Job # 30750 49  
Township of Cherry Hill  
County of Camden, New Jersey**


**WEEKLY PROGRESS REPORT #5  
April 22, 2019 to April 26, 2019**



*Figure: 1 – Reconstruction of storm sewer manhole and replacement of double ‘B’ castings along the northbound lane approaching Cuthbert Boulevard*



*Figure: 2 – Directional drilling of 4” SDR 11 HDPE sanitary sewer force main*

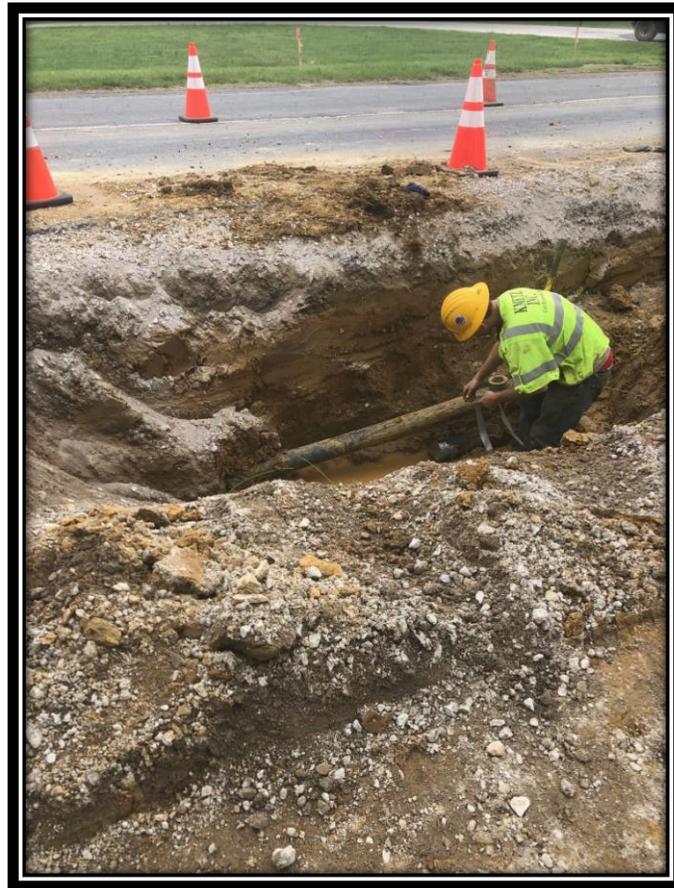

*Figure: 3 – Pressure testing of newly installed sanitary sewer force main*

**Work Completed the Week of April 22, 2019:**

R.E. Pierson's pipe crew continued work on the proposed drainage improvements. The pipe crew reconstructed one double inlet with a new casting and also reconstructed a storm sewer manhole. The pipe crew also removed 3 24" to 36" diameter trees and 2 trees with diameters greater than 36". Pierson's force main subcontractor completed the main line installation of the sanitary force main. They directionally drilled 950 linear of 4" SDR 11 HDPE sanitary sewer force main, installed 1 4" terminating gate valve, and conducted a pressure test on the 1,425 linear feet of newly installed force main. Pierson's pipe crew also dug 18.1 cubic yards of test pits for their subcontractor to verify the location of existing utilities.

- #2: Police Uniform Law Enforcement Officer – 80 Hours**
- #32: Reconstruct Manhole – 1 Unit**
- #55: Tree Removal, 24" to 36" Diameter – 3 Units**
- #56: Tree Removal, over 36" Diameter – 2 Units**
- #M20: Excavation, Test Pit – 18.1 CY**
- #M22: 4" SDR 11 HDPE Thick – 950 LF**
- #M26: 4" Terminating Gate Valve – 1 Unit**
- #M27: Final Testing – 1,425 LF**

**Anticipated Work for the Week of April 29, 2019:**

R.E. Pierson's pipe crew will continue installation of the proposed drainage improvements. Pierson's force main subcontractor will complete the final connection of the newly installed force main into the existing sanitary collection system. Pierson's concrete subcontractor will mobilize to the site and begin concrete improvements starting at the intersection with Chapel Avenue.

**Notice to Proceed Date: April 1, 2019**

**Anticipated Completion Date: June 14, 2019**

Prepared By:



C. Jeremy Noll, PE, CME, CPWM  
Resident Engineer  
Environmental Resolutions, Inc.
