Susan Shin-Angulo Freeholder Liaison

John Wolick Director



Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 Phone 856.566.2980 Fax 856.566.2988 highway@camdencounty.com

East Atlantic Avenue (C.R. 729) over Nicholson Road (C.R. 635) Bridge Replacement Project

Borough of Audubon County of Camden, New Jersey Weekly Progress Report Sunday 10/22/2017 thru Friday 10/27/2017

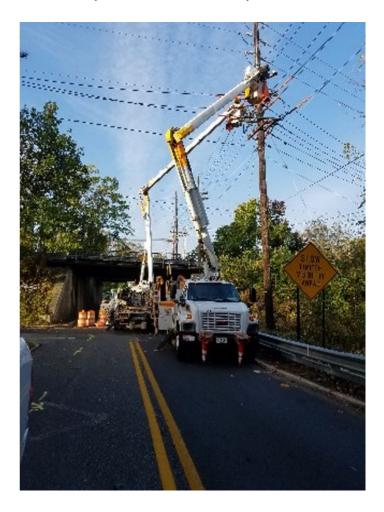


Figure 1
PSE&G transferring wires to new poles

Susan Shin-Angulo Freeholder Liaison

John Wolick Director



JOHNSON, MIRMIRAN & THOMPSON
Engineering A Brighter Future®

Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 Phone 856.566.2980 Fax 856.566.2988 highway@camdencounty.com



Figure 2

Clearing site – Subcontractor Bergholz Tree Service for tree removal

Susan Shin-Angulo Freeholder Liaison

John Wolick Director Charles J. DePalma Complex 2311 Egg Harbor Road Lindenwold, NJ 08021 Phone 856.566.2980 Fax 856.566.2988 highway@camdencounty.com



Figure 3

Clearing site – Subcontractor Bergholz Tree Service for tree removal

Susan Shin-Angulo Freeholder Liaison

John Wolick Director



Lindenwold, NJ 08021 Phone 856.566.2980 highway@camdencounty.com

Charles J. DePalma Complex 2311 Egg Harbor Road

Fax 856.566.2988



The following Construction Activities took place during the period stated above.

PSE&G

PSE&G completed work on Wednesday, October 25, 2017. Wires have been transferred to new poles, old poles have been removed, and old wires have been de-energized and decommissioned.

Vibration Monitoring

SSI, R.E. Pierson's sub-contractor, installed Vibration Monitoring on the Conrail bridge on Tuesday, October 24, 2017.

Clearing Site

R.E. Pierson on site for clearing site activities on Thursday, October 26, 2017. Subcontractor Bergholz Tree Service was on site removing six (6) trees through the course of the day.

Soil Erosion and Sediment Control

R.E. Pierson on site to install silt fence and inlet sacks. A total of 530 LF of Silt Fence and 5 U of Inlet Sacks installed prior to Clearing Site activities.

Traffic Safety

The contractor maintained a safe construction area and flow of traffic by using a (2) lane undivided, lane and shoulder closure w/ flaggers as needed.

Anticipated Work for the 10/30/17 thru 11/03/17

Bridge deck and beam demolition, A full 5-week closure is expected to last through Tuesday, November 28, 2017.

Notice to Proceed: 09/28/17 **Anticipated Completion Date: 11/20/18**

Prepared By: Alfred Brenner

Resident Engineer
