

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director

camden **county**

Making It Better, Together.



An Employee Owned Company

Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

[highway@camdencounty.com](mailto:highway@camdencounty.com)

**East Atlantic Avenue (C.R. 729)  
over Nicholson Road (C.R. 635)  
Bridge Replacement Project**

*Borough of Audubon  
County of Camden, New Jersey  
Weekly Progress Report  
Tuesday 01/02/2018 thru Friday 01/05/2018*



**Figure 1**  
*RE Pierson hoerammng South Abutment*

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director



Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988

[highway@camdencounty.com](mailto:highway@camdencounty.com)



**Figure 2**


*Contractor loading concrete debris from North Abutment*

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director

Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)

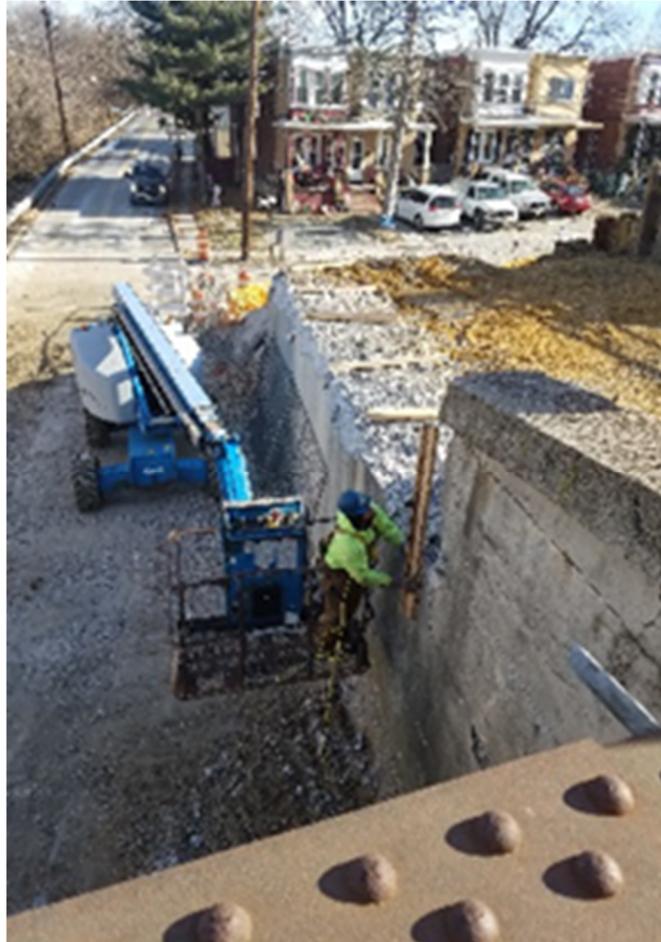

**Figure 3**

*Dockbuilder installing safety railing at South Abutment*

Department of Public Works

Susan Shin-Angulo  
Freeholder Liaison

John Wolick  
Director



Making It Better, Together.



Charles J. DePalma Complex  
2311 Egg Harbor Road  
Lindenwold, NJ 08021  
Phone 856.566.2980  
Fax 856.566.2988  
[highway@camdencounty.com](mailto:highway@camdencounty.com)

**The following Construction Activities took place during the period stated above.**

### **Demolition**

On Tuesday, January 2, 2018, RE Pierson performed demolition of the top sections of the North and South Abutments by hoerammimg concrete to soil grade line. Concrete debris from both the North and South Abutments was hauled away. Asphalt roadway pavement at the South side of Nicholson Road was removed for the preparation of the installation of temporary sheeting.

### **Rebar Cages**

Ironworkers continued fabricating rebar cages for pipe piles.

### **Weather**

Due to the inclement weather, the RE Pierson did not work on Thursday, January 4, 2018 or Friday, January 5, 2018. Helacol Anchor Company (tieback subcontractor) mobilized equipment on site on Friday, January 5, 2018.

### **Anticipated Work for 1/8/18 thru 1/12/19**

The installation of the temporary sheeting is slated to continue. Tiebacks will be installed on both the North and South Abutments. Additionally, excavation of regulated material will continue.

**Notice to Proceed:** 09/28/17

**Anticipated Completion Date:** 11/20/18

**Prepared By:** Alfred Brenner  
Resident Engineer
