

**Camden County Department of Public Works
Division of Engineering
Roadway & Drainage Improvements along Fern Avenue (CR 640)
Haddon Ave (CR 561) to Cuthbert Boulevard (CR 636)
Camden County, New Jersey
Weekly Progress Report No. 9
June 17, 2019 to June 23, 2019**



Figure 1: Milling along Fern Ave

Work Completed Week of June 17, 2019

- Installed concrete sidewalk, vertical curb, and curb ramps
- Milled between Cuthbert Boulevard and Haddon Ave
- Pipework at Haddon Ave intersection

Quantities Week of June 17, 2019

- **Item #7:** Police Uniform Law Enforcement Officer (104 MH)
- **Item #11:** HMA Milling, 3" or less (6225.11 SY)
- **Item #12:** Base Repair (If & Where Directed) (4.78 SY)
- **Item #18:** Hot Mix Asphalt 9.5M64 Surface Course, 2" Thick (12.73 TON)
- **Item #26:** 16" Ductile Iron Pipe, Class 53 (42 LF)
- **Item #49:** Concrete Sidewalk, 4" Thick (71.99 SY)
- **Item #50:** 9"x18" Concrete Vertical Curb (63 LF)
- **Item #51:** Public Sidewalk Curb Ramp Detectable Warnings, PVC Truncated Domes (48 SF)

Summary of Work Completed Week of June 17, 2019

Asphalt Paving Systems (APS) continued demolition of existing concrete and installation of new concrete vertical curb, sidewalk, and curb ramps moving up station towards Haddon Ave. The pipework at the intersection of Haddon Ave and Fern Ave was completed. The contractor milled the roadway between Cuthbert Boulevard and Fern Ave throughout the week in preparation for paving operations. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control.

Anticipated Work for Week of June 24, 2019

APS will start paving operations as specified per plans and continue with the restoration of Fern Ave. Daily traffic control will continue to be implemented for the duration of the project. An onsite progress meeting will be held on June 25, 2019 to review all project related activities.



Figure 2: Concrete slab demolition

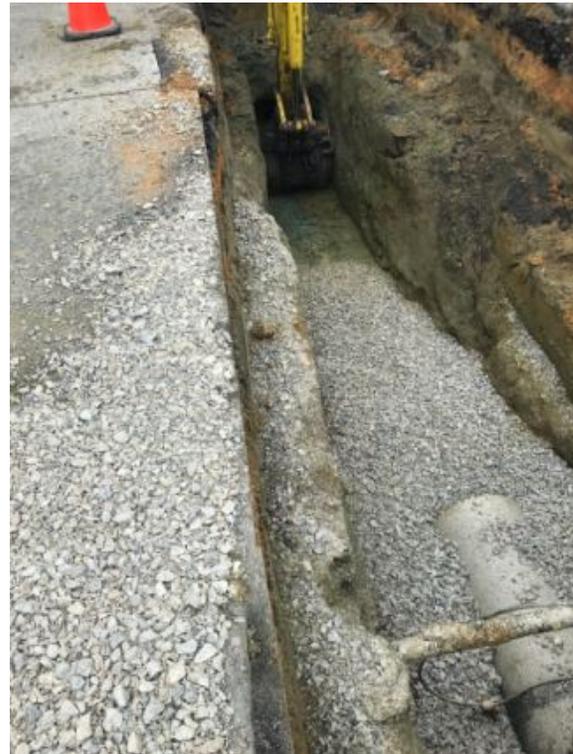


Figure 3: Pipework at Haddon Ave



Figure 4: Milling and Grading Operations



Figure 5: Concrete curb ramp sidewalk

Notice to Proceed

April 22, 2019

Contract Completion

Substantial Completion

July 21, 2019

Final Completion

August 20, 2019

Prepared By:

Handwritten signature of Joseph R. Ragusa in blue ink.

Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
