



**Improvements to Avondale Avenue (CR646) from Hopkins Road to Woodland Ave.
and Improvements to Breslin Avenue from Graisbury Avenue to Avondale Avenue**

*Township of Haddon
Camden County
Bid No. B2-19*

MC Project No. 19000074G

Progress Report # 8

Monday, July 8, 2019 to Saturday, July 13, 2019



Figure 1: Completed curb, gutter and new inlets on Avondale Avenue.



Figure 2: New concrete sidewalk and handicap ramps at Avondale & Foreman Avenues.



Figure 3: New sidewalk at Avondale & Foreman Avenues.



Work Completed this week:

Charles Marandino Concrete continues installing monolithic curb, gutter and sidewalk on Avondale Avenue from Woodland Avenue to Crystal Lake Avenue. The contractor has also continued to pour driveways and handicap ramps. The areas behind the new curb were restored with topsoil. The contractor continued to reconstruct the inlets near Woodland Avenue. These two blocks were closed to traffic during the daytime. A short detour around the block was be posted. Access to homeowners was be maintained. There was no work performed over the July 4th holiday.

Items completed this week:

#2:	Police Traffic Directors	98 HOURS
#15:	Inlet, Type 'B'	2 UN
#22:	Concrete Sidewalk, 4" Thick	159 SY
#23:	Concrete Driveway, 6" Thick	78 SY
#25:	Detectable Warning Surface	7 SY
#27:	Monolithic Concrete Curb and Gutter	1609 LF

• PROGRESS NEXT TWO (2) WEEKS


- Charles Marandino Concrete will continue working on Avondale Avenue between Crystal Lake Avenue and Woodland Avenue. He will continue to install curb, gutter, driveways and handicap ramps in two block increments. These two blocks will be closed during the work day.
- The contractor plans to replace the concrete roadway at the intersection of Avondale and Crystal Lake Avenues. A detour will be posted. (copy attached)
- All areas behind the curb will be backfilled and topsoiled.
- The contractor will continue to work 7:00 AM to 4:30 PM.
- The contractor may also work on selected Saturdays.

• NEXT MEETING

- Next Progress Meeting is scheduled for Tuesday, July 23, 2019 at 10:00 AM.

<u>Notice to Proceed Date:</u>	May 13, 2019
<u>Contract Completion Date:</u>	August 11, 2019
<u>Anticipated Completion Date:</u>	August 11, 2019

Prepared by: Vincent E. Baglivo
Maser Consulting

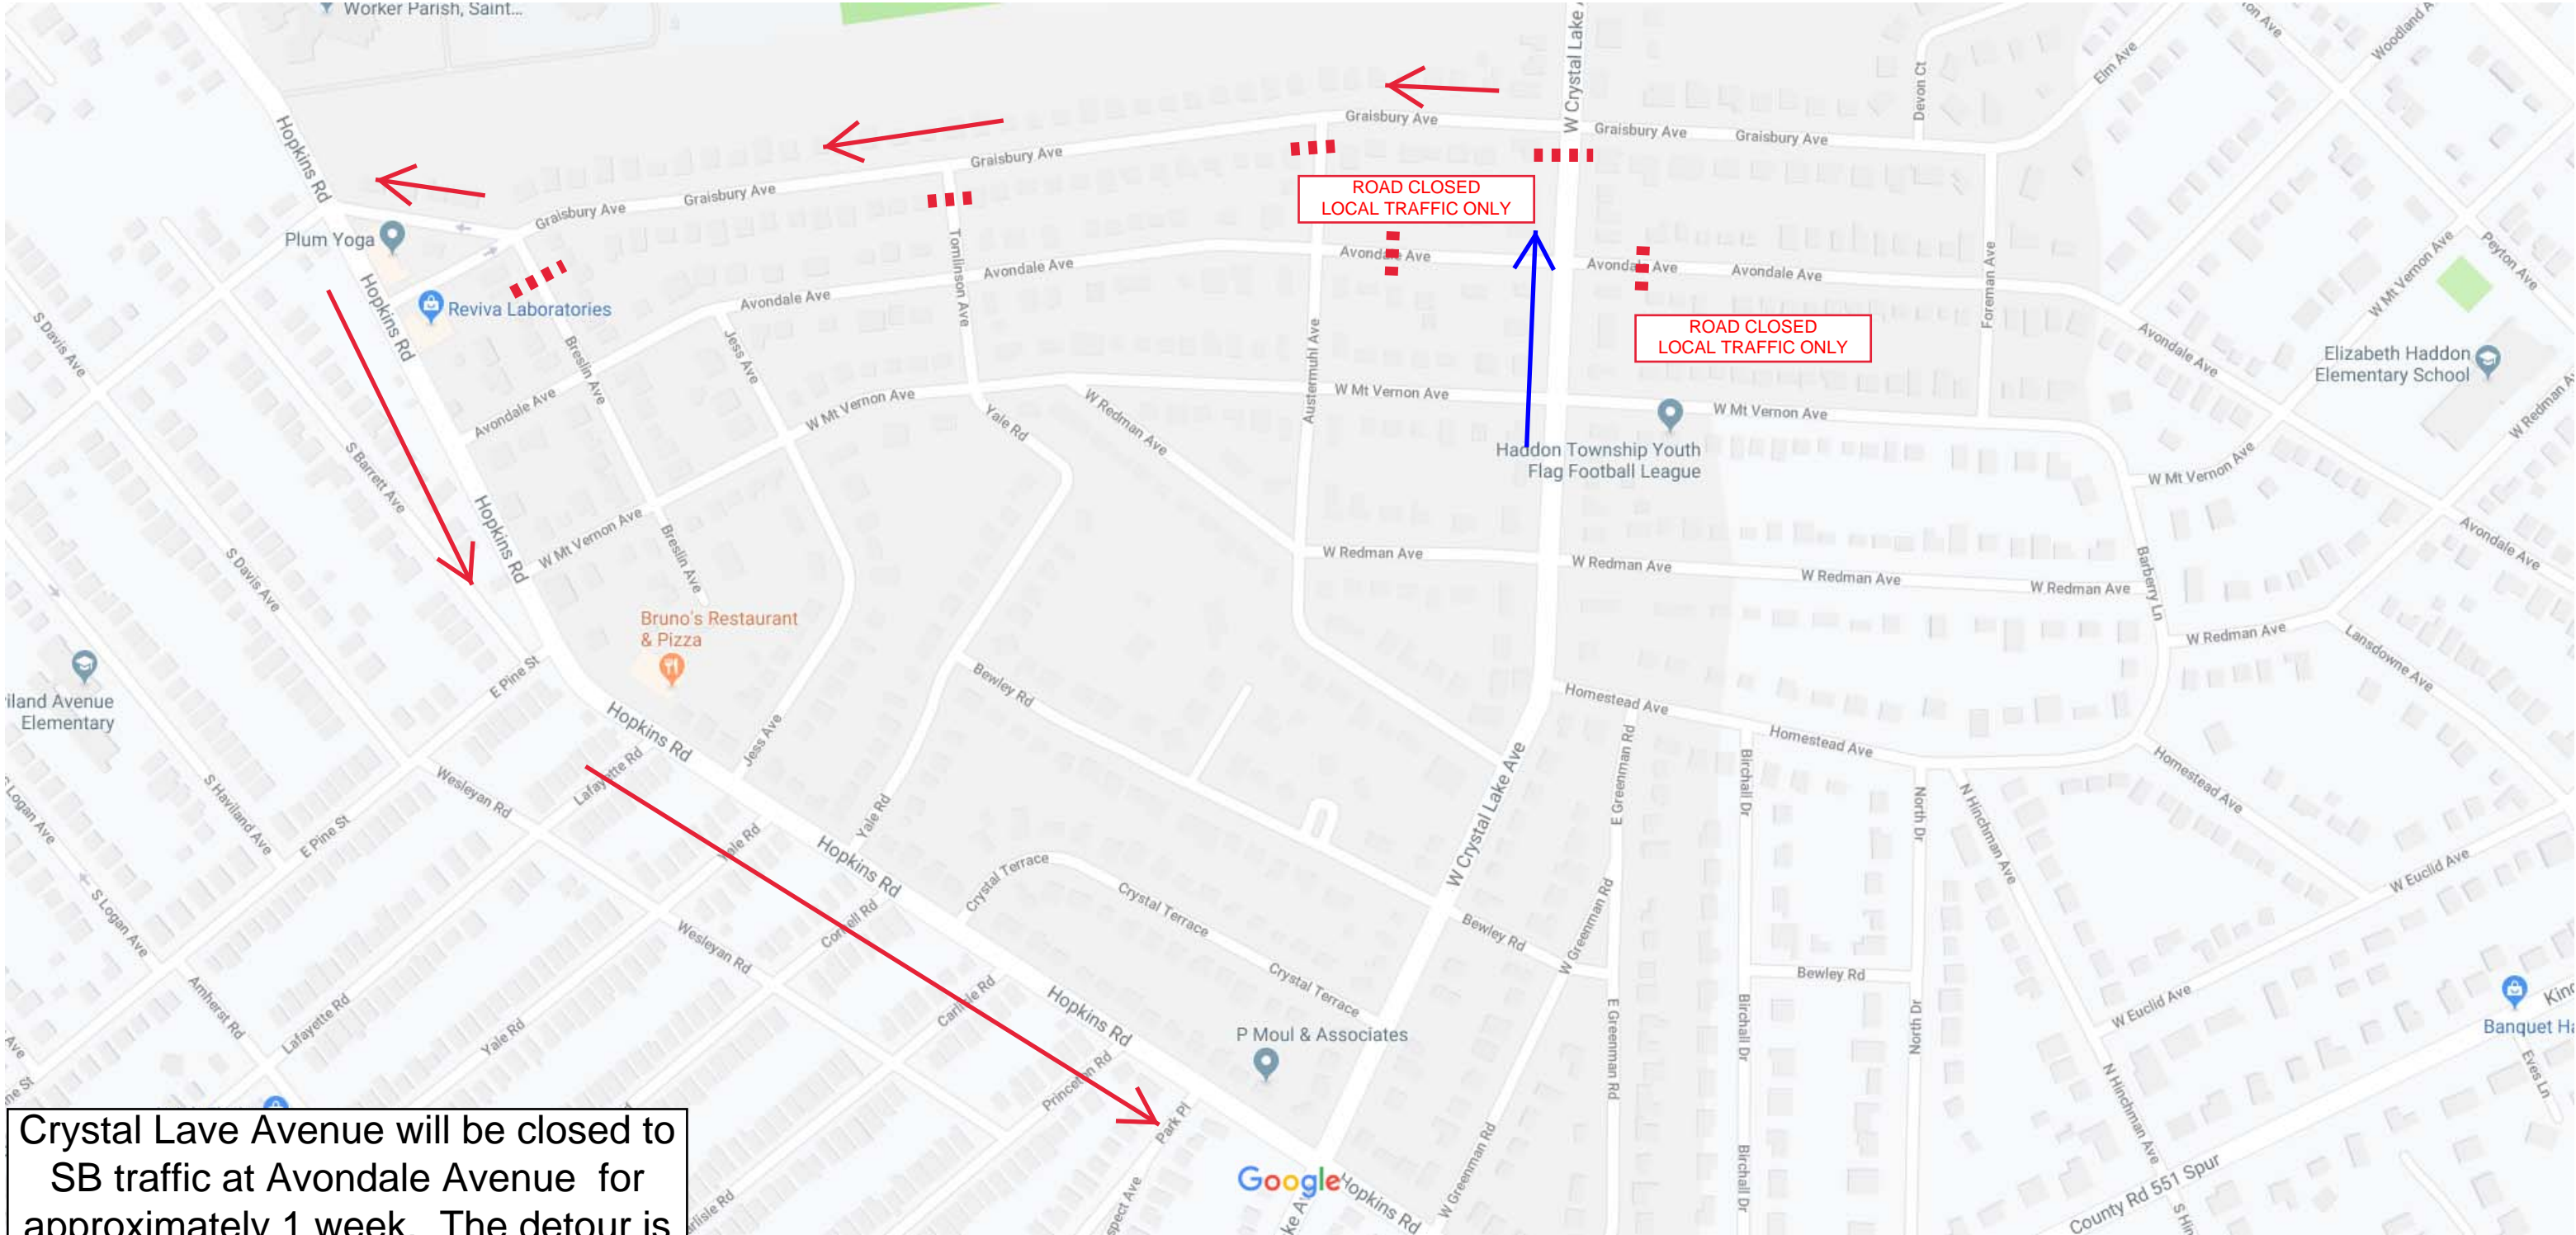

Crystal Lave Avenue will be closed to SB traffic at Avondale Avenue for approximately 1 week. The detour is scheduled for 7/17/19 through 7/26/19.

Crystal Lake SB Detour

Crystal Lake NB to remain open
