



**Improvements to Avondale Avenue (CR646) from Hopkins Road to Woodland Ave.
and Improvements to Breslin Avenue from Graisbury Avenue to Avondale Avenue**

*Township of Haddon
Camden County
Bid No. B2-19*

MC Project No. 19000074G

Progress Report # 9

Monday, July 15, 2019 to Friday, July 19, 2019



Figure 1: New concrete roadway on Avondale Avenue at Crystal Lake.



Figure 2: Existing SB roadway on Crystal Lake Avenue at Avondale.



Figure 3: New SB roadway on Crystal Lake Avenue at Avondale.



Work Completed this week:

Charles Marandino Concrete completed the installation of monolithic curb, gutter and sidewalk on Avondale Avenue from Woodland Avenue to Crystal Lake Avenue, including driveways and handicap ramps. The area behind the new curb was restored with topsoil. The contractor also removed and replaced a portion of the existing concrete roadway at the intersection of Avondale and Crystal Lake Avenues. SB traffic on Crystal Lake Avenue was detoured from Wednesday until Friday afternoon. Access to homeowners was maintained.

Items completed this week:

#2:	Police Traffic Directors	112 HOURS
#6:	Remove Concrete Roadway	262 SY
#9:	Concrete Roadway, 9" Thick	262 SY
#22:	Concrete Sidewalk, 4" Thick	89 SY
#23:	Concrete Driveway, 6" Thick	92 SY
#25:	Detectable Warning Surface	8 SY
#27:	Monolithic Concrete Curb and Gutter	1191 LF

• PROGRESS NEXT TWO (2) WEEKS


- Charles Marandino Concrete will continue to reconstruct the intersection of Crystal Lake and Avondale Avenues.
- Crystal Lake Avenue will remain open to NB traffic; SB traffic will be detoured to Graisbury and Hopkins. The detour will be in place from Tuesday through Friday. A copy of the detour is attached.
- The contractor will install the interlocking retaining walls at specified locations.
- All areas behind the curb will be backfilled and topsoiled.
- The contractor plans to mill and pave Avondale Avenue the week of August 5, 2019.
- The contractor will continue to work 7:00 AM to 4:30 PM.
- The contractor may also work on selected Saturdays.

• NEXT MEETING

- Next Progress Meeting is scheduled for Tuesday, August 6, 2019 at 10:00 AM.

<u>Notice to Proceed Date:</u>	May 13, 2019
<u>Contract Completion Date:</u>	August 11, 2019
<u>Anticipated Completion Date:</u>	August 11, 2019

Prepared by: Vincent E. Baglivo
Maser Consulting

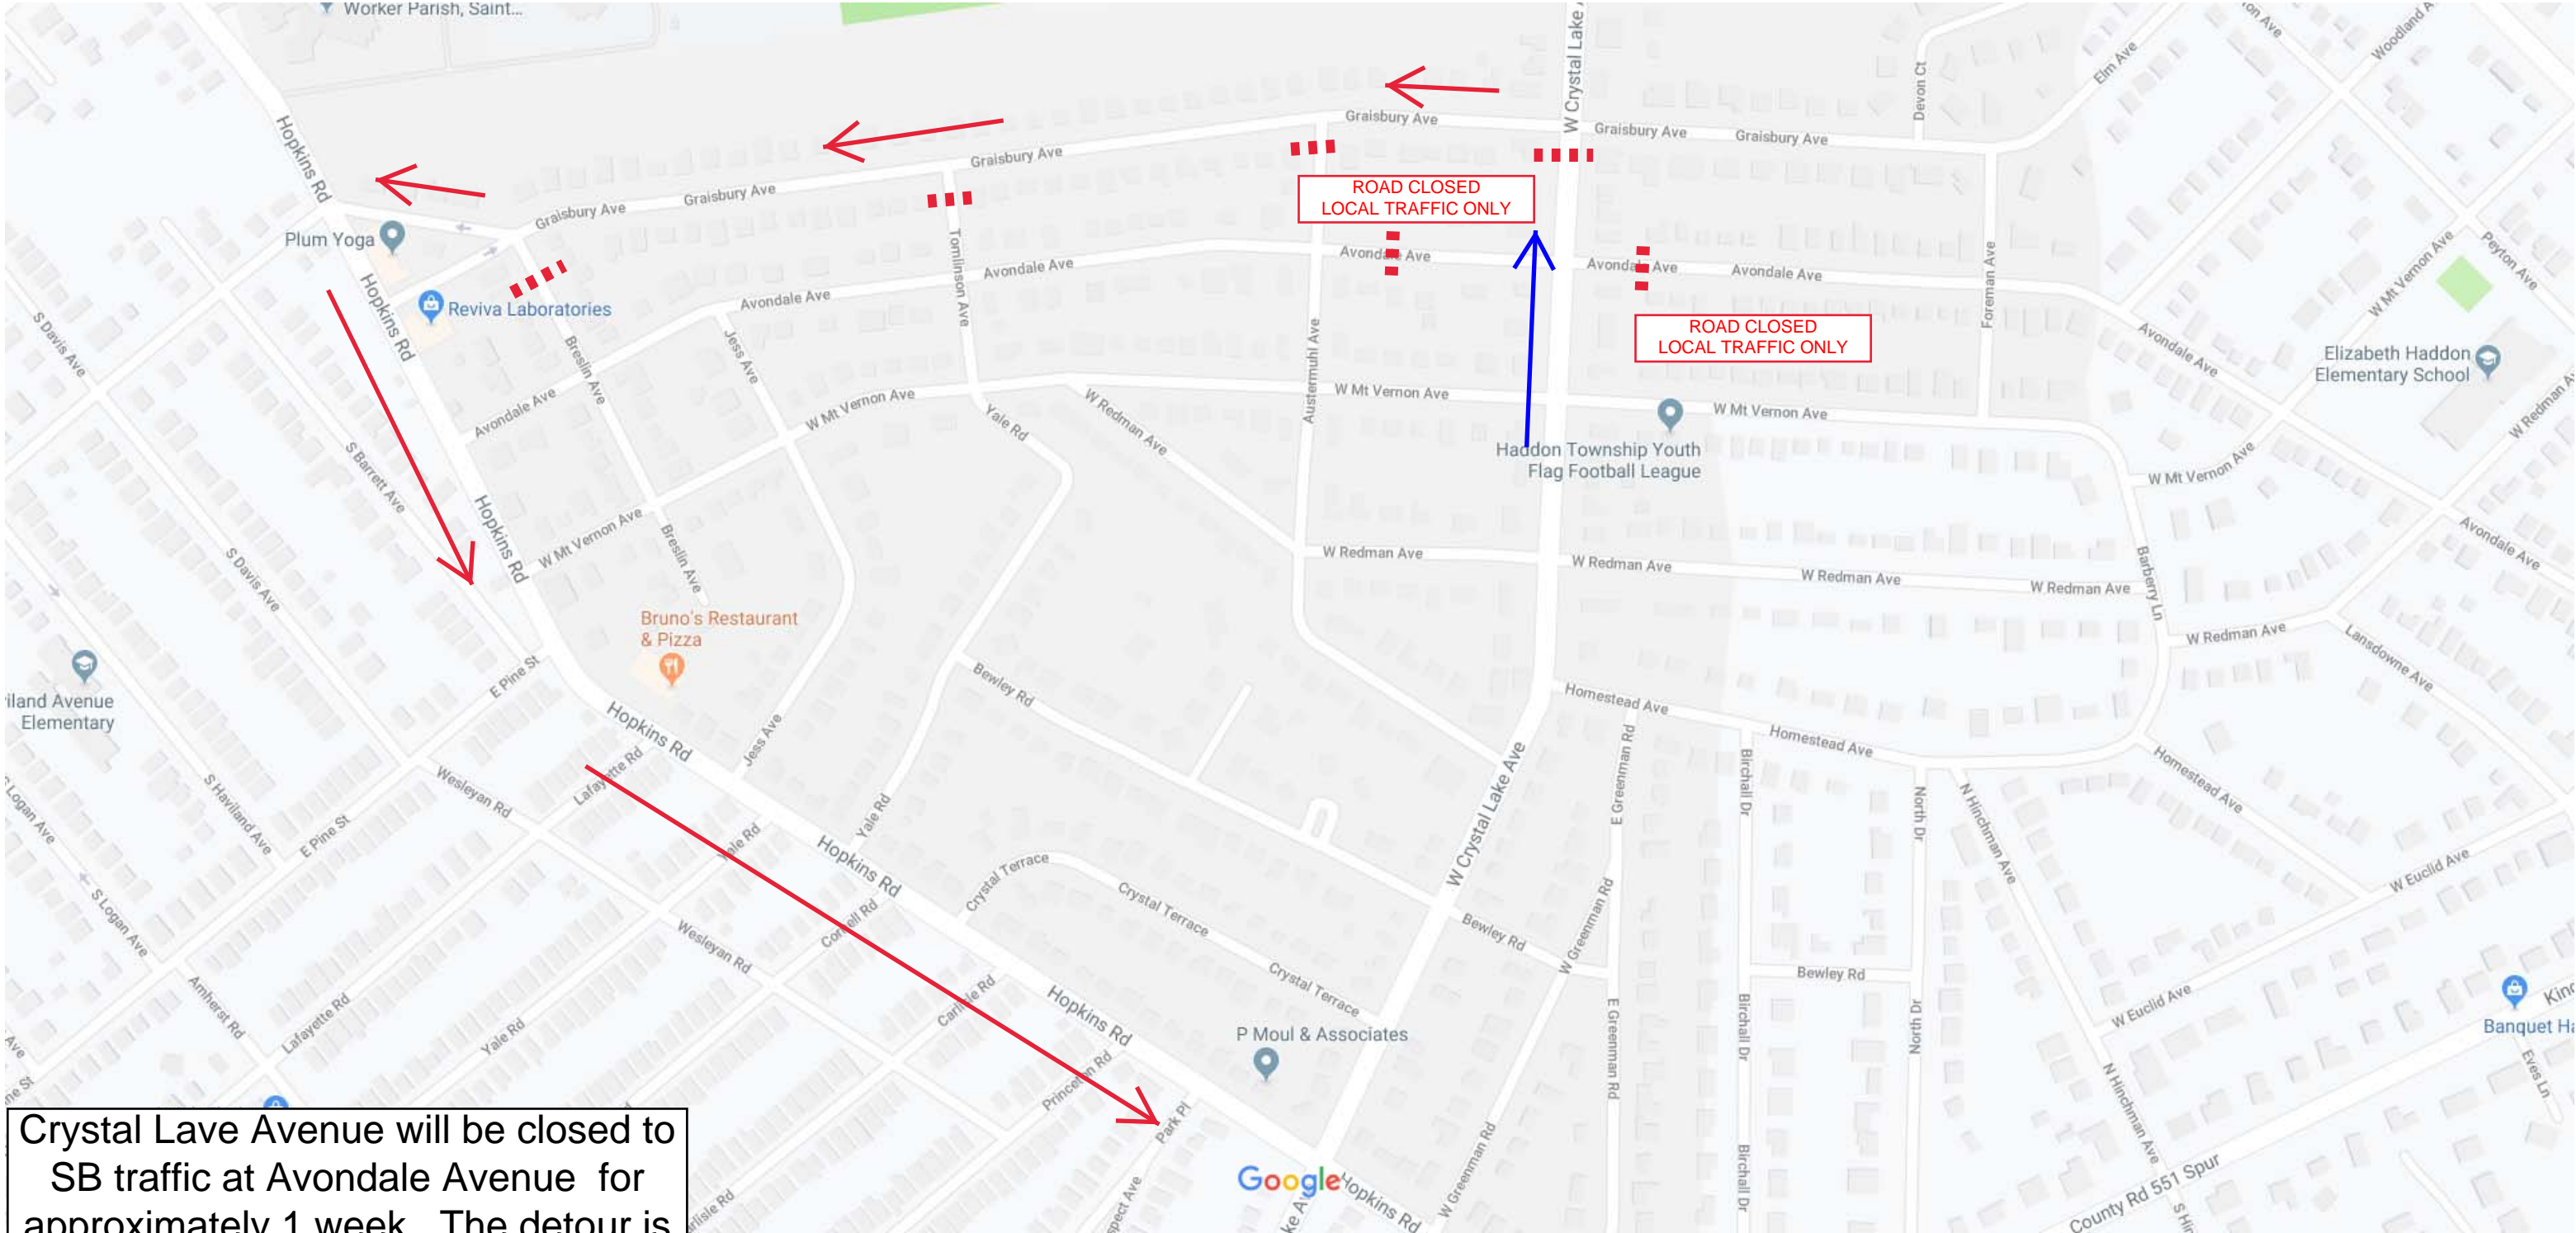

Crystal Lave Avenue will be closed to SB traffic at Avondale Avenue for approximately 1 week. The detour is scheduled for 7/17/19 through 7/26/19.

Crystal Lake SB Detour

Crystal Lake NB to remain open
