

Camden County Department of Public Works
Division of Engineering
Station Avenue & Atlantic Avenue Pedestrian Improvements
Camden County, New Jersey
Weekly Progress Report No. 2
July 15, 2019 to July 21, 2019

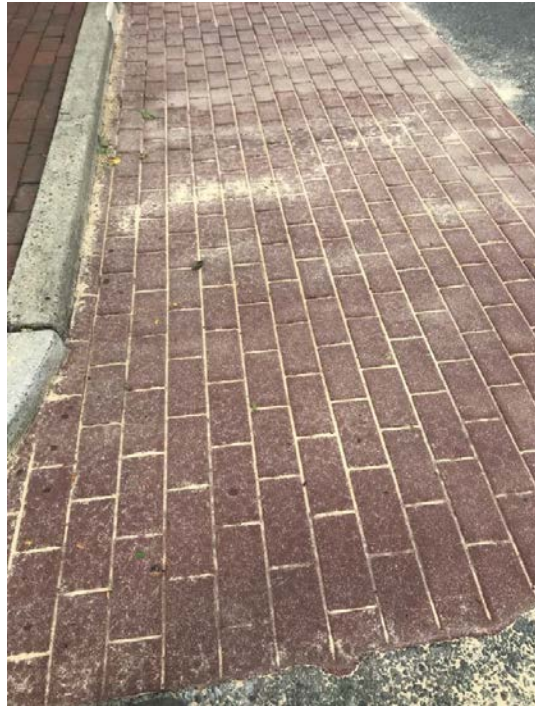


Figure 1: Stamped synthetic pavement completed

Work Completed Week of July 15, 2019

- Installed remaining concrete curb ramp by railroad tracks
- Installed stamped synthetic pavement to the pavement radius around newly installed curb ramps

Quantities Week of July 15, 2019

- **Item #6:** Stamped Synthetic Pavement (1,266.5 SF)
- **Item #8:** 9" x 18" Concrete Vertical Curb (10 LF)
- **Item #9:** Concrete Sidewalk, 4" Thick (5.78 SY)
- **Item #10:** Public Sidewalk Curb Ramp Detectable Warnings, Brick Truncated Domes (16 SF)
- **Item #14:** Police Traffic Directors (48 MH)

Summary of Work Completed Week of July 15, 2019

Charles Marandino LLC, (Marandino) installed the remaining concrete curb ramp by the railroad tracks on the north side of the intersection of Station Avenue and West Atlantic Avenue. The pavement radius around the curb ramps were milled, and stamped synthetic pavement was installed by Marandino's subcontractor. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control. Conrail representative onsite due to work being conducted by the railroad tracks.

Anticipated Work for Week of July 21, 2019

Marandino will allow time for the stamped synthetic pavement to cure, and then remove the traffic control around the concrete curb ramps and stripe the roadway.



Figure 2: Concrete curb ramp formed

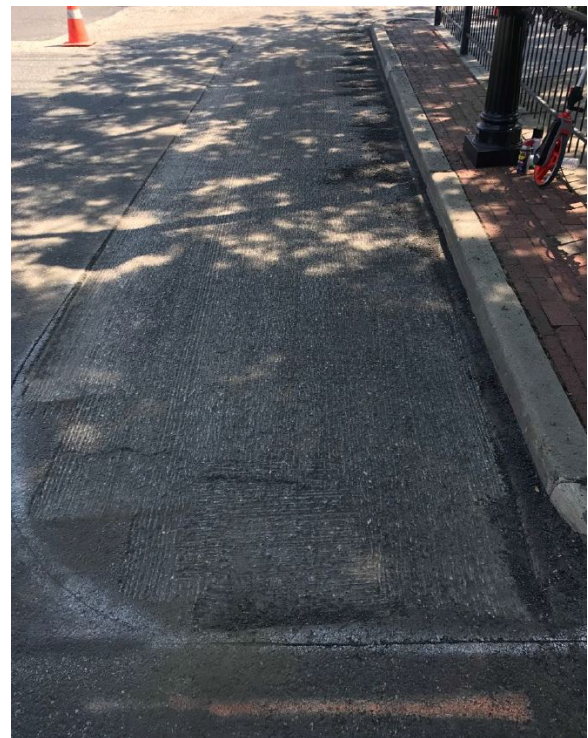


Figure 3: Radius around curb ramp milled



Figure 4: Stamped synthetic pavement installation



Figure 5: Stamped synthetic pavement installation

Prepared By:

Joseph R. Ragusa, P.E.
Remington and Vernick Engineers
