



**Improvements to Avondale Avenue (CR646) from Hopkins Road to Woodland Ave.
and Improvements to Breslin Avenue from Graisbury Avenue to Avondale Avenue**

*Township of Haddon
Camden County
Bid No. B2-19*

MC Project No. 19000074G

Progress Report # 21

Monday, October 7, 2019 to Friday, October 11, 2019

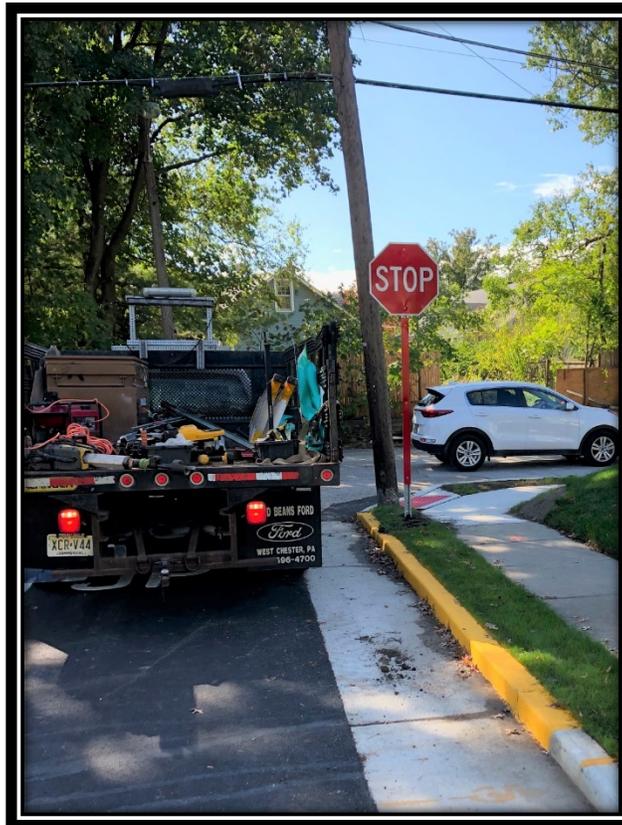


Figure 1: Contractor on-site installing new signs on Avandale Avenue.



Figure 2: Contractor installed new speed limit signs with reflective posts on Avondale Avenue.



Figure 3: Contractor installed new stop signs with reflective posts on project.



Work Completed this week:

The contractor completed the installation of new traffic signs on the project. Installed pavement reflectors at the hydrants and removed detour signs. Pavement cores taken to verify pavement quality.

Items completed this week:

#31: RPM, Bi-Directional, Blue Lens	7 UN
#32: Regulatory and Warning Signs	29 UN

• **PROGRESS NEXT TWO (2) WEEKS**

- The contractor plans to complete gabion installation and headwall repair near Woodland Avenue.
- He will begin installation of trees throughout the project.
- He plans to complete all punchlist work on the project.
- The contractor will continue to work 7:00 AM to 4:30 PM.

• **NEXT MEETING**

- Next Progress Meeting is scheduled for Tuesday, October 15, 2019 at 10:00 AM.

<u>Notice to Proceed Date:</u>	May 13, 2019
<u>Contract Completion Date:</u>	August 11, 2019
<u>Anticipated Completion Date:</u>	October 15, 2019

Prepared by: Vincent E. Baglivo
Maser Consulting
