

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 3
November 3, 2019 to November 9, 2019**

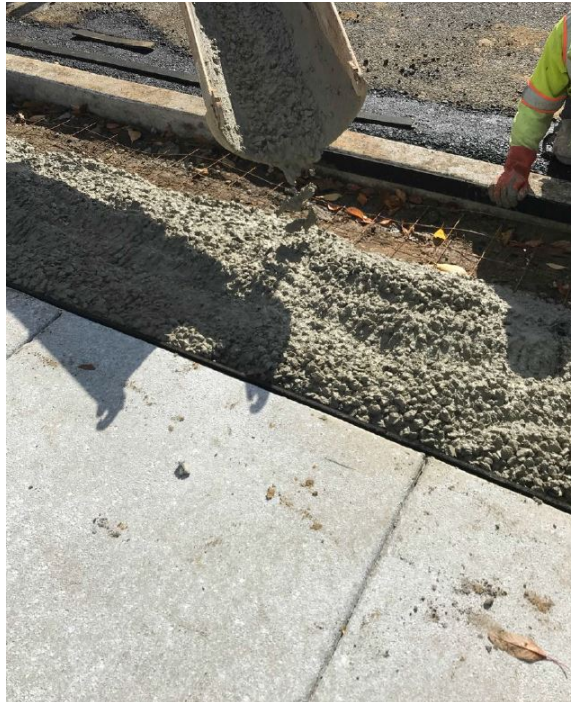


Figure 1: Concrete driveway placement

Work Completed Week of November 9, 2019

- Installation of concrete sidewalk, curb, reinforced driveways, and curb ramps along Chapel Avenue
- Roadway restoration where new concrete vertical curb was constructed

Quantities Week of November 9, 2019

- **Item #17:** Dense Graded Aggregate Base Course, 8" Thick (31.55 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (11.79 TON)
- **Item #31:** Concrete Driveway, Reinforced, 6" Thick (107.67 SY)
- **Item #34:** 9"x18" Concrete Vertical Curb (271 LF)
- **Item #70:** Police Uniform Law Enforcement Officers (24 HR)
- **Item #1C:** Concrete Sidewalk, 4" Thick (53.34 SY)

Summary of Work Completed Week of November 9, 2019

Lexa Concrete (Lexa) continued with demolition of existing concrete and replacement with new concrete sidewalk, curb, reinforced driveways, and curb ramps. Lexa conducted roadway restoration by the locations where new concrete curb was placed. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control.

Anticipated Work for Week of November 16, 2019

Lexa will continue with the removal and replacement of concrete curb, sidewalk, driveways, and curb ramps as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project. An onsite progress meeting will be held on November 12, 2019 to review all project related activities.



Figure 2: Concrete driveway



Figure 3: Concrete sidewalk



Figure 4: Concrete sidewalk placed



Figure 5: Excavation operations

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read "JR" or "Ragusa".

Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
