

**Camden County Department of Public Works
Division of Engineering
Roadway Improvements to Hopkins Avenue (CR 647) from
Crystal Lake Avenue (CR 643) to Cuthbert Boulevard (CR 636)
Camden County, New Jersey
Weekly Progress Report No. 17
November 24, 2019 to November 30, 2019**

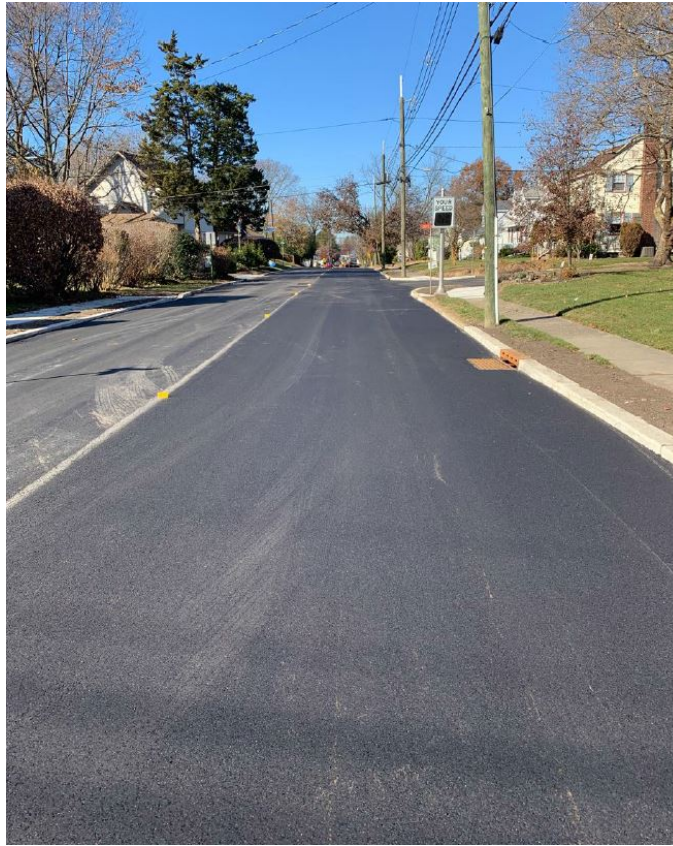


Figure 1: Hopkins Avenue paved

Work Completed Week of November 30, 2019

- Milling and paving operations on Hopkins Ave
- Concrete block wall construction

Quantities Week of November 30, 2019

- **Item #2:** Police Uniform Law Enforcement Officer (119 MH)
- **Item #7:** HMA Milling, 0" to 2" (597.66 SY)
- **Item #11:** HMA, 9.5M64, Surface Course, 2" Thick (1682.3 TON)
- **Item #54:** Polymerized Joint Adhesive (1550 LF)

Summary of Work Completed Week of November 30, 2019

Charles Marandino's (Marandino) subcontractor South State milled and paved Hopkins Avenue. Marandino constructed concrete block walls during the week. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control.

Anticipated Work for Week of December 7, 2019

Marandino will conduct roadway striping and sign installation along Hopkins Avenue as well as punchlist work. Daily traffic control will continue to be implemented for the duration of the project.



Figure 2: Milled roadway cleaned and tack applied



Figure 3: Paved driveway



Figure 4: Paving operations

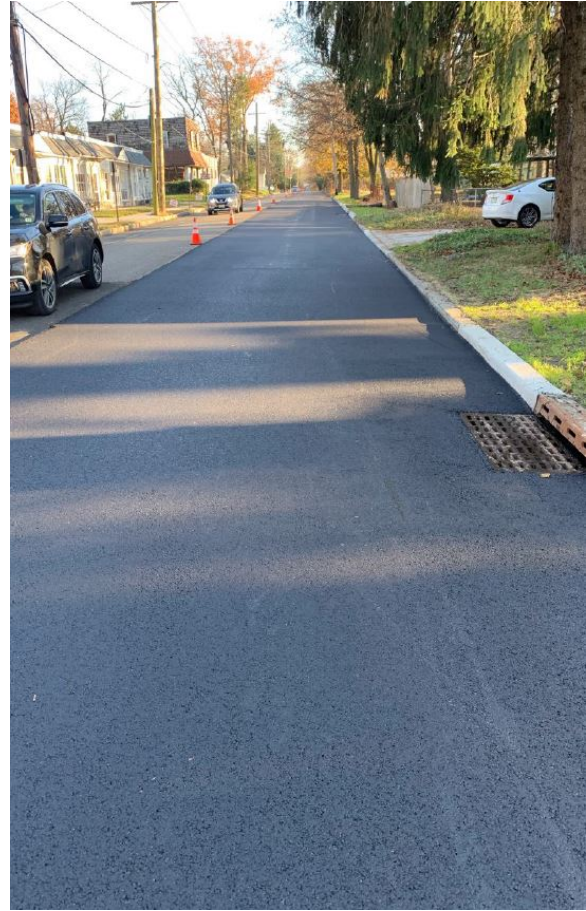


Figure 5: Paved roadway

Notice to Proceed

July 30, 2019

Contract Completion

Substantial Completion

November 12, 2019

Final Completion

November 27, 2019

Prepared By:

Joseph R. Ragusa, P.E.
Remington and Vernick Engineers
