

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 8
December 8, 2019 to December 14, 2019**



Figure 1: Driveway excavated

Work Completed Week of December 14, 2019

- Installation of concrete sidewalk, curb, reinforced driveways, and curb ramps along Chapel Avenue
- Asphalt roadway and topsoil restoration

Quantities Week of December 14, 2019

- **Item #17** Dense-Graded Aggregate Base Course, 8" Thick (46.23 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (29.19 TON)
- **Item #30:** Concrete Sidewalk, 4" Thick (18.55 SY)
- **Item #31:** Concrete Driveway, Reinforced, 6" Thick (109.11 SY)
- **Item #32:** Detectable Warning Surface (2.22 SY)
- **Item #33:** Hot Mix Asphalt Driveway, 6" Thick (19.44 SY)

- **Item #34:** 9”x18” Concrete Vertical Curb (180 LF)
- **Item #66:** Topsoiling, 4” Thick (166.83 SY)
- **Item #68:** Fertilizing and Seeding, Type F (166.83 SY)
- **Item #70:** Police Uniform Law Enforcement Officers (29 HR)

Summary of Work Completed Week of December 14, 2019

Lexa Concrete (Lexa) continued with demolition of existing concrete and replacement with new concrete sidewalk, curb, reinforced driveways, and curb ramps. Lexa also constructed asphalt roadway restoration and topsoil restoration operations. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Police Uniform Law Enforcement Officers are additionally utilized for traffic control. An onsite progress meeting was held on December 12, 2019 to review all project related activities.

Anticipated Work for Week of December 21, 2019

Lexa will continue with the removal and replacement of concrete curb, sidewalk, driveways, and curb ramps as specified in the plans along Chapel Avenue until the winter shutdown. Daily traffic control will continue to be implemented for the duration of the project.

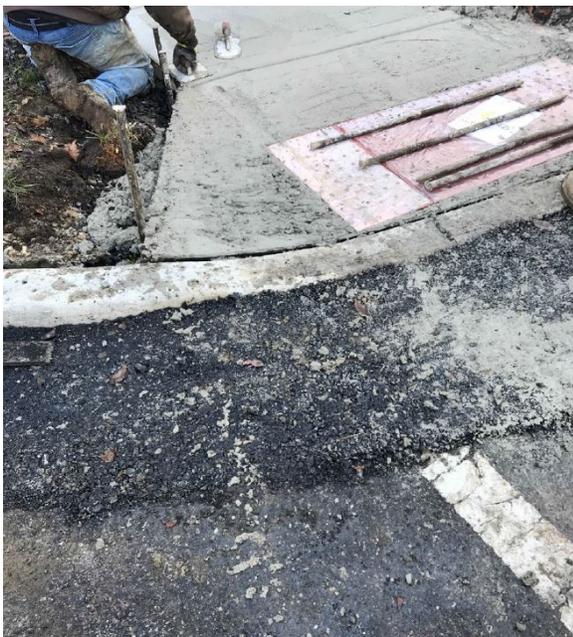


Figure 2: Concrete curb ramp placed



Figure 3: Concrete sidewalk placed



Figure 4: Sidewalk excavated



Figure 5: Topsoiling operations

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

Joseph R. Ragusa, P.E.

Remington and Vernick Engineers
