

Camden County Department of Public Works

Division of Engineering

Roadway Improvements

Along Pennington Ave & Chew Rd (CR 536)

White Horse Pike (RT 30) to Pestletown Rd.

Winslow & Waterford Townships, Camden County, New Jersey

Weekly Progress Report #7

Aug. 03, 2020 to Aug. 07, 2020



Figure 1

Concrete gutter installed Pennington Ave. left Station 18+00 to 18+30.

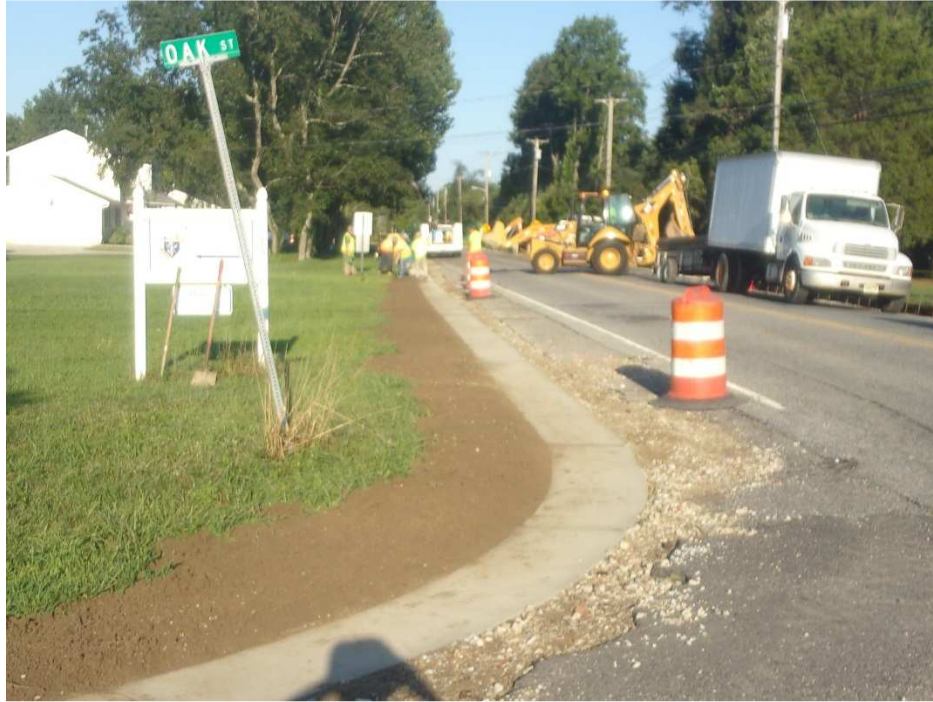


Figure 2
Top soiling and Turf repair strip installed Pennington Ave.



Figure 3
Milling to subgrade along Chew Road.



Figure 4
Milling to subgrade at Pestletown and Chew Rd



Figure 5
Concrete Gutter and Monolithic Curb and gutter installed Sta. 18+30 to 21+13 left Pennington Ave.

Work Completed week of August 03, 2020:

August 03 thru 07 traffic control signage was in place and used to detour traffic around Pennington Ave. and uniformed police were used on Chew Road.

Aug. 03 Concrete gutter was installed along Pennington Ave left from Sta. 16+95 to 18+00 and Full Depth Reclamation (FDR) was performed from Sta. 56+50 to 28+70 Chew Road right

Aug. 04 Contractor did not work due to weather.

Aug. 05 Concrete gutter was installed from Sta 18+00 to 18+30 Left Pennington Ave. Pourer curb for Item S7 from Sta. 19+98 to Oak St. left Pennington Ave. and Top Soiled and Turf Repair Strip Along Both sides of Pennington Ave behind completed curb and gutter.

Aug. 06 Concrete crew did not work this day due to weather. Milling crew milled and tacked Pestletown and Chew road intersection.

Aug. 07 Concrete crew installed Gutter and Mono lithic curb and gutter Sta. 18+30 to 21+13 along the left side of Pennington Ave. and the milling crew milled both east and West bound Chew Rd. from sta. 57+00 to 78.75.

Quantities of work the week of August 03, 2020:

- Item #4: Full Depth Reclamation, Concrete (3,827 SY)
- Item #25: Police Uniform Law Enforcement Officer (78 MH)
- Item #32: Topsoiling 4" Thick (244 SY)
- Item #33: Turf Repair Strip 1,100 LF)
- Item #40: HMA Milling More Than 3" To 6" (12,451 SY)
- Item #42: Excavation, Test Pit (0 CY)
- Item #43: Concrete Gutter (192 LF)
- Item #S7: Monolithic Concrete Curb and Gutter (226 LF)

Anticipated work for Week of August 10, 2020:

Continue with concrete flat work along of Pennington Ave., Milling of the Chew Road portion of the project and HMA Base paving.

Contract Completion Milestones

Notice to Proceed Date:	Monday, June 8, 2020
Substantial Completion Date:	Saturday, September 26, 2020
Final Completion Date:	Friday, October 16, 2020

Percent Complete by Duration: 28.66%

Percent Complete by Payments: 0%

Prepared By:
CES



David Firman
Lead Inspector
