

**Camden County Department of Public Works
Division of Engineering
Improvements to Chapel Avenue (CR 626) from
Haddonfield Road (CR 644) to New Jersey Route 41 (Kings Highway)
Township of Cherry Hill, Camden County, New Jersey
Weekly Progress Report No. 28
June 28, 2020 to July 4, 2020**



Figure 1: Concrete center island

Work Completed Week of July 4, 2020

- Lexa Concrete sawcut and demolished roadway for concrete islands construction
- Concrete edge restraint and subbase placed for concrete islands
- Installed cobblestone pavers within concrete islands

Quantities Week of July 4, 2020

- **Item #16:** Removal of Pavement (45.89 SY)
- **Item #21:** Hot Mix Asphalt 19M64 Base Course (23.11 TON)
- **Item #70:** Police Uniform Law Enforcement Officers (96 HR)
- **Item #71:** 6"x12" Concrete Edge Restraint (119.75 LF)
- **Item #72:** Cobblestone Paving (431.99 SY)

Summary of Work Completed Week of July 4, 2020

Lexa Concrete (Lexa) continued work on concrete islands along Chapel Avenue. Lexa sawcut and demolished sections of the existing roadway in preparation for concrete island construction. Concrete edge restraint and concrete subbase was placed for the installation of cobblestone pavers within the islands. Maintenance and Protection of Traffic (MPT) is set up before each work day and taken down at the end of each work shift. Flaggers are being utilized and continuously coordinated with the Cherry Hill Township Police Department. Uniformed Law Enforcement Officers are additionally utilized for traffic control. The project will continue as planned despite the current pandemic. The project is approximately 65% complete.

Anticipated Work for Week of July 11, 2020

Lexa will continue with the removal of existing roadway and installation of concrete islands as specified in the plans along Chapel Avenue. Daily traffic control will continue to be implemented for the duration of the project. An onsite progress meeting will be held on July 7, 2020 to review all project related activities.

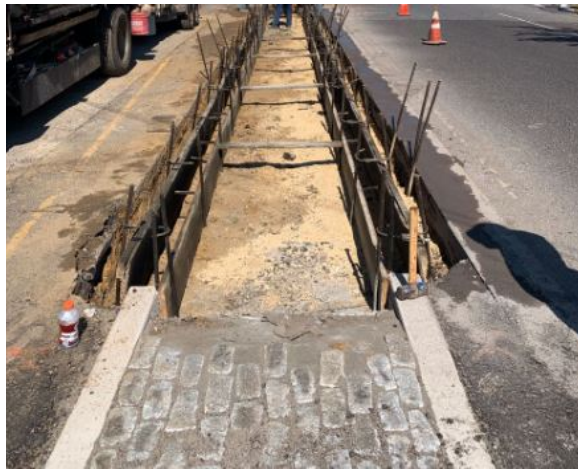


Figure 2: Concrete restraint curb forms



Figure 3: Concrete island curb placed



*Figure 4: Concrete center island
cobblestone construction*



*Figure 5: Concrete center island
construction*

Notice to Proceed

October 14, 2019

Contract Completion

Substantial Completion

September 13, 2020

Final Completion

October 13, 2020

Prepared By:

A handwritten signature in blue ink, appearing to read "J. Ragusa".

Joseph R. Ragusa, P.E.
Remington & Vernick Engineers
