

Camden County Department of Public Works

Division of Engineering

Roadway and Drainage Improvements

Along Peter Cheeseman Road (CR 759)

Hickstown Road (CR 688) to Erial Road (CR 706)

Gloucester Township, Camden County, New Jersey

Weekly Progress Report # 2

June 22, 2020 to June 26, 2020



Figure 1

Drainage pipe trench is being compacted in lifts using a vibratory plate compactor on excavator



Figure 2
Geese in the area crossing the road near College Drive



Figure 3
VMS was moved to a safer location around Sta. 67+00 Lt.

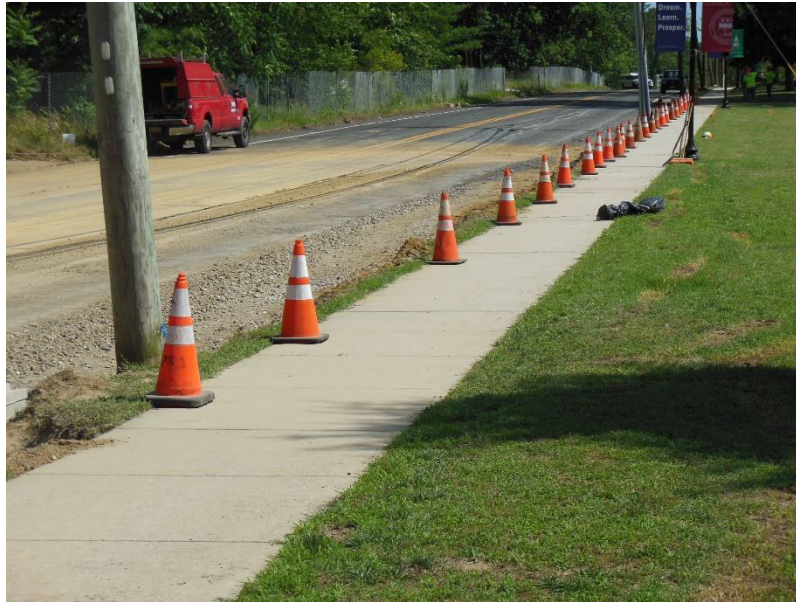


Figure 4
Storm pipe was removed to a storage location not on College property



Figure 5
Installation of Type B inlet at Sta. 35+45.16 Rt.

Work Completed Week of June 22, 2020:

- Installed 18" RCP
- Relocated VMA for safety reasons
- Relocated 18" RCP in front of college to stored area
- Electrical work started
- Cross drain installed at Sta. 36+50

Quantities Week of June 22, 2020:

- Item #3: Uniformed Police (82 MH)
- Item#22: 18"RCP (750 LF)
- Item #25: Inlet Type B (1 UN)

Summary of Work Completed Week of June 15, 2020:

Contractor continues the installation of 18" RCP. At the request of Camden County officials stored material in ROW was relocated to a storage area. Also, the VMS at Hickstown road and Peter Cheeseman was relocated to the NB side of the roadway to Sta. 67+00. It was much safer at this location. Clay Electric was on site Friday to start electrical work.

Anticipated work for Week of June 22, 2020:

Installation of drainage will continue this week. The contractor will also start sidewalk and ADA ramp at College Dr.

Notice to Proceed Date: Monday, June 15, 2020

Contract Completion Milestones

Substantial Completion Date: Sunday , September 13, 2020

Final Completion Date: Tuesday, October 13, 2020

Accelerated Completion Date: **Saturday, August 15, 2020**

Percent Complete by Duration: **23%**

Percent Complete by Payments: **10%**

Prepared By:

AECOM



Anthony Guerrieri
Project Manager
