

Camden County Department of Public Works

Division of Engineering


Roadway and Drainage Improvements

Along Peter Cheeseman Road (CR 759)

Hickstown Road (CR 688) to Erial Road (CR 706)

Gloucester Township, Camden County, New Jersey

*Weekly Progress Report # 4
July 6, 2020 to July 10, 2020*

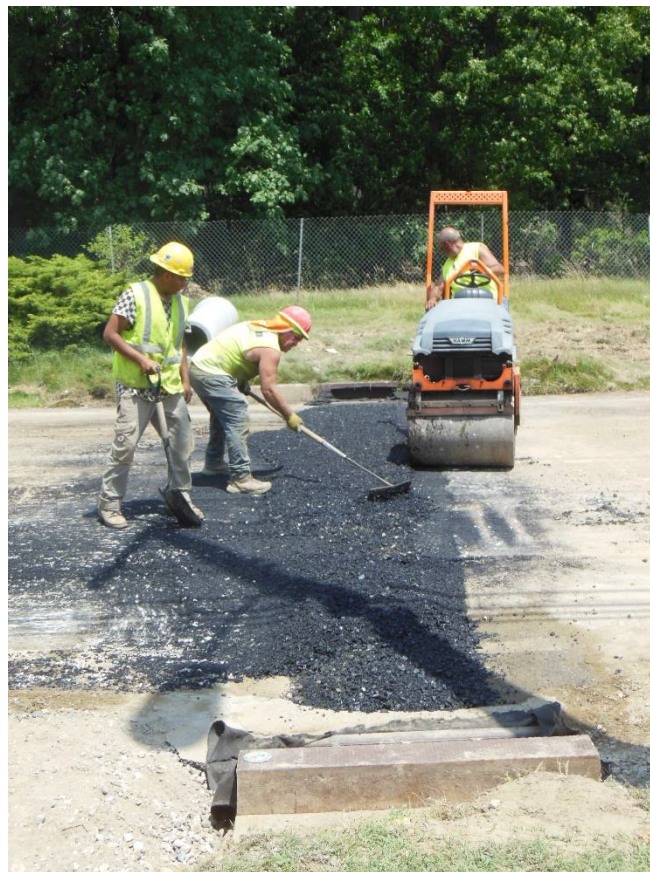

*Figure 1
Cross Drain that was installed at Sta.36+50*




*Figure 2
Image Detector installed at the intersection of Hickstown and Peter Cheeseman*



*Figure 3
Compaction of material under the curb to be poured*



*Figure 4
Pouring curb in forms set the grade and offset*

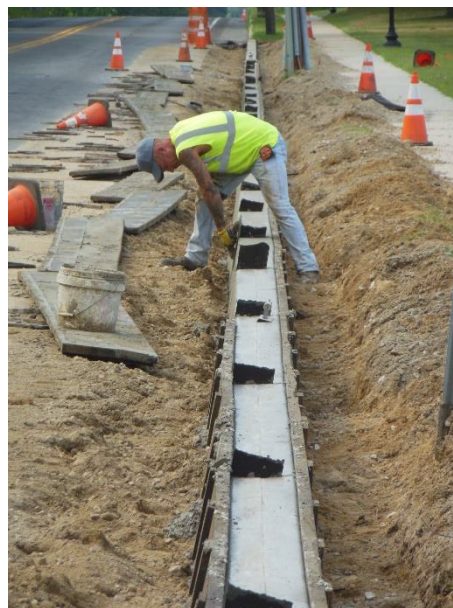

*Figure 5
Contractor's removing forms from curb after concrete set up enough to finish face*



*Figure 6
Sign showing Camden County Public Works*

Work Completed Week of July 6, 2020:

- Completed all drainage items
- Continued curb and sidewalk
- Layout of profile centerline has continued
- I

Quantities Week of July 6, 2020:

- Item #3: Uniformed Police (57 MH)
- Item 12: DGA (11.1 SY)
- Item #37: Concrete Sidewalk (11.1 SY)
- Item # 42: Concrete Curb (1339.5 LF)

Summary of Work Completed Week of July 6, 2020:

Contractor is working on curb and sidewalk item throughout the project. They hope to be completed sometime next week

Anticipated work for Week of July 13, 2020:

As Curb and sidewalk work is being completed the contractor plans on stating the milling operation Wednesday July 15. Once Milling is completed the will begin the paving operations. Layout of profile line and electrical items work will continue.

Notice to Proceed Date: Monday, June 15, 2020

Contract Completion Milestones

Substantial Completion Date: Sunday , September 13, 2020

Final Completion Date: Tuesday, October 13, 2020


Accelerated Completion Date: **Saturday, August 15, 2020**

Percent Complete by Duration: **39% (are calculated to Accelerated Date)**

Percent Complete by Payments: **19%**

Prepared By:

AECOM



Anthony Guerrieri
Project Manager
