

Camden County Department of Public Works

Division of Engineering


Roadway and Drainage Improvements

Along Peter Cheeseman Road (CR 759)

Hickstown Road (CR 688) to Erial Road (CR 706)

Gloucester Township, Camden County, New Jersey

*Weekly Progress Report # 7
July 27, 2020 to July 31, 2020*

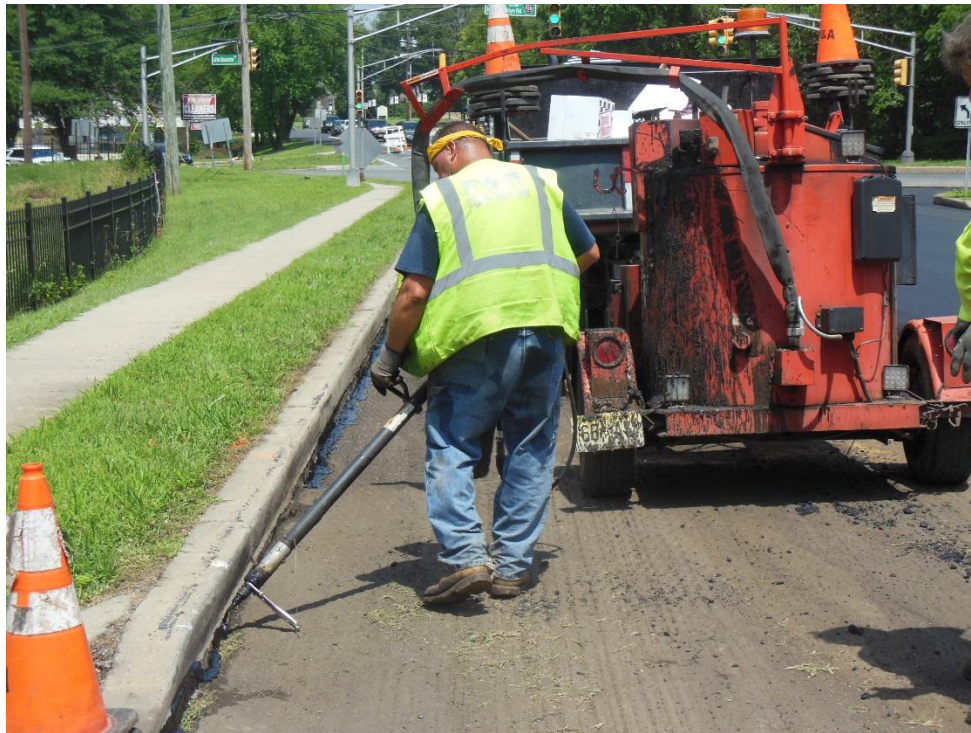

*Figure 1
Installing tack along edge of curb*



*Figure 2
Paver being loaded by the MTV*



*Figure 3
Paving train with roller in the background*



Figure 4
Straw mulch completed after seed was placed



Figure 5
Paved roadway with temporary marked in center



Figure 6
Verizon made it in to perform the pole transfer

Work Completed Week of July 27, 2020:

- Contractor completed seeding and installing straw mulch
- Paving was completed

Quantities Week of July 27, 2020:

- Item #3: Uniformed Police (53 MH)
- Item #15: Polymerized Joint Adhesive (19,824 LF)
- Item #16: Tack Coat (984.4 Gal)
- Item #17: Hot Mixed Asphalt Surface Course (3476.64 T)
- Item #38: Hot Mixed Asphalt Driveway, 6" thick (6 SY)

Summary of Work Completed Week of July 27, 2020:

Contractor completed the paving operations.

Anticipated work for Week of August 3, 2020:

Pavement markings will be installed. Signage will be placed as shown on plans. The electrical items will be completed

Notice to Proceed Date: Monday, June 15, 2020


Contract Completion Milestones

Substantial Completion Date: Sunday , September 13, 2020

Final Completion Date:	Tuesday, October 13, 2020
Accelerated Completion Date:	Saturday, August 15, 2020
Percent Complete by Duration:	74% (are calculated to Accelerated Date)
Percent Complete by Payments:	67%

Prepared By:

AECOM



Anthony Guerrieri
Project Manager
