

**Camden County Department of Public Works  
Division of Engineering  
Roadway Improvements along Blackwood Clementon Road  
Gloucester Township, Camden County, New Jersey  
Progress Report No. 1  
August 8, 2022 to August 12, 2022**



*Figure 1: Westbound Blackwood Clementon Road work area*

**Work Completed Period of August 12, 2022**


- Cleaned out inlet and existing pipes.
- 18” joint repair to storm drains piping between Emerson Road and Little Gloucester Road.



*Figure 2: Separation in joint of pipe was fixed*



*Figure 3: Pipe encased in concrete*

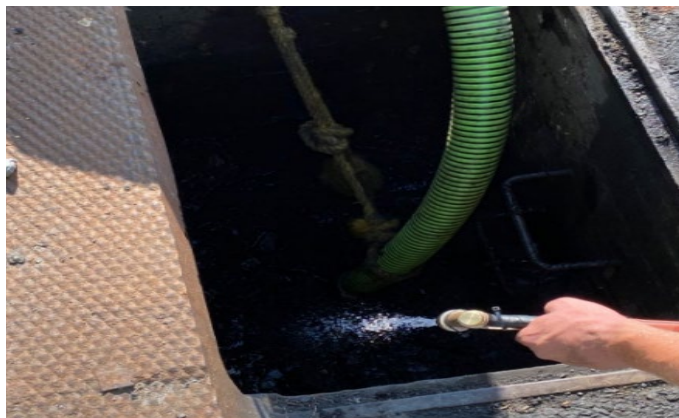

*Figure 4: Vacuuming process*



*Figure 5: View of pipe interior from inlet towards manhole*



*Figure 6: Mortar parged around wire mesh placed around separation*

#### **Quantities Period of August 12, 2022**

- **Item #4:** Drum (135 UNIT)
- **Item #5:** Breakaway Barricade (28 UNIT)
- **Item #6:** Breakaway Barricade with Sign (12 UNIT)
- **Item #7:** Traffic Control Truck with Mounted Crash Cushion (1 UNIT)
- **Item #8:** Traffic Safety Services (40 MH)
- **Item #14:** HMA Base Course, 19M64, 6" Thick (17.36 TON)
- **Item #18:** Joint Repair, 15" Reinforced Concrete Pipe (3 UNIT)
- **Item #19:** Joint Repair, 18" Reinforced Concrete Pipe (3 UNIT)

**Summary of Work Completed Period of August 12, 2022**

The crew completed joint repairs. Areas excavated, pipe cleared off, adhesive and fabric paper applied then encased in concrete. Repairs completed and areas were backfilled and compacted. Crew also completed clean out of the inlet and pipe.

**Anticipated Work for Period of August 15, 2022**


- Continue with pipe replacement which will include excavation, backfilling, and concrete placement.

**Notice to Proceed:** August 1, 2022

**Substantial Completion:** October 30, 2022

**Final Completion:** November 29, 2022

**Prepared By:**



Joseph R. Ragusa, P.E.  
Remington & Vernick Engineers
